



April 18th, 2024












Today's Topics

- Project Update
- Consent Business
- Non-consent Business
- Committee Discussion
- Announcements
- Public Invitation



Project Office Update

West vertical circulation tower construction at West Lake Street Station in Minneapolis

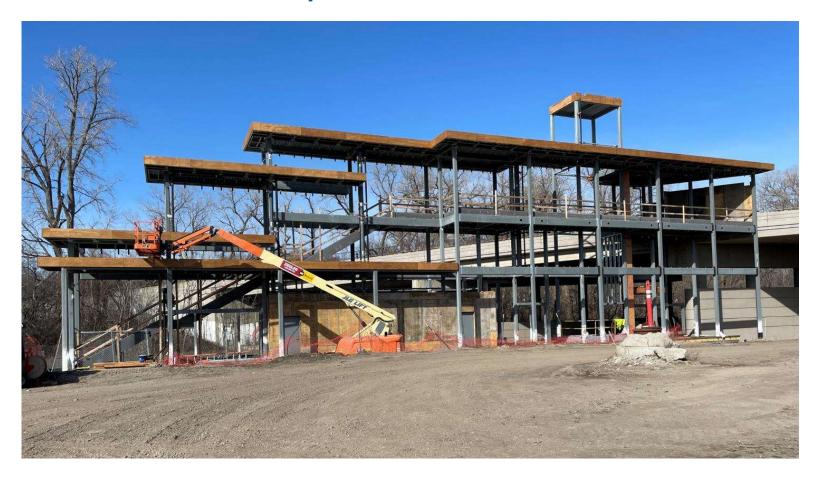



East vertical circulation tower at West Lake Street Station in Minneapolis






East vertical circulation tower at West Lake Street Station and west heading excavation at the Kenilworth LRT Tunnel in Minneapolis






West heading base slab preparation at the Kenilworth LRT Tunnel in Minneapolis



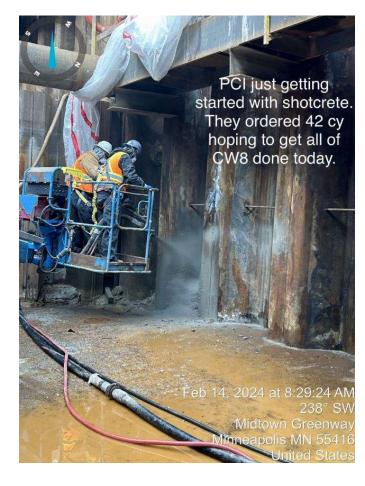



West heading base slab preparation at the Kenilworth LRT Tunnel in Minneapolis

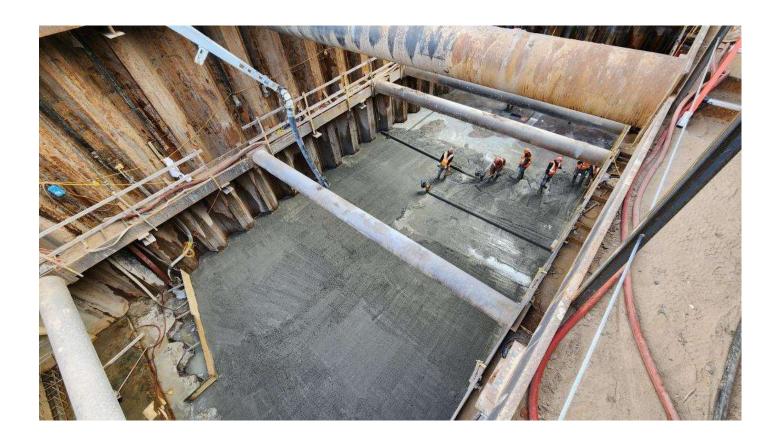




Fire lift station form installation at the Kenilworth LRT Tunnel in Minneapolis





East heading boat section at the Kenilworth LRT Tunnel

in Minneapolis

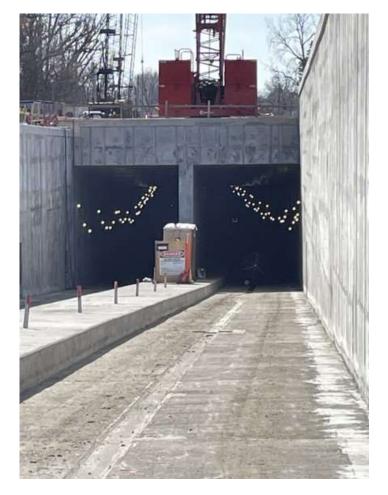



Overhead contact system (OCS) shield installation on the Burnham Road Bridge in Minneapolis





Bryn Mawr Station vertical circulation tower and pedestrian overpass in Minneapolis





Mesh panel installation at the Bryn Mawr Station vertical circulation tower in Minneapolis





Elevator curtain wall at Bryn Mawr Station in Minneapolis.





Pedestrian overpass and vertical circulation tower interior ceiling installation at Bryn Mawr Station in Minneapolis







Vertical circulation tower at Bassett Creek Valley Station in Minneapolis






Royalston Avenue/Farmers Market Station in Minneapolis





LRT rail signals in preparation for testing at SouthWest Station Interlocking in Eden Prairie

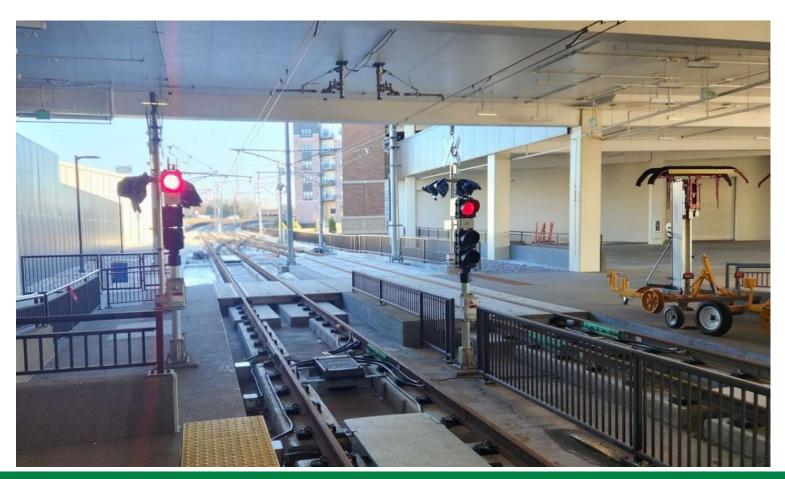




Lighting in TH 62 LRT Tunnel in Minnetonka





Signal house cable pulling and termination work at Opus Station in Minnetonka



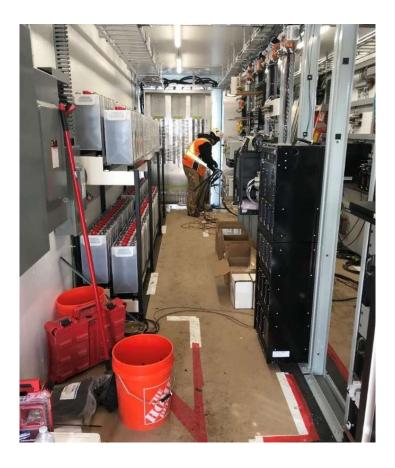



TPSS 309 site work and the AC and DC substation house foundations poured near Shady Oak Station in Hopkins





TPSS 311 foundation poured under Excelsior Boulevard LRT Bridge in Hopkins





OCS poles installed through Louisiana Avenue Station in St. Louis Park





OCS poles installed through the Beltline Boulevard Station crossing in St. Louis Park





Consent Business

DBE Achievement Report

DBE Achievement as of Feb 29, 2024

Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	% DBE to Date	As of Date
LMJV 16% Goal	Civil	\$1,043,392,388	\$966,659,852	\$231,219,007	23.9%	2/29/24
APJV 12% Goal	Systems	\$239,906,397	\$160,730,741	\$25,357,090	15.8%	11/30/23
	Closed Contracts	\$41,626,766	\$41,626,766	\$6,539,604	15.7%	
		Contract Amount	Billed to Date	DBE Billed to Date	% DBE to Date	
15% Goal		\$1,324,925,551	\$1,169,017,359	\$263,115,701	22.5%	

Non-Consent Business

Civil Contract Work

Civil Contract DBE Updates



MARCH – DBEs working on project



- E&J Rebar
- Gunnar Electric
- MBE
- On Call Pavement Sweepers
- PWS
- Safety Signs
- Stonebrook Fence
- Sun Mechanical

Civil Contract Workforce Achievement Updates





MONTHLY WORKFORCE - March 2024 IN & OUT BREAKDOWN (LMJV/Lunda/CS McCrossan)

IN REPORT	TOTAL MALE		WHITE FEMALE	MINORITY MALE	MINORITY FEMALE	
TRANSFERS	0	0	0	0	0	
REHIRE/ RETURN	3	3	0	0	0	
NEW HIRE	2	2 0		0	0	

OUT REPORT	TOTAL	WHITE MALE	WHITE FEMALE	MINORITY MALE	MINORITY FEMALE 0	
TRANSFERS	12	9	0	3		
Lay-Off	0	0	0	0	O	
Voluntary Leave			0	0	0	

GOOD FAITH EFFORT – Previous

2nd Talk w/ Trades Event for Building Strong Communities Program – 3/21/2024

40 BSC Participants 6 Union Stations – project rep & union rep

Collected Surveys & 6+ applications UPDATE: Working w/ internal teams at Lunda, CS McCrossan, Subcontractors on potential placement of BSC candidates



GOOD FAITH EFFORT – Current



Helmets 2 Hardhats

- Registered for their H2H Job Board. LMJV will post any positions for LMJV that may come up on H2H board. Working with Lunda & CSMcCrossan to also utilize
- H2H presenting at April Sub Meeting. Goal to get 80%+ subs utilizing H2H Job Board
- -H2H is now partnered with us on upcoming JA/ROTC class event on May 2nd



GOOD FAITH EFFORT – Current



Building Strong Communities – Graduation Celebration May 3

- Lunda/LMJV is on the Graduation Day Planning Committee that meets weekly
- Lunda/LMJV is assisting with invites & RSVPs for BSC grads/partners –
 Please let me know if you'd like to receive invitation
- Day of Event set up, assisting registration, logistics, people movers, food, etc



GOOD FAITH EFFORT – Coming Up



Building Strong Communities - Graduation May 3rd

Lake Street Works - Mock Interviews April 18

- Graduation May 8th

Junior Achievement - Amazing Rails Event May 2nd

MN Con Crew Hiring Fair - Carpenters Hall May 14th

2024 Rockin' the Rails DATE: Late Sept/Early Oct

- Planning meetings underway

Systems Contract Work

Systems Update

- APJV will participate in Junior Achievement Outreach on May 2, 2010 in conjunction with LMJV
- APJV will attend Build Strong Communities graduation Academy on Friday, May 3, 2023.
- APJV will participate in Mock Interviews at Summit Academy on Friday, May 10, 2023.

Workforce Achievement Update

SWLRT – Systems Workforce Trade Participation by Hours

February 2024

TRADES	Total	Male	Female	Female %	POCI	POCI %
Carpenter	6.00	5.00	1.00	16.67%	1.00	16.67%
Cement Finisher	1.00	1.00	-	0.00%	-	0.00%
Electricians	29.00	26.00	3.00	10.34%	7.00	24.14%
Equipment Operators	7.00	7.00	-	0.00%	-	0.00%
Ironworkers	5.00	5.00	-	0.00%	2.00	40.00%
Laborers	27.00	27.00	-	0.00%	9.00	33.33%
Surveyors	1.00	1.00	-	0.00%	-	0.00%
Truck Driver	2.00	2.00	-	0.00%	-	0.00%
TOTALS	78.00	74.00	4.00	5.13%	19.00	24.36%

APJV – Systems Contract, DBE with Fieldwork in February 2024

- Gunnar Electric
- Bald Eagle
- Moltron Builders

Announcements

Public Invitation

- Each speaker is limited to a three-minute presentation
- Pre-register as you sign in for attendance at the start of the meeting



Closing

- Next Meeting date: May 16th, 2024, from 2:00 4:00 PM
 - Virtual
- Adjourn

MORE INFORMATION

Website: GreenLineExt.org

Email: swlrt@metrotransit.org

Twitter: @GreenLineExtMN

Instagram: @GreenLineExtMN
