

Target Field Station Update




Transportation Committee

March 10, 2014

Presented by

Robert Rimstad, P.E.

Metro Transit, Engineering and Facilities

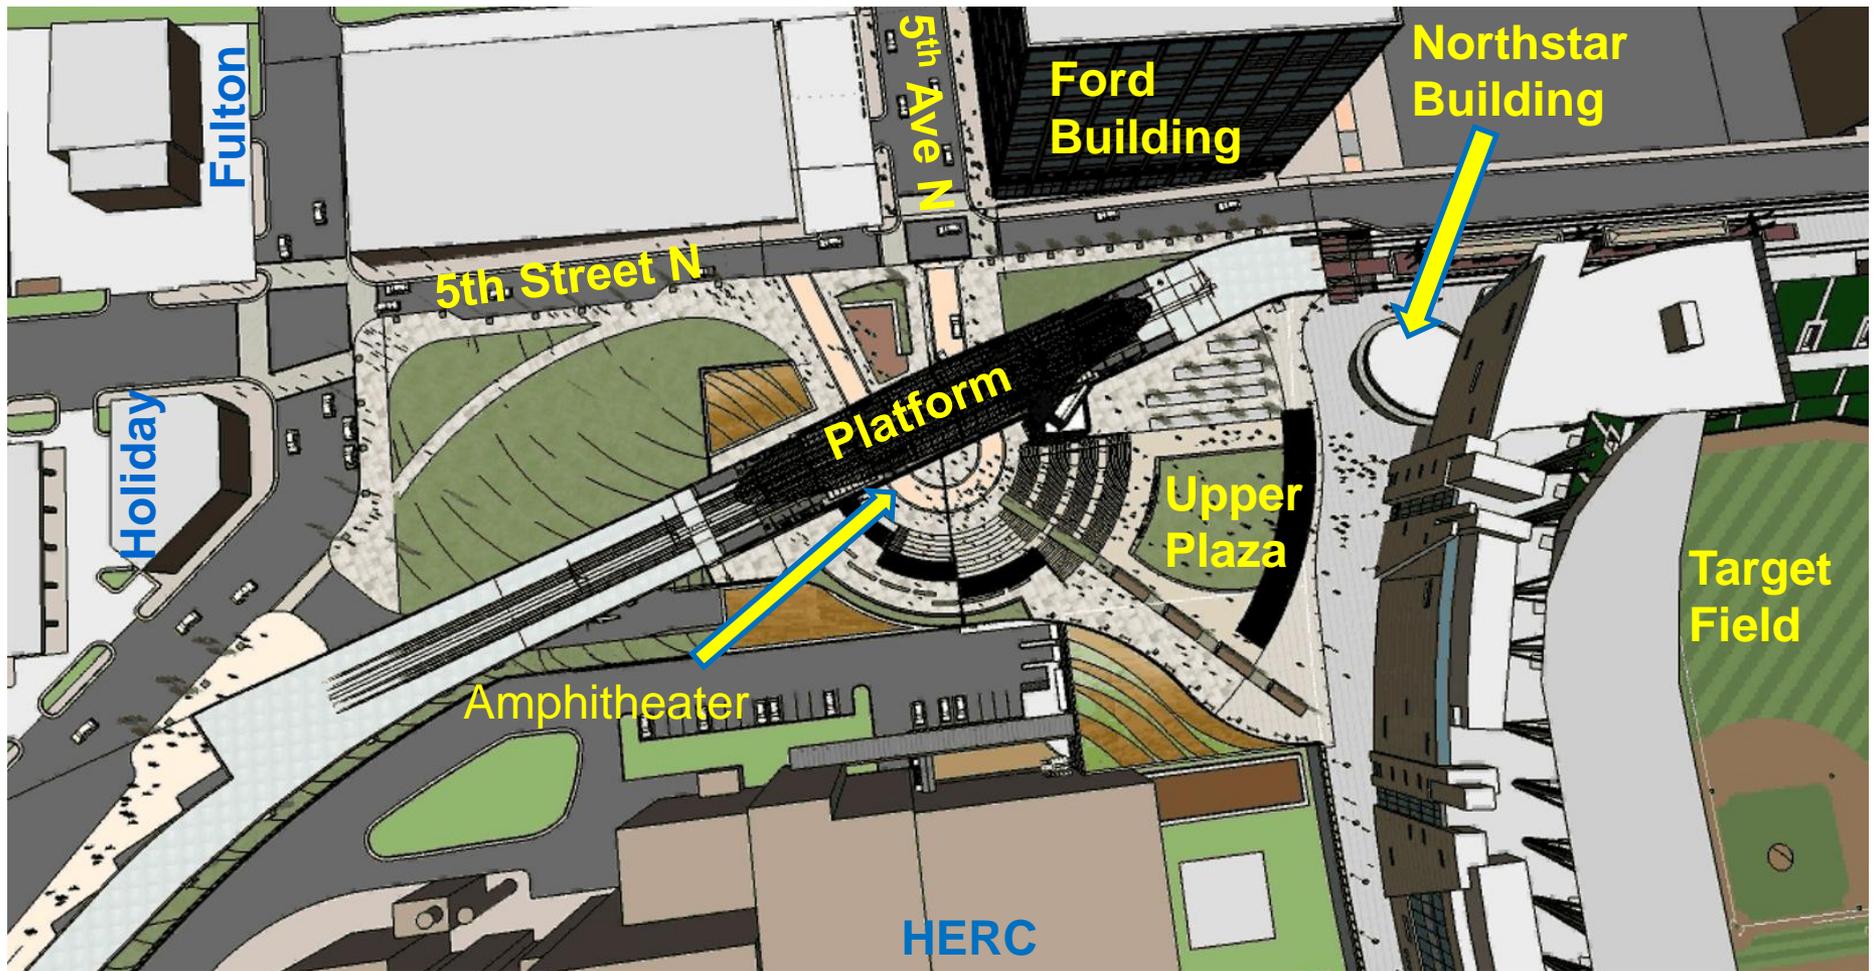

Schedule


- 1) LRT systems testing and integration February - March 2014
- 2) Overhead catenary system cut over March 7-9
- 3) April 5 - Target date for Blue Line Operations to Utilize Tail Track
- 4) April 19 – Target Date Green Line Test Trains begin operating to Target Station (Interchange) Platforms on Pre-Revenue Service Schedule
- 5) Grand Opening May 17, 2014









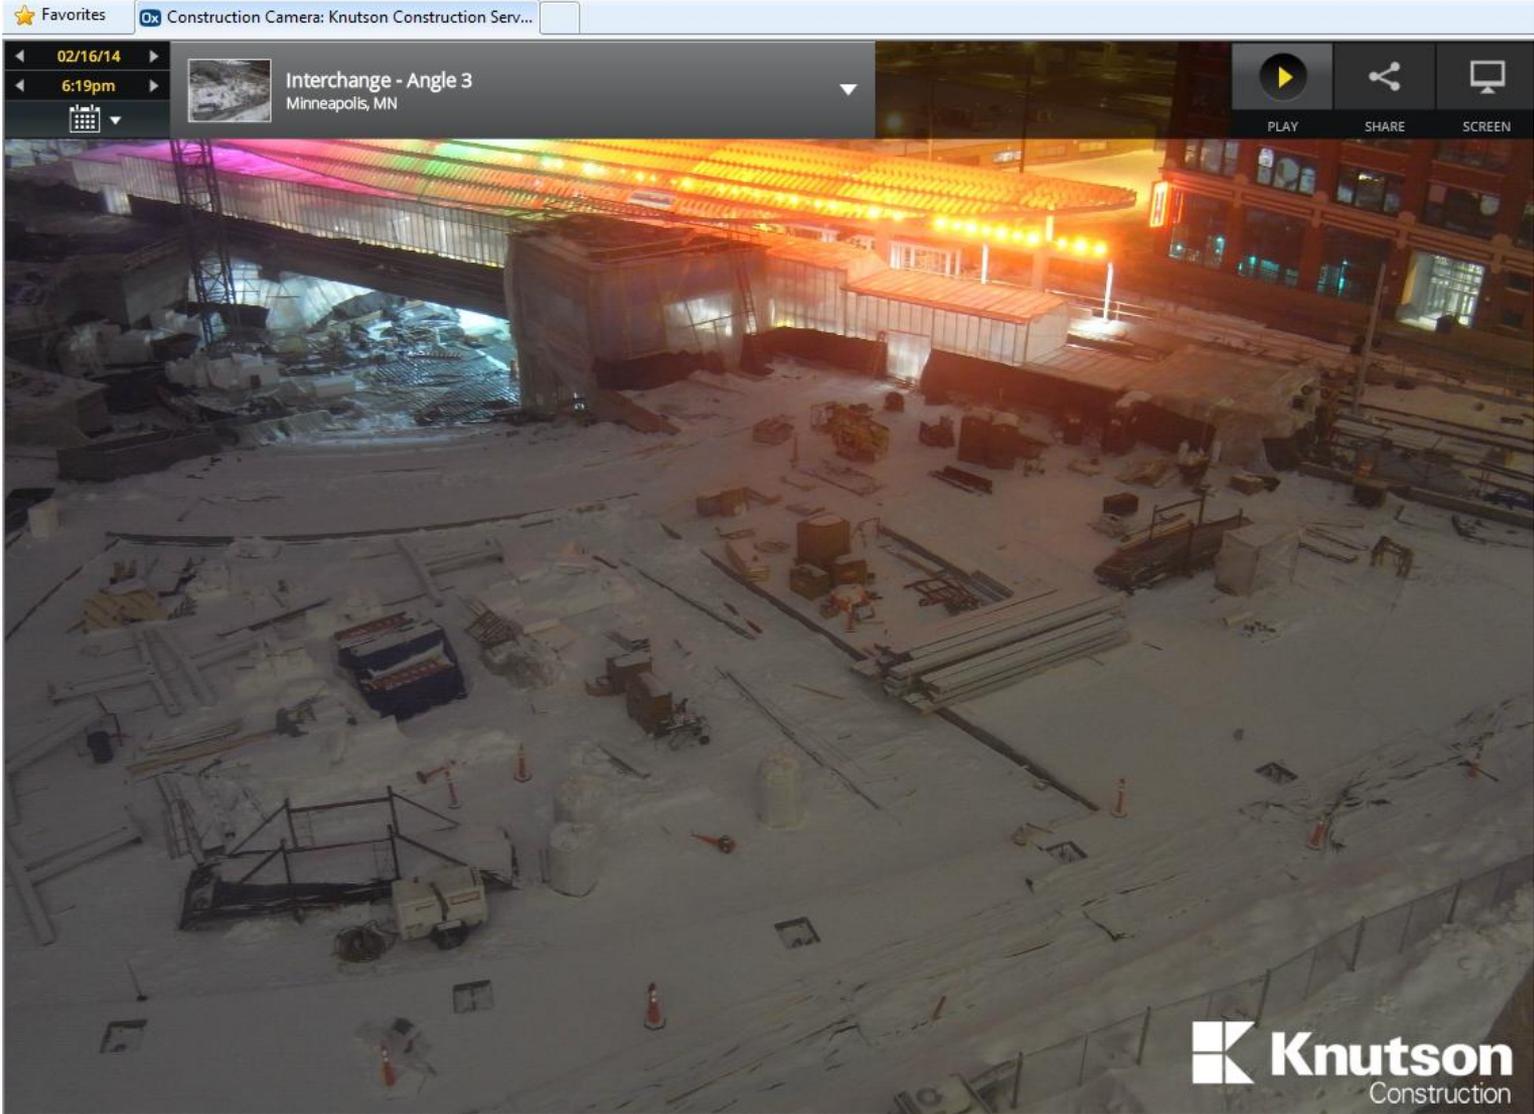



LRT platform shelter work continues (steel work)



Finish work of concrete in LRT platform area




Work also continues on the planters
in the Cascade/amphitheater



The Interchange

\$77M Budget

72.9% Complete through 1/31/2014

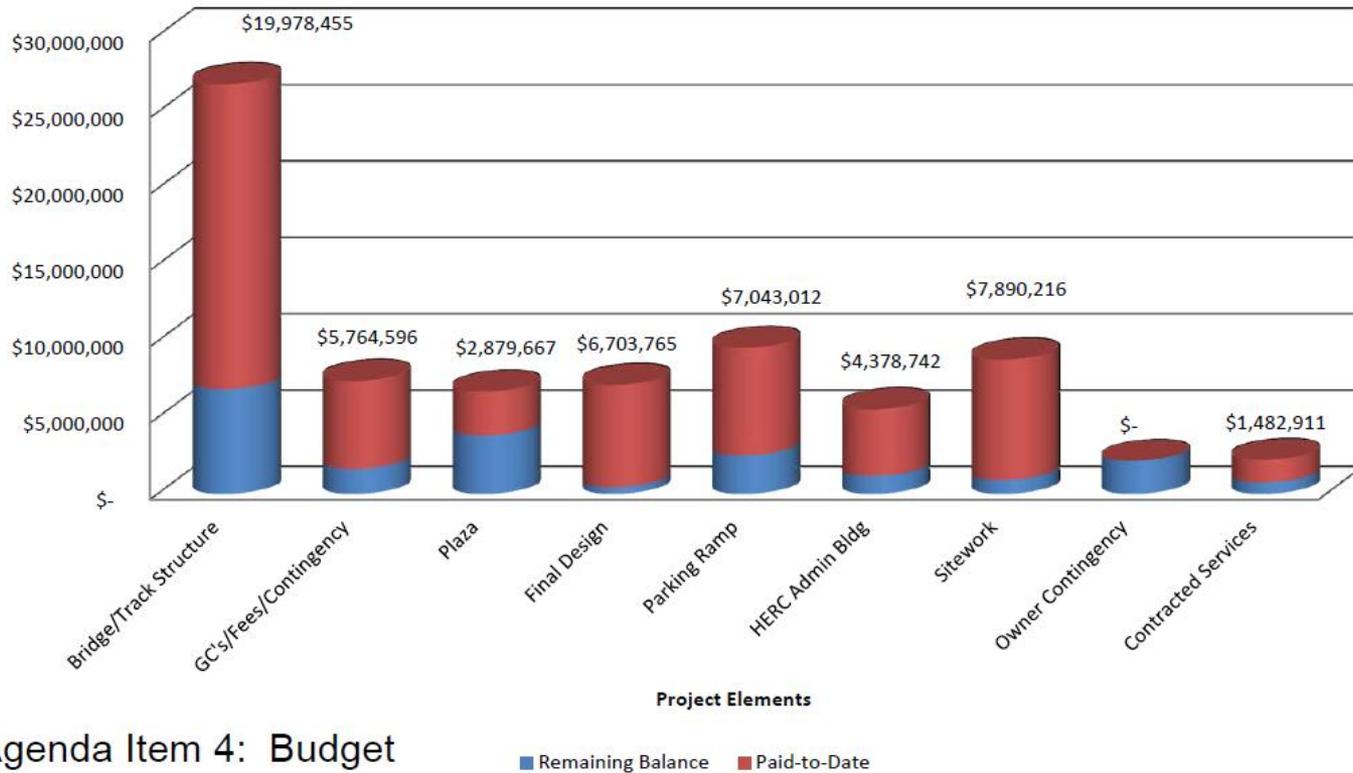

Agenda Item 4: Budget

**For more information +
a live construction webcam
visit www.theinterchange.net**



Interchange
The new Target Field Station

Robert Rimstad, P.E.

Robert.Rimstad@metrotransit.org

612-349-7768
