


Transit Police Headquarters Construction Update



Cathy Nordin
Sr. Project Coordinator
Engineering and Facilities

Transportation Committee - December 11, 2017

Site

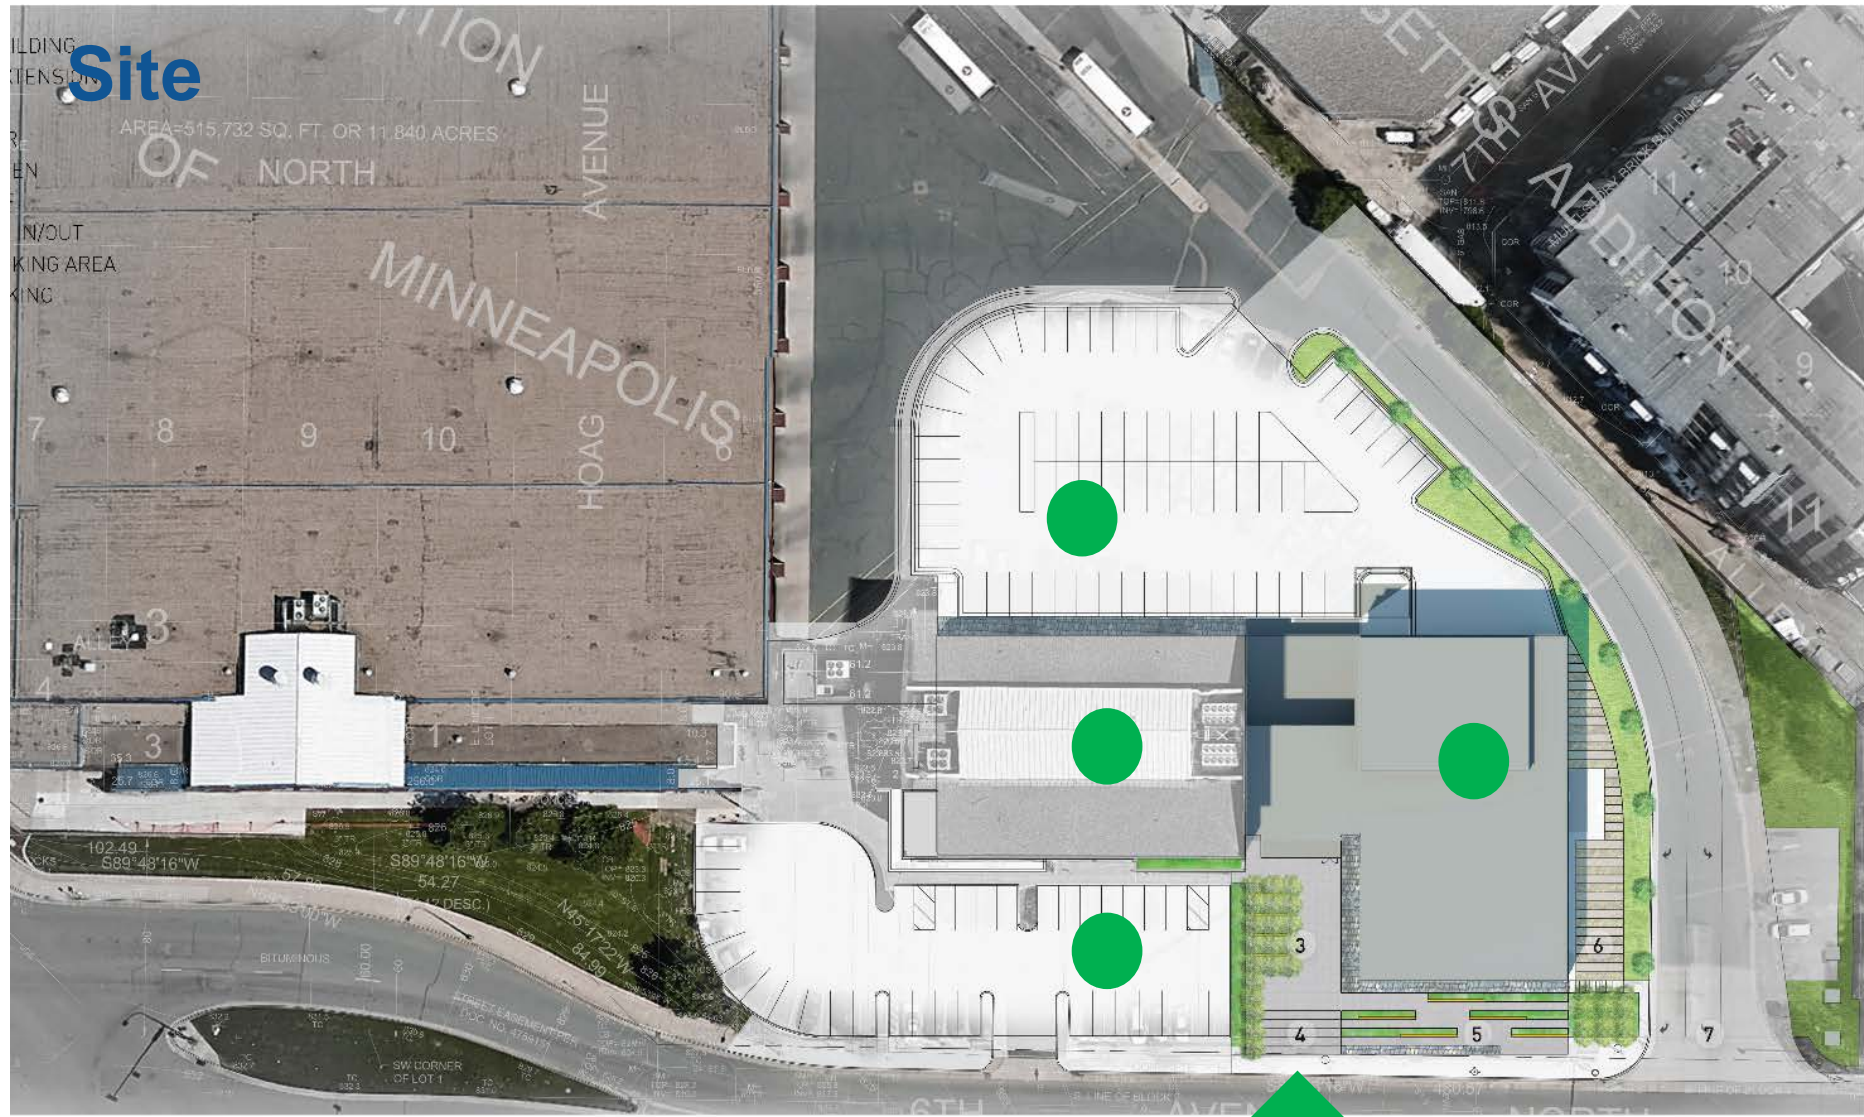

Project Status

- August 15 – Site Preparation Complete – Driveway open
- September 6 – Building construction Start Date
- September 25 - Partial Building Demolition
- October 11 through November 11 – Pile Driving (164)
- November and December – Foundation Walls

Next Steps

- December through March – Steel Erection
- March - Roofing
- March and April - Exterior Wall framing

Construction Photos



Partial Building Demolition



Pile Driving




Foundation Wall Framing



Foundation Wall

Project Milestones

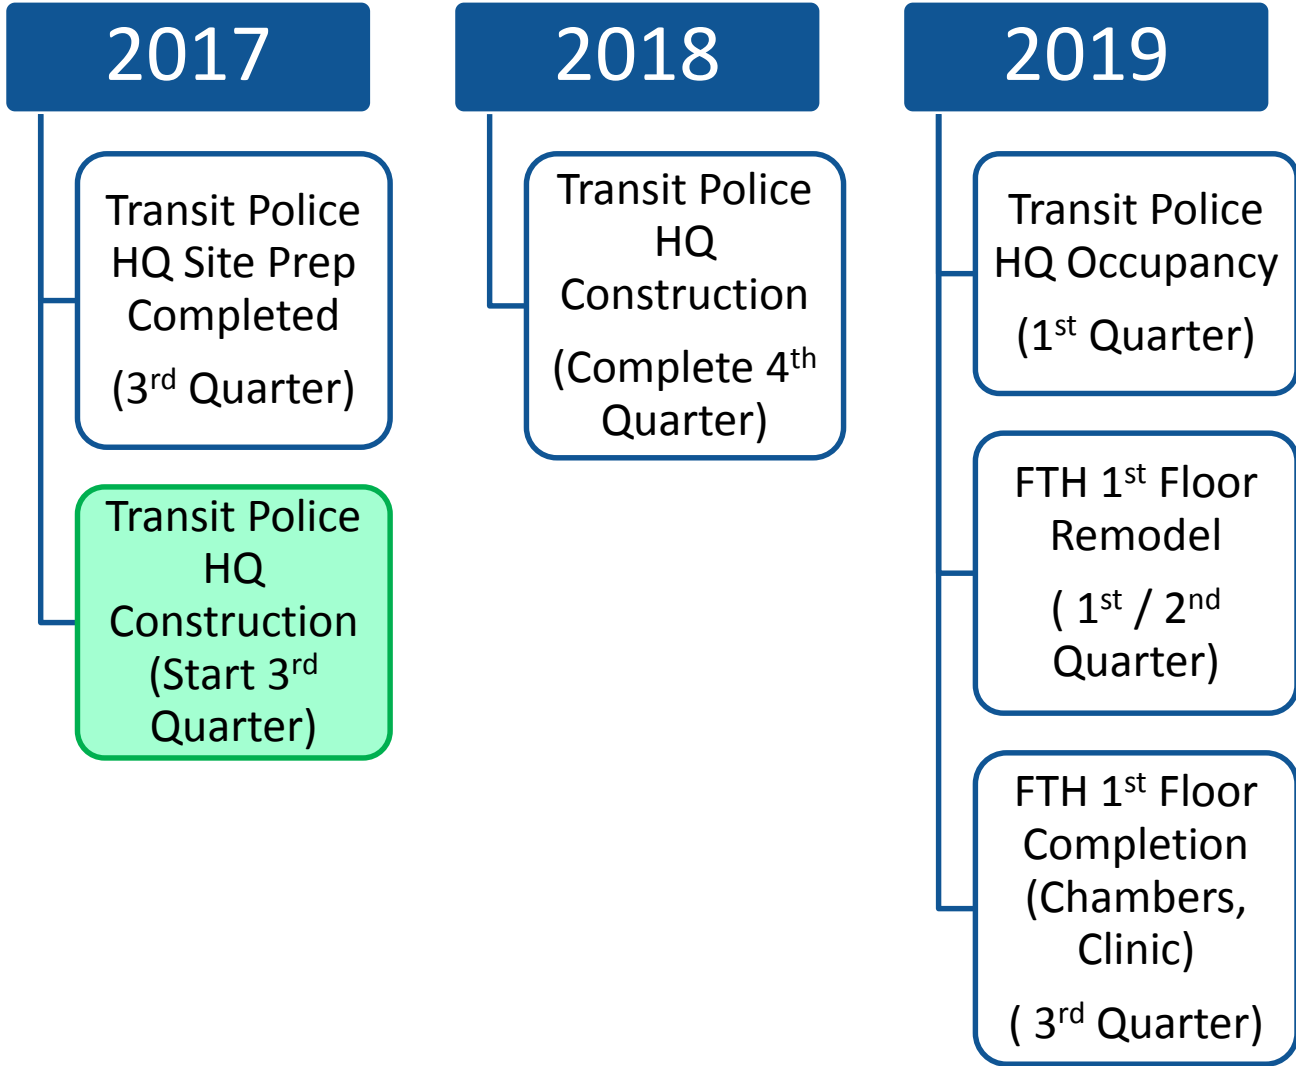


Transit Police HQ Funding

- Federal 5307 Funds/RTC Match: \$ 27.50 M
- Council Medical Self Insurance: \$ 0.25 M
- Total Funding: \$ 27.75 M

Transit Police HQ Budget

- Design Contract: \$ 2.80 M
- Project/Constr. Management: \$ 1.25 M
- Construction – Site Prep: \$ 2.40 M
- Construction - Building: \$ 18.00 M
- Furniture and Equipment: \$ 1.75 M
- Contingency: \$ 1.55 M
- **Total Budget: \$ 27.75 M**

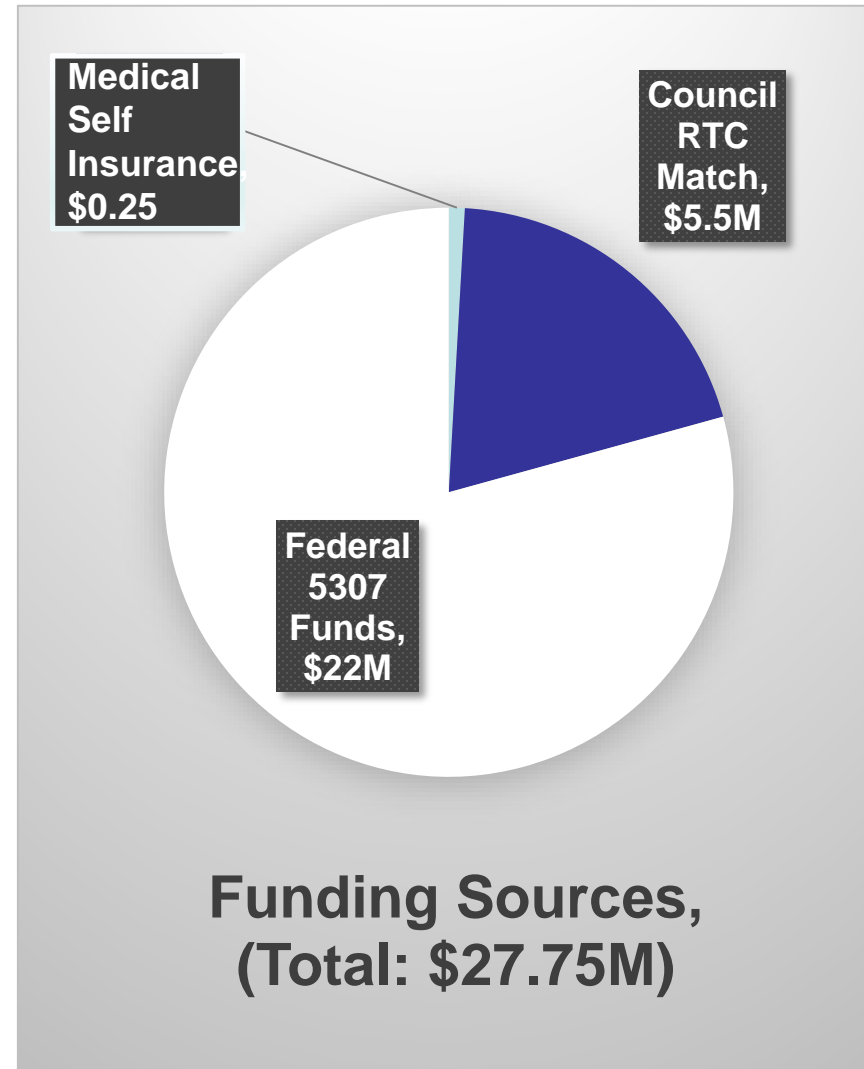

Questions



<https://www.metrotransit.org/campus-construction>
