

SOUTHWEST

Green Line LRT Extension



Southwest LRT Corridor Management Committee

September 1, 2021



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

Today's Topics

- Project Update
- DBE & Workforce Update
- Communications & Outreach Update



Project Milestone: LRT in Hopkins!



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK

Aug. 24: Senator Tina Smith and FTA Administrator Nuria Fernandez Visit SWLRT



Project Update

Jim Alexander
SWLRT Project Director

SouthWest Station, Eden Prairie




EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS



Prairie Center Drive LRT Bridge, Eden Prairie



Valley View Road LRT Bridge, Eden Prairie

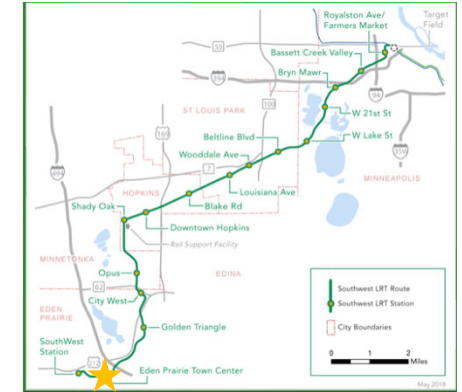

EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS




Nine Mile Creek LRT Bridge, Eden Prairie




EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS



Golden Triangle Station, Eden Prairie

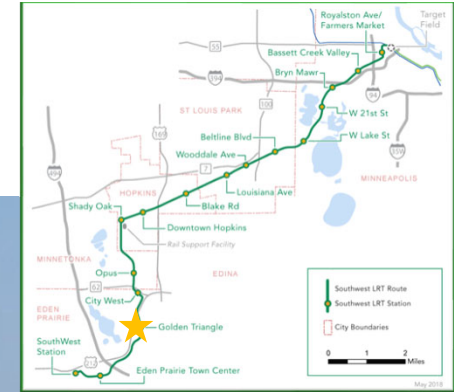

Shady Oak Rd/TH212 LRT Bridge, Eden Prairie

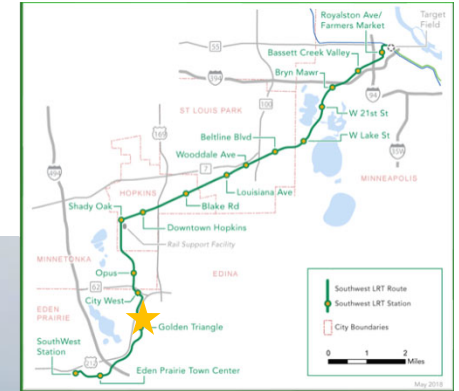


TH 62 LRT Tunnel, Eden Prairie

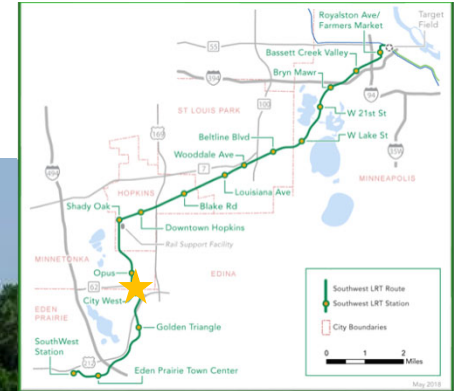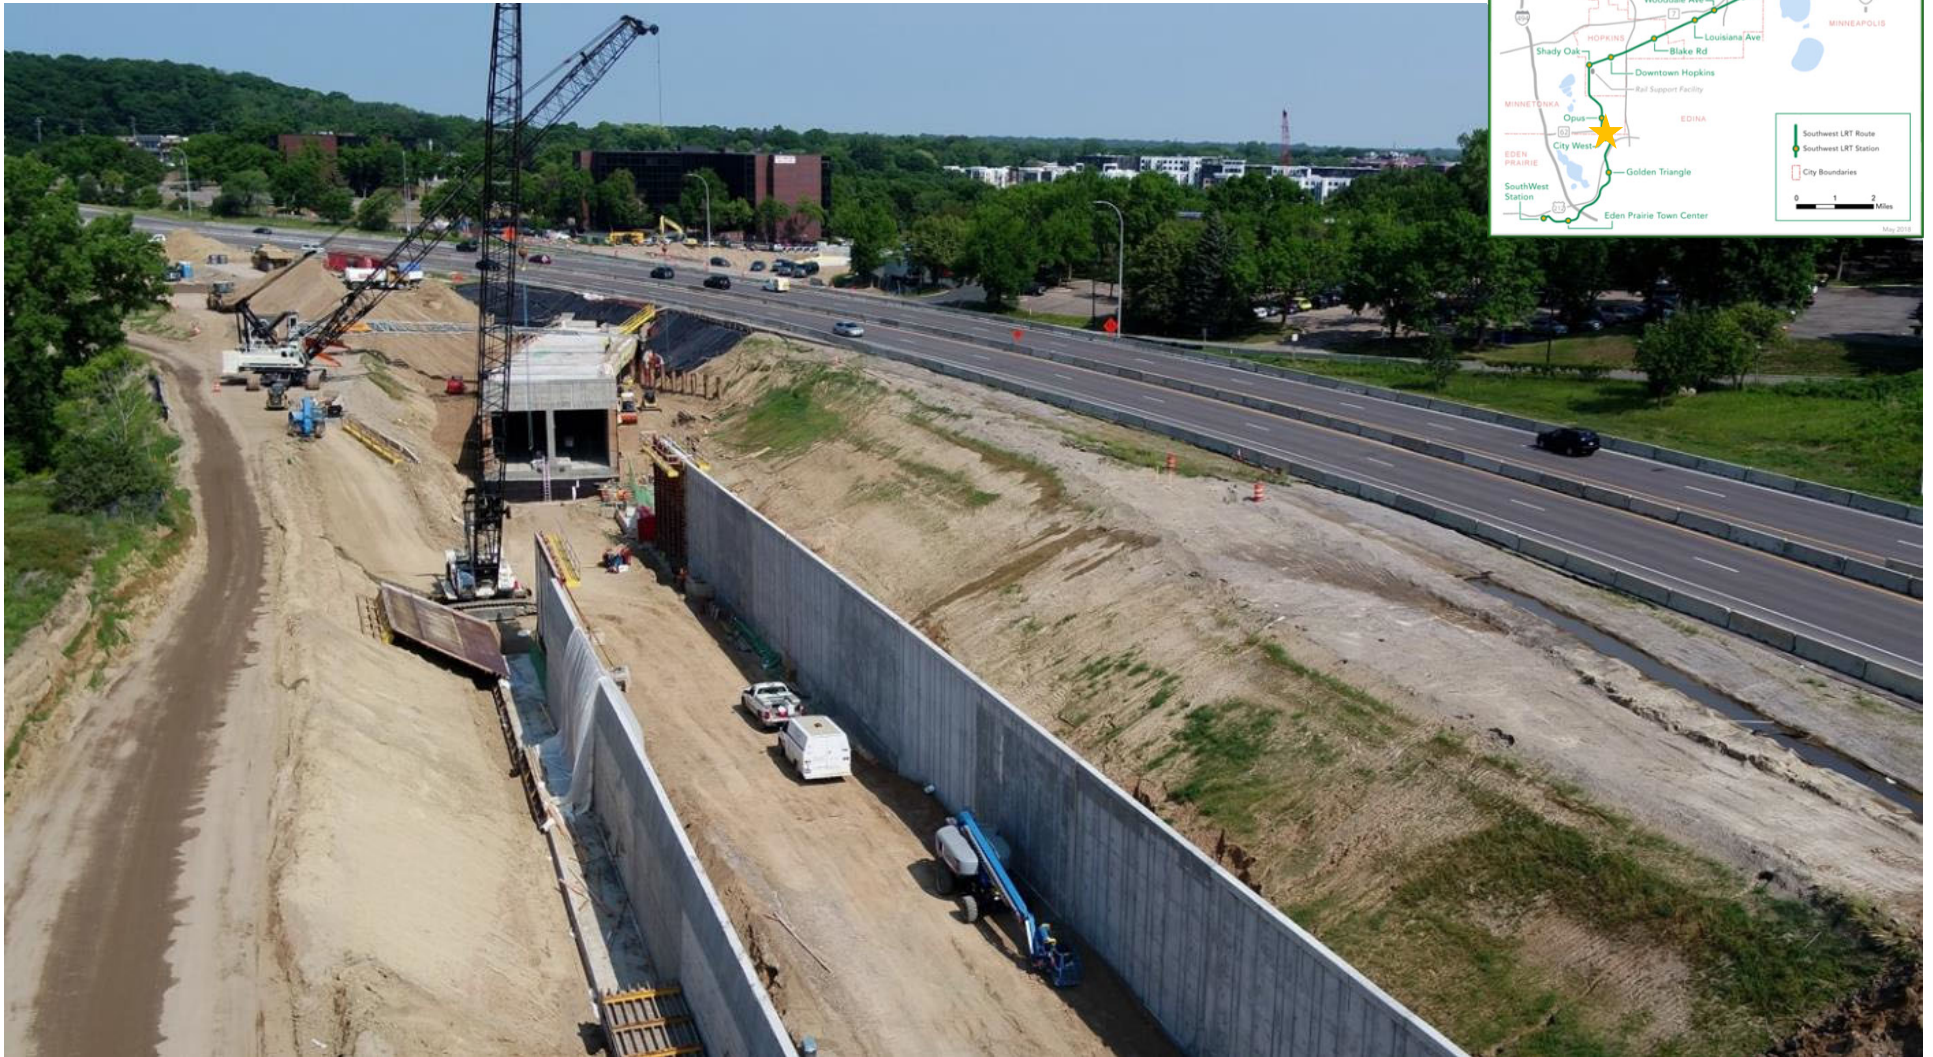

Smetana and Feltl Road Bridges, Minnetonka




Minnetonka-Hopkins LRT Bridge

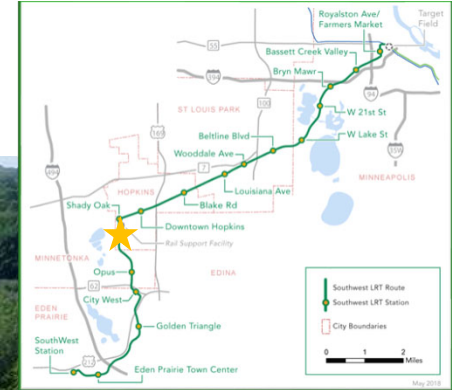

Shady Oak Station, Hopkins



Cantilevered Form Traveler at Excelsior Boulevard LRT Bridge, Hopkins

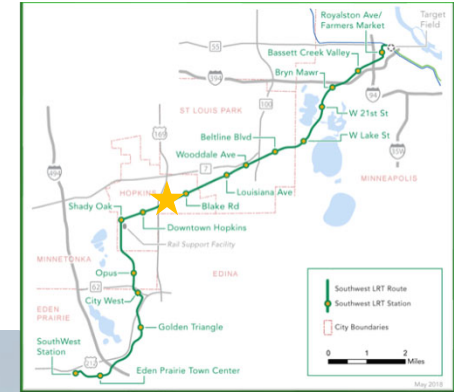


Blake Road Pedestrian Underpass, Hopkins



Louisiana Avenue LRT Bridge, St. Louis Park




Kenilworth LRT Tunnel, Minneapolis

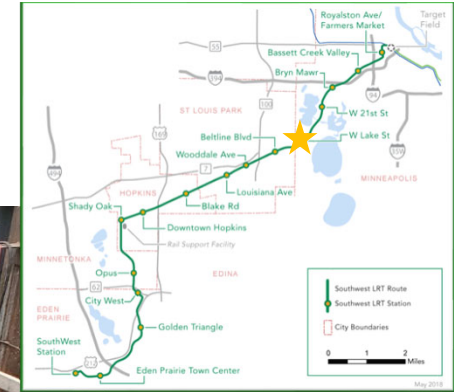

EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS



Cedar Lake Channel LRT Bridge, Minneapolis

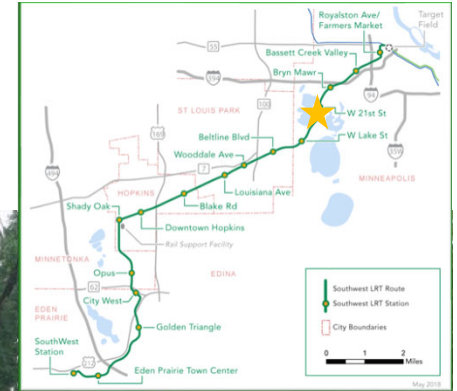

West 21st St Station, Minneapolis



Wall Panels for the Corridor Protection Barrier, Minneapolis



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

Glenwood Avenue LRT Bridge, Minneapolis



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

LRT Bridge over 5th Ave & 7th St, Minneapolis



Systems Contract Work

TPSS 15B in Factory Production Rain Testing



TPSS 15B Delivery to Franklin O&M Facility



Franklin O&M Facility

North Yard Modifications



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

West Runner Tracks



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

DBE and Workforce Update

Jon Tao
Met Council's Office of Equal Opportunity

Commercially Useful Function Visits


- OEO conducted CUF visits with 16 DBEs
 - 9 on the Civil construction contract
 - 2 on the Systems construction contract
 - 5 on the Franklin O&M Facility Modification contract



DBE Achievement as of June 30, 2021


Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	DBE Date %	As of Date
LMJV 16% Goal	Civil	\$950,521,491	\$495,468,008	\$102,573,802	20.7%	6/30/21
APJV 12% Goal	Systems	\$193,831,209	\$58,803,887	\$8,970,311	15.3%	6/30/21
LS Black 15% Goal	Franklin O&M Facility	\$39,180,098	\$29,599,752	\$5,821,738	19.7%	6/30/21
17% Goal	Closed Contracts	\$404,992	\$404,992	\$74,610	18.4%	
		Contract Amount	Billed to Date	\$ DBE to Date	% DBE to Date	
15% Goal		\$1,183,937,790	\$584,276,639	\$117,440,461	20.1%	

Civil DBE Participation as of Jun. 30, 2021

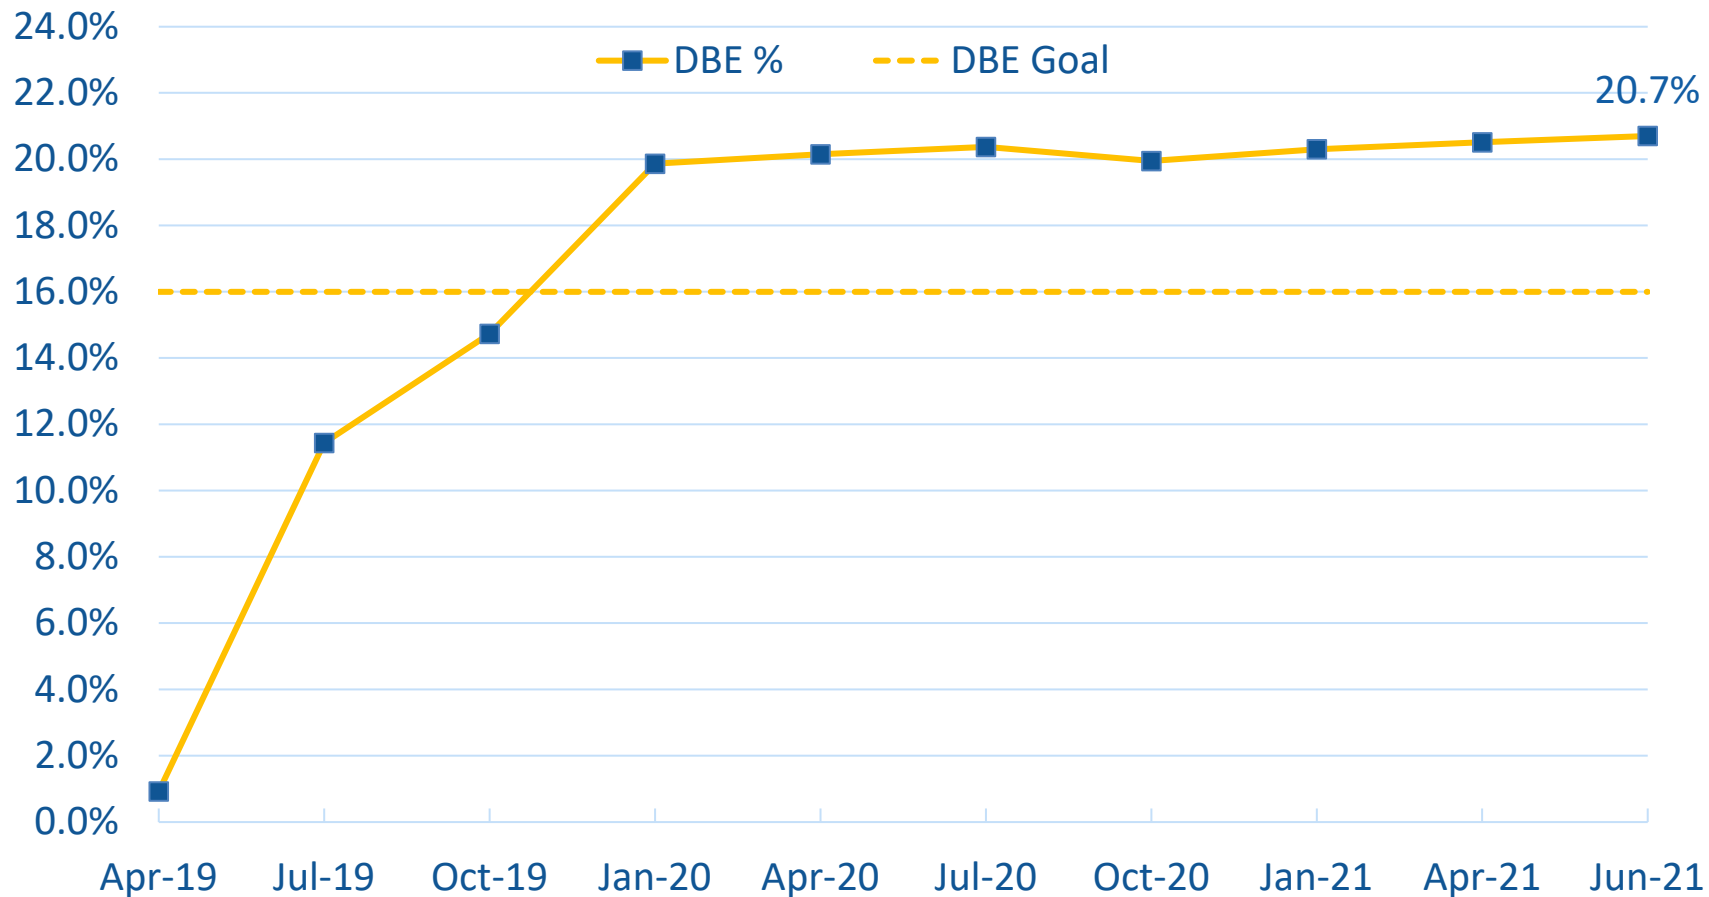


*DBE Goal for the Civil Contract is 16%

Systems DBE Participation as of Jun. 30, 2021

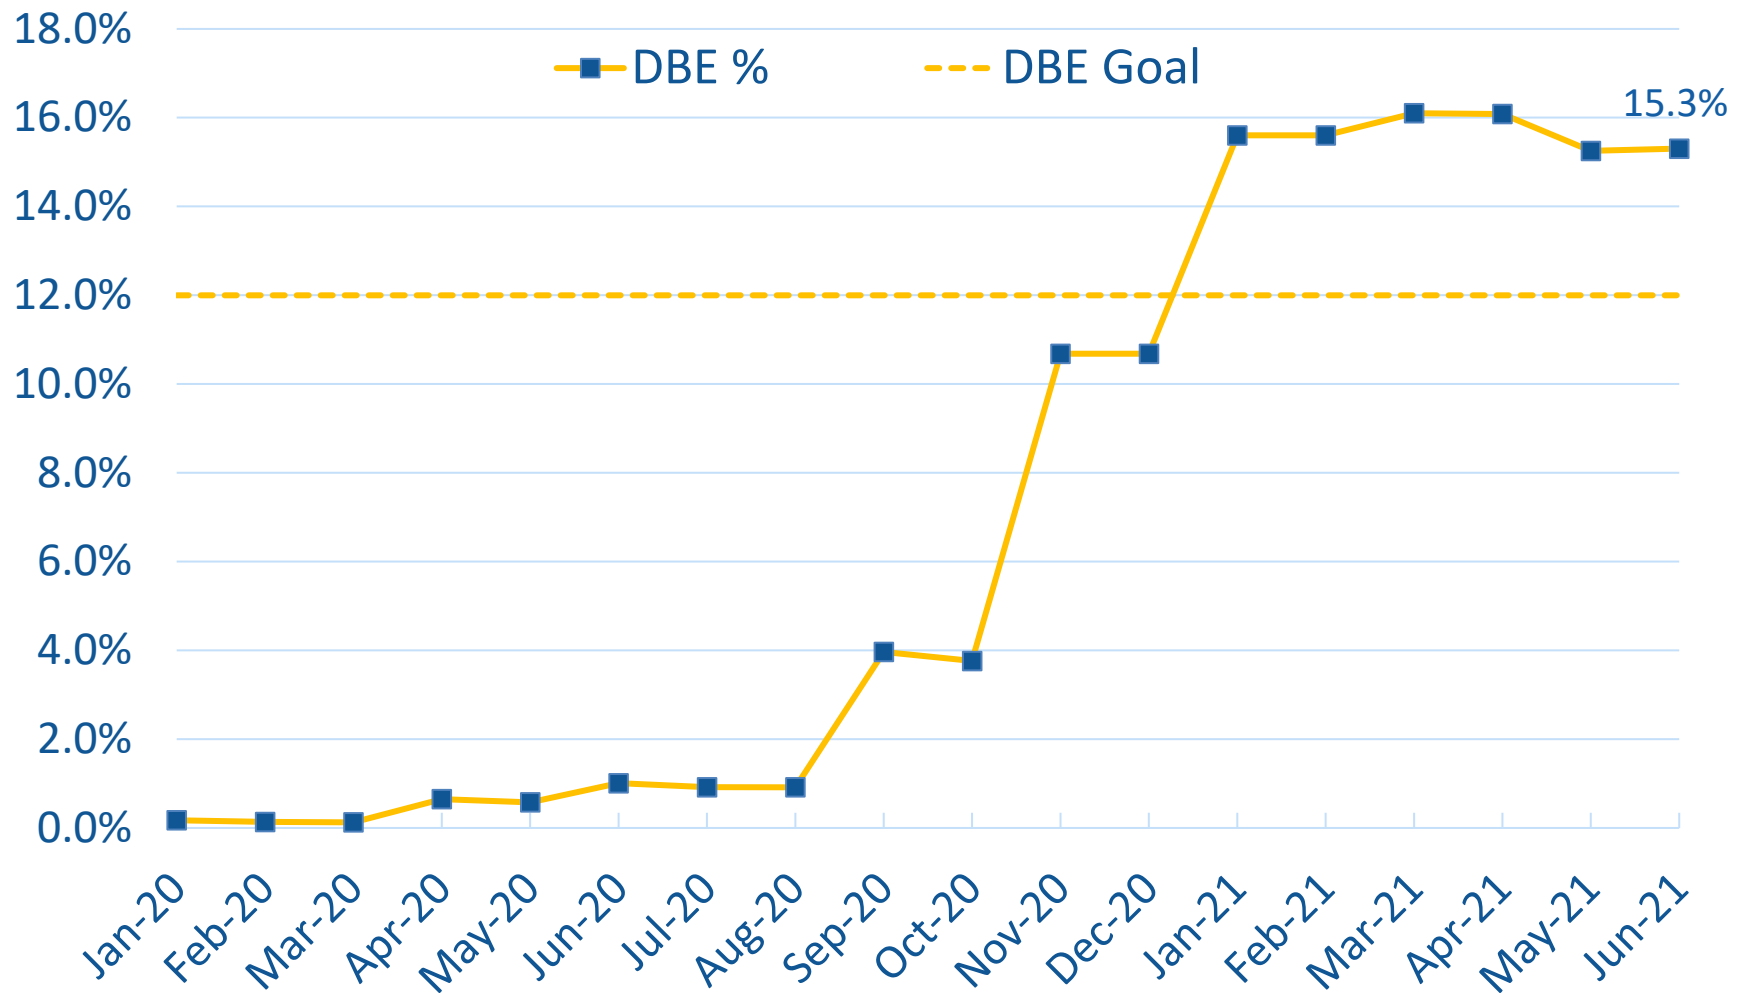

*DBE Goal for the Systems Contract is 12%

Franklin DBE Participation as of Jun. 30, 2021

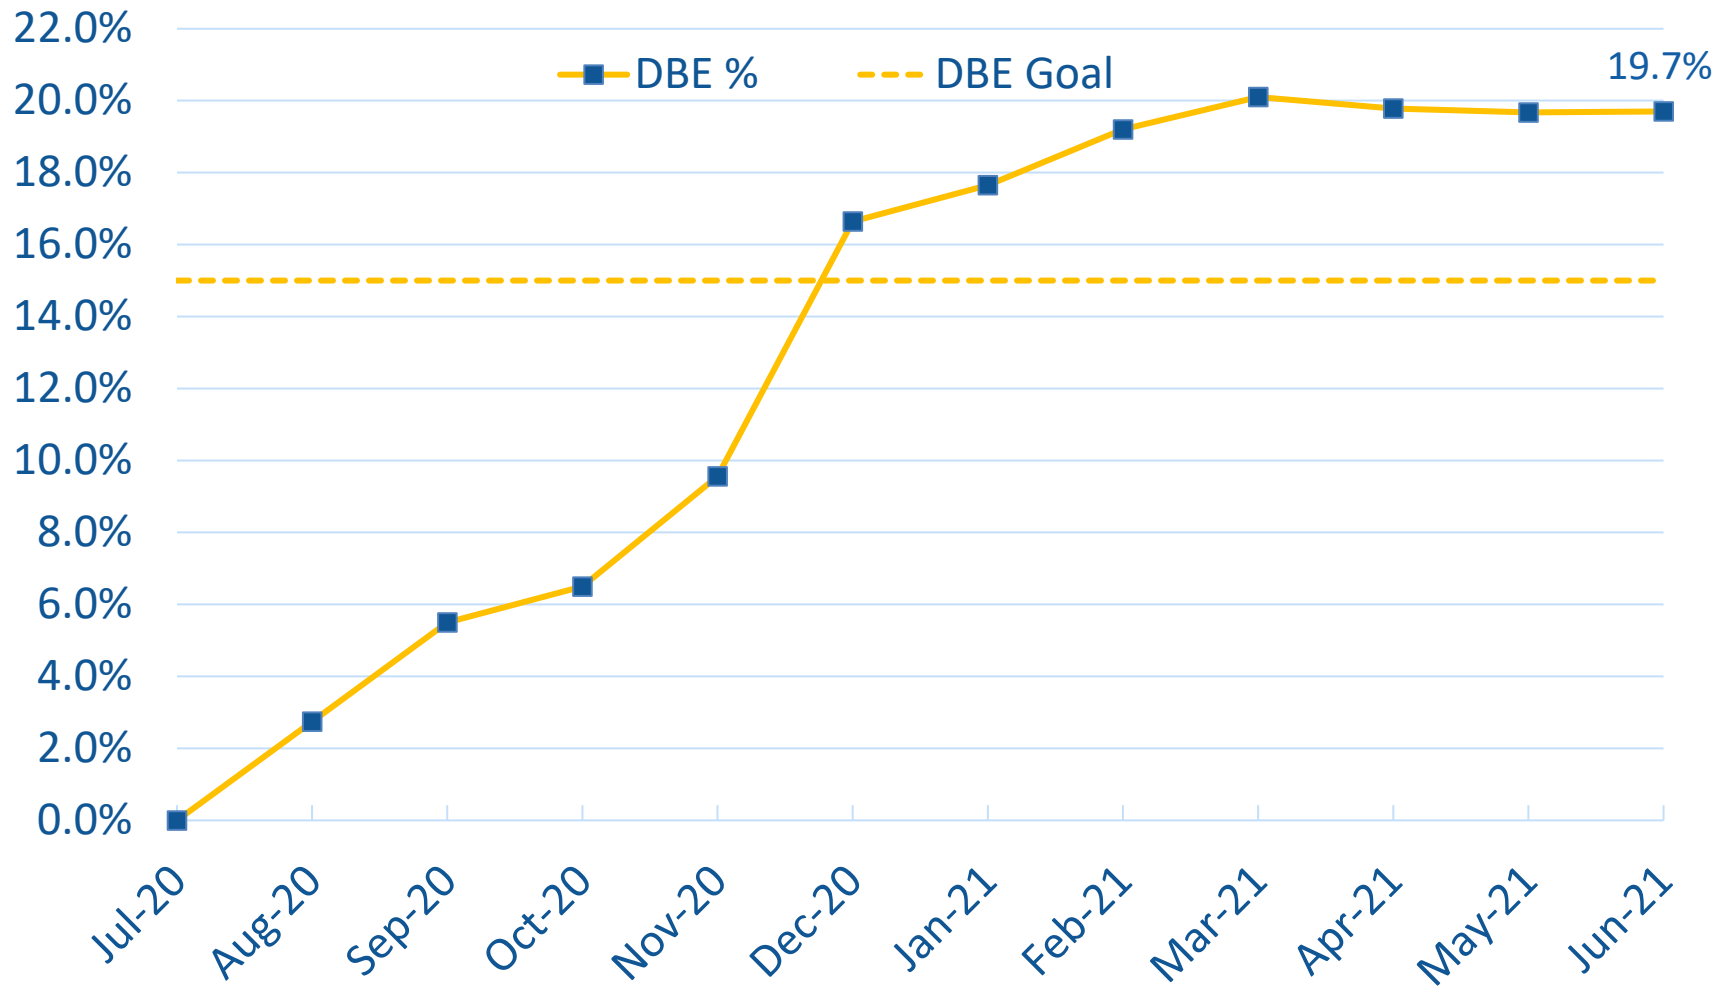

*DBE Goal for the Franklin O&M Contract is 15%

SWLRT Construction Contracts Disaggregated*

- Construction Contracts Total: \$1,183,937,790


Ethnic Group	Women		Men		Total	
Asian Pacific	\$	277,743	0.02%	\$ 40,021,329	3.38%	\$ 40,299,072 3.40%
Asian Subcontinent	\$		0.00%	\$ 1,900,001	0.16%	\$ 1,900,001 0.16%
Black	\$	43,369	0.00%	\$ 9,227,926	0.78%	\$ 9,271,295 0.78%
Hispanic	\$	727,600	0.06%	\$ 28,726,050	2.43%	\$ 29,453,650 2.49%
Native American	\$	3,812,256	0.32%	\$ 18,538,811	1.57%	\$ 22,351,067 1.89%
White Women	\$	119,918,487	10.13%			\$ 119,918,487 10.13%
DBE Contracts Total					\$ 223,193,571	18.85%

*Contract values are as of 6/30/21 and includes: Civil, Systems, Franklin O&M & OMF Demo

Disaggregated Construction DBE Data*

- DBE contract participation by state:


State	Totals
MN	\$ 192,852,513
FL	\$ 20,500,000
GA	\$ 6,907,529
IL	\$ 479,004
MD	\$ 1,000,000
SD	\$ 795,000
WI	\$ 659,526

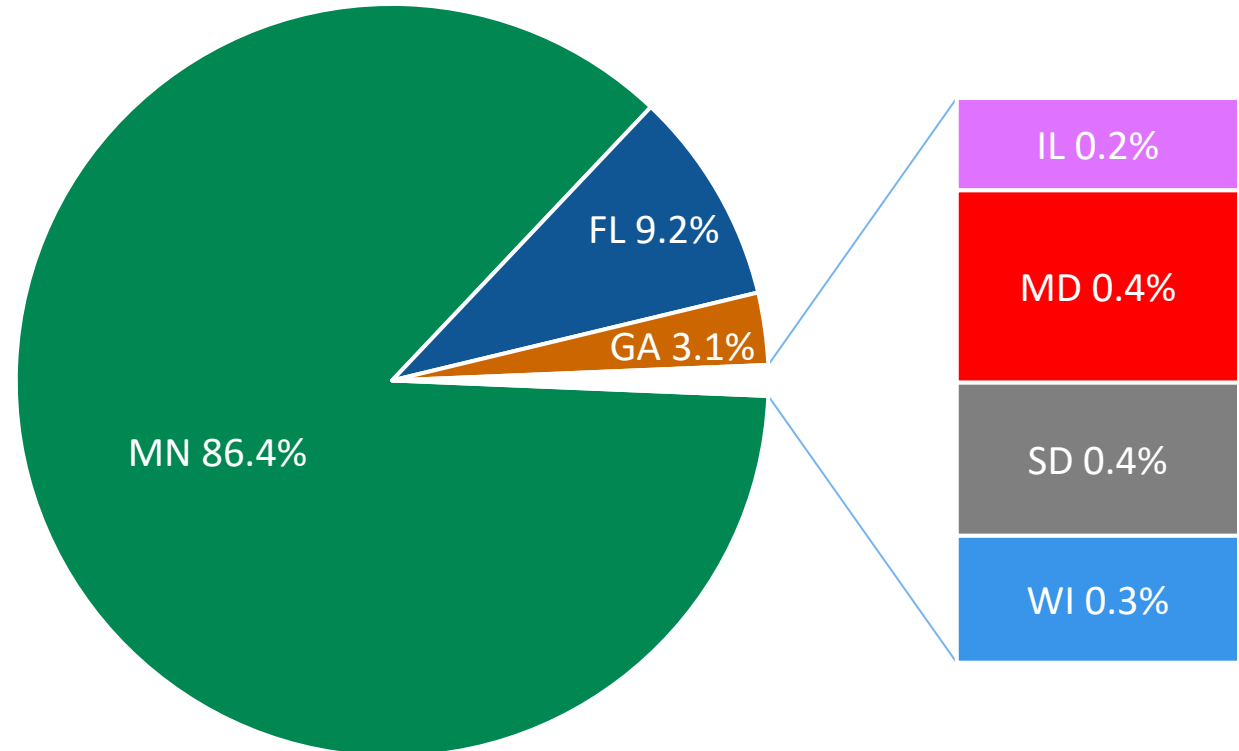

*Contract values for Civil, Systems, Franklin O&M, and OMF Demolition as of June 30, 2021

Civil Workforce Participation Percentage*


- June 2021: 83,947 hrs
- Civil Construction Total: 1,352,740 hrs

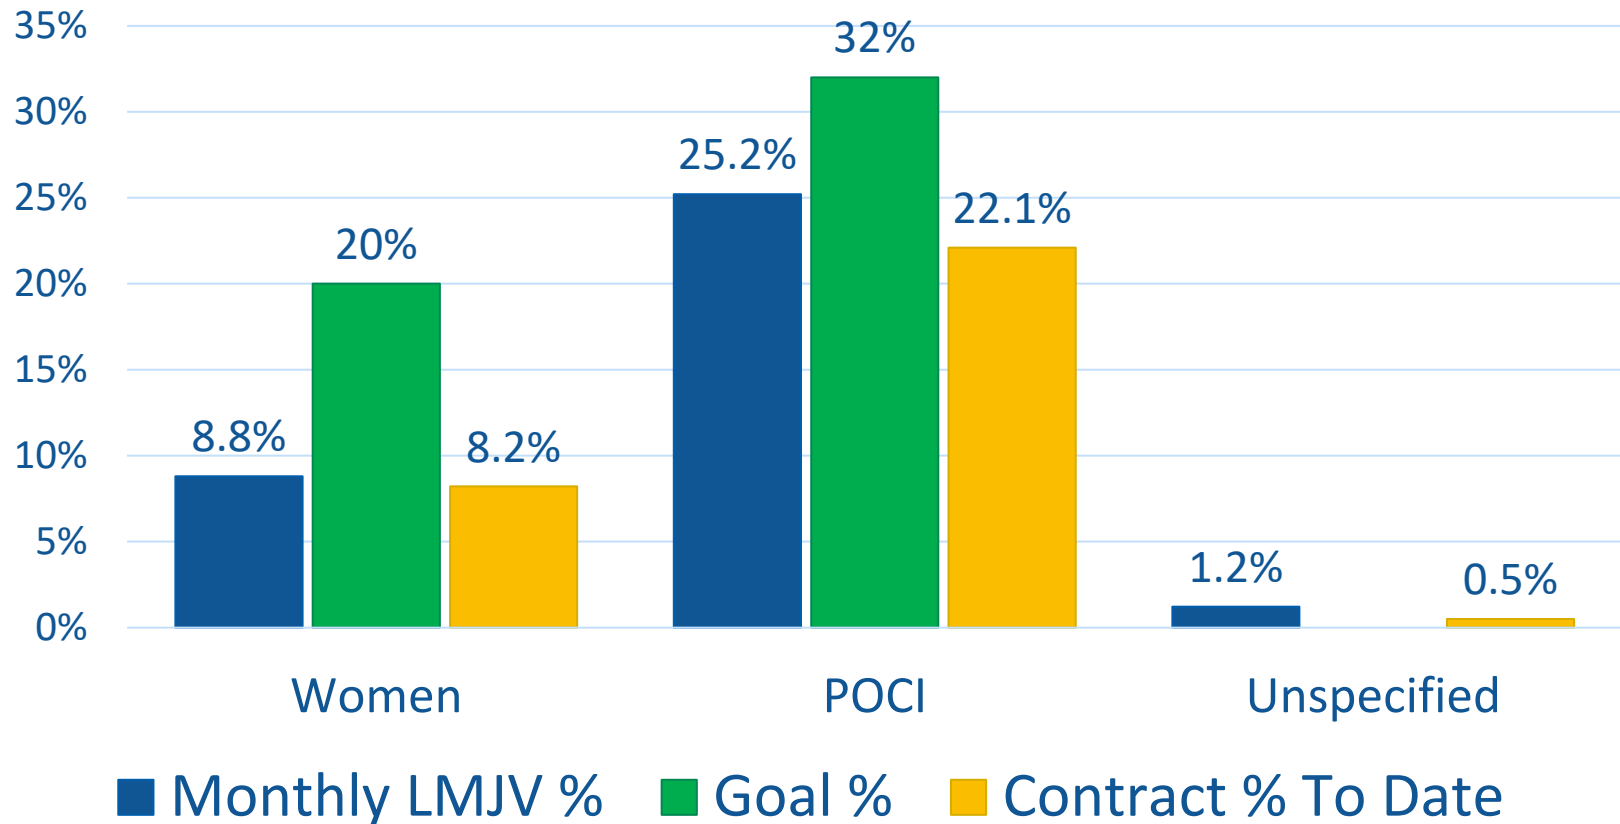

*Based on LCP Tracker Workforce Report for June 2021
People of Color/Indigenous (POCI)

Monthly Civil Workforce Participation*


- Total Women hours to date: 110,030 hrs
- Cumulative participation: 8.21%

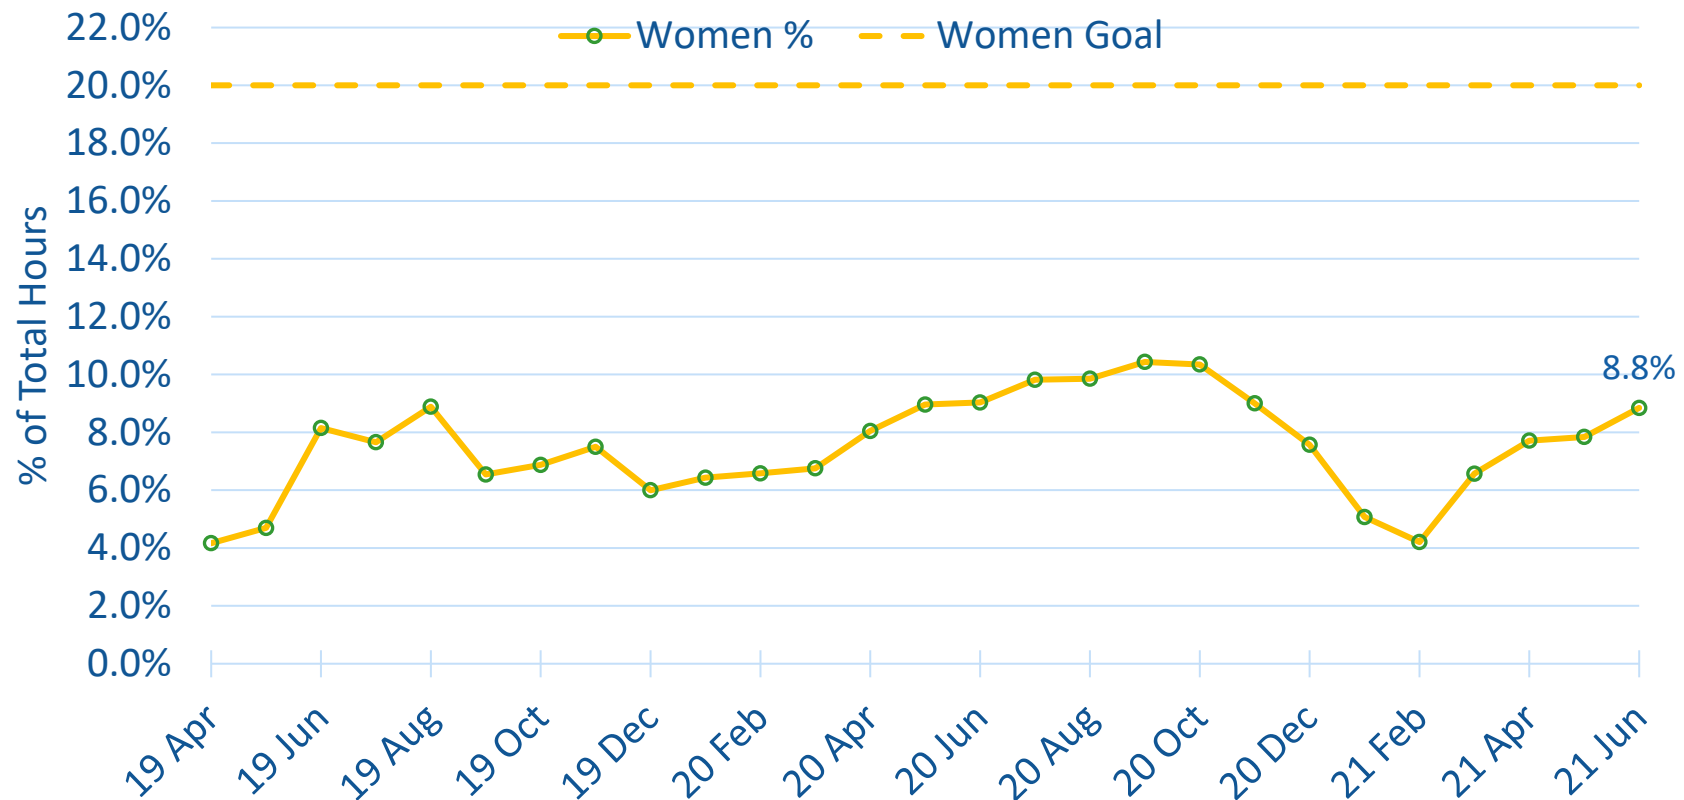

*Workforce data is based on the June 2021 report from LCP Tracker.

Monthly Civil Workforce Participation*

- Total POCI hours to date: 299,470 hrs
- Cumulative participation: 22.1%

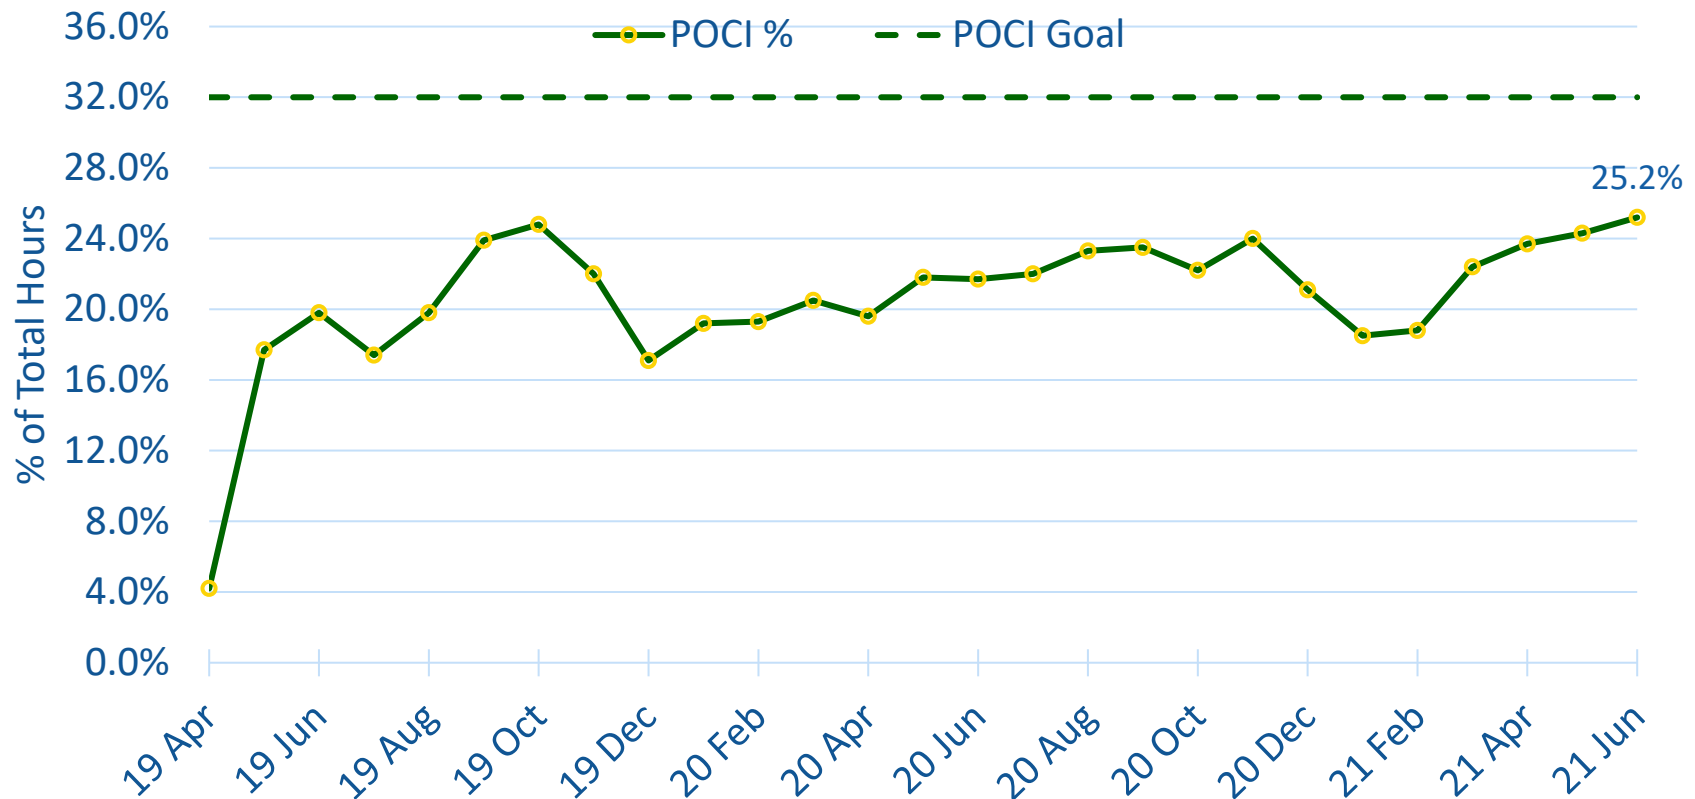

*Workforce data is based on the June 2021 report from LCP Tracker.

Civil Workforce Cumulative Disaggregated*


- Project Total: 1,352,740 hrs
- Total POCl: 299,470 hrs (21.1%)
- Total Women: 110,030 hrs (8.2%)

Ethnic Group	Women	Women %	Men	Men %	Total	Total %
Asian	91	0.0%	42,825	3.2%	42,916	3.2%
Black	15,971	1.2%	62,673	5%	78,644	5.8%
Hispanic	3,731	0.3%	127,217	9.4%	130,948	9.7%
Multi-racial	700	0.1%	18,574	1.4%	19,274	1.4%
Native American	10,492	0.8%	17,197	1.3%	27,689	2.0%
Not Specified	135	0.0%	6,382	0.5%	6,517	0.5%
White	79,911	5.9%	966,830	71.5%	1,046,741	77.4%

*Based on workforce data from LCP Tracker Reports. Women, People of Color and Indigenous People (POCl) participation from 12/1/18 – 6/30/21

Franklin O&M Workforce Participation Percentage*


- June 2021: 7191 hrs
- Franklin O&M Construction Total: 78,804 hrs

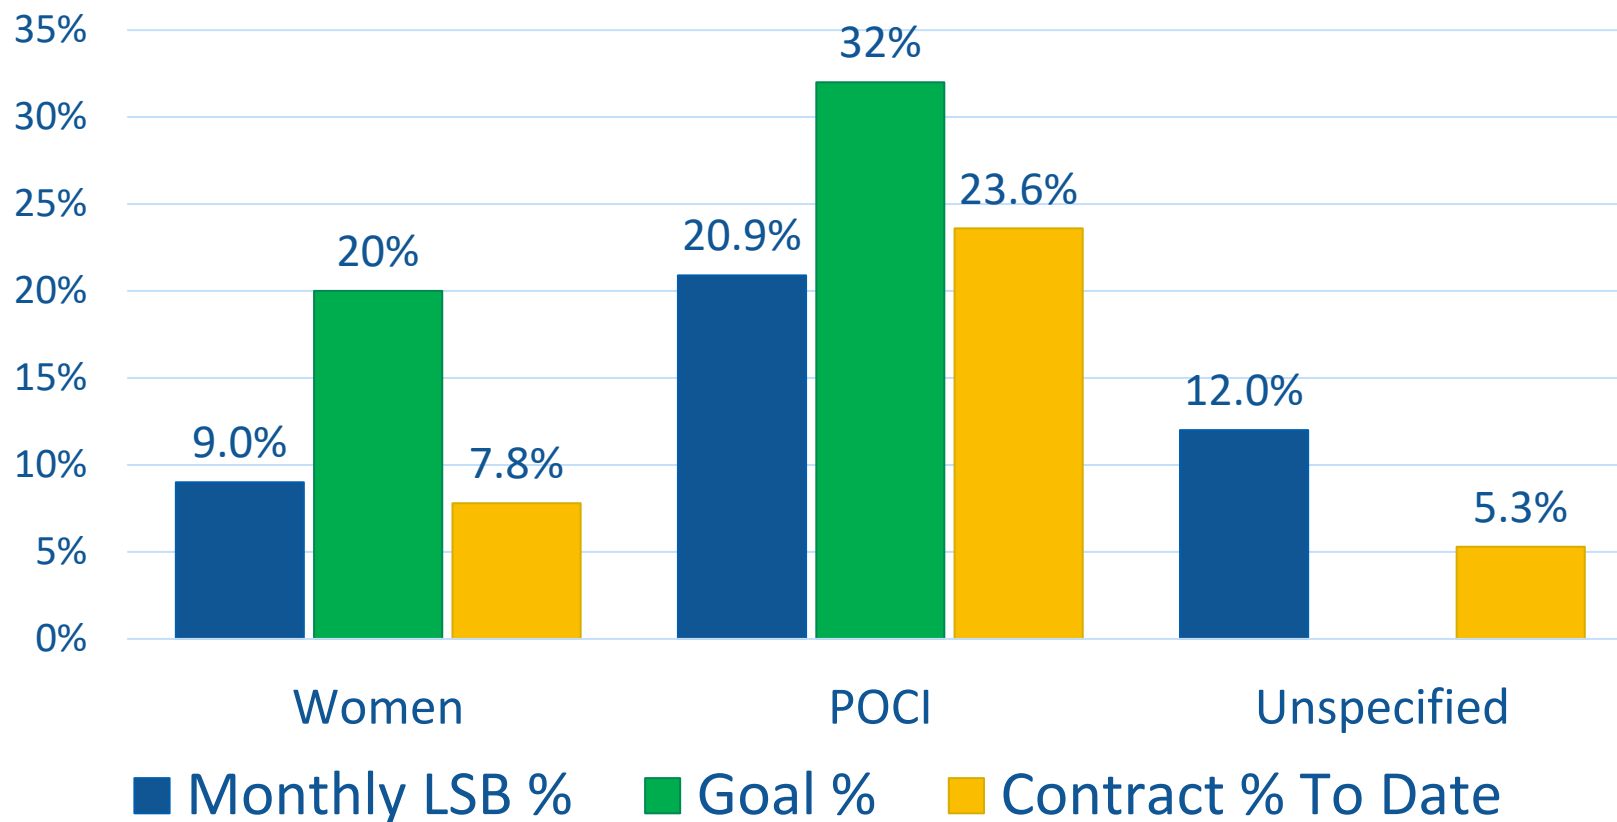

*Based on LCP Tracker Workforce Report for June 2021
People of Color/Indigenous (POCI)

Monthly Franklin O&M Workforce Participation*


- Total Women hours to date: 6,174 hrs
- Cumulative participation: 7.8%

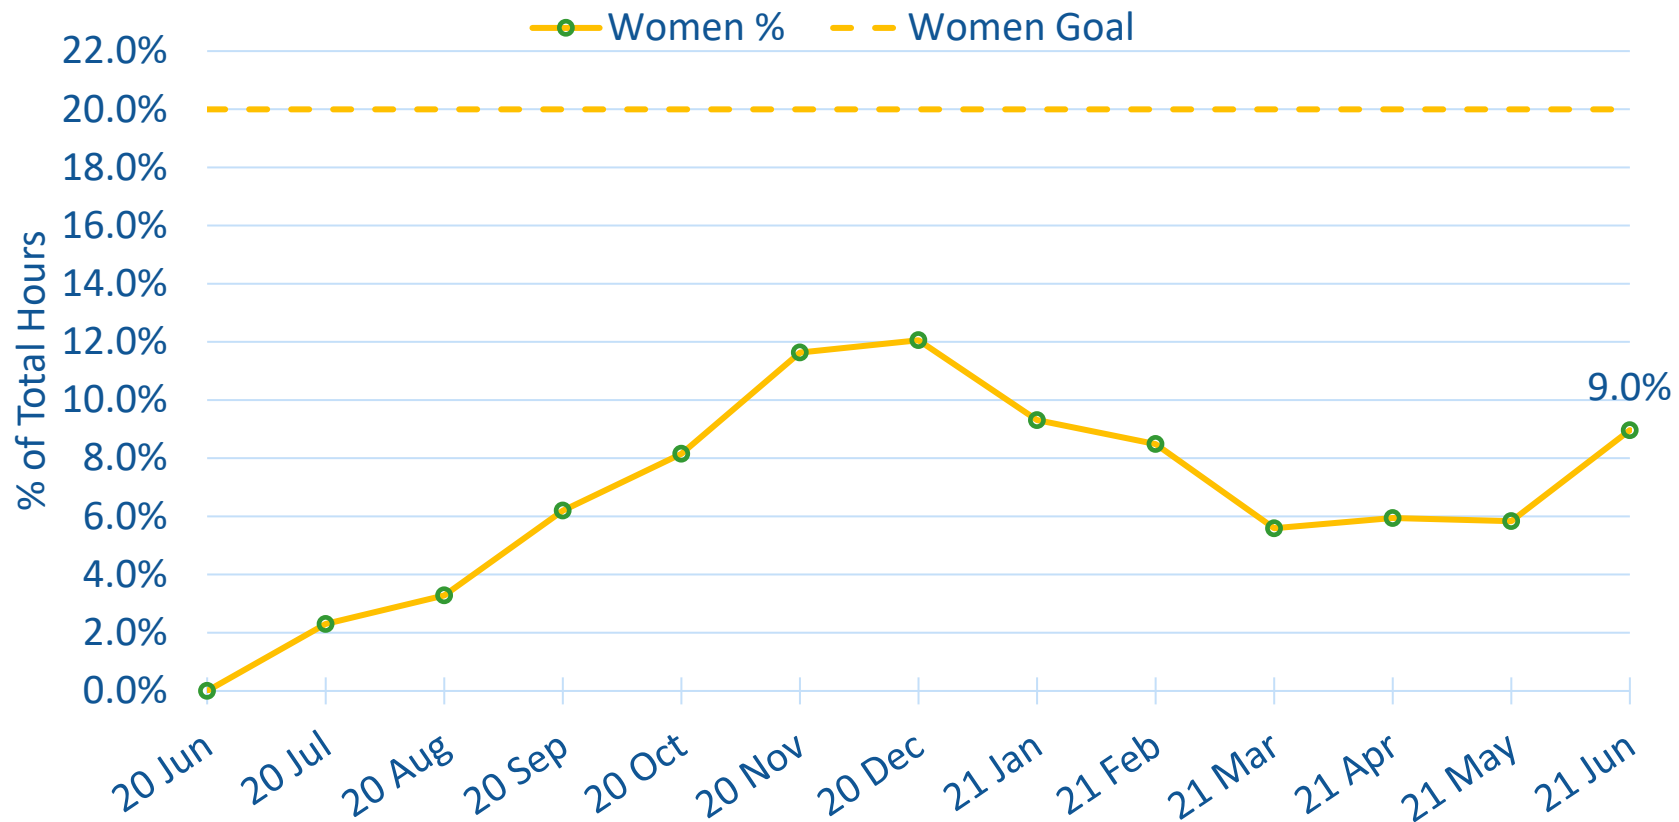

*Workforce data is based on the June 2021 report from LCP Tracker.

Monthly Franklin O&M Workforce Participation*

- Total POCI hours to date: 18,613 hrs
- Cumulative participation: 23.6%

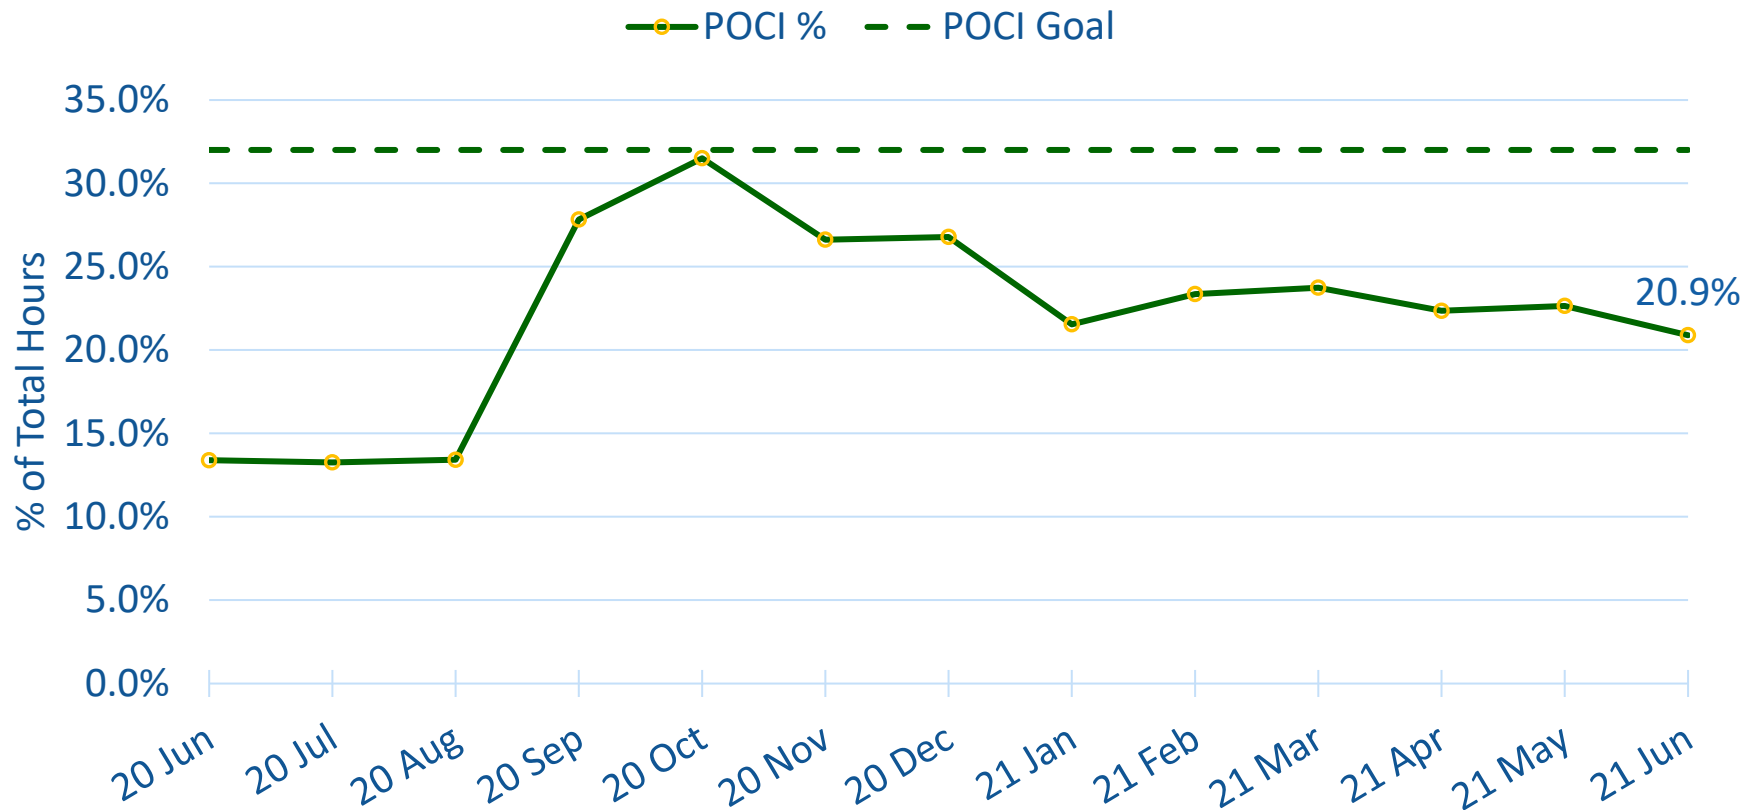

*Workforce data is based on the June 2021 report from LCP Tracker.

Franklin O&M Workforce Disaggregated*

- Total Project Hours: 78,804 hrs
- Total POCI Hours: 18,613 hrs (23.6%)
- Total Women Hours: 6,174 hrs (7.8%)

Ethnic Group	Women	Women %	Men	Men %	Total	Total %
Asian	216	0.3%	2,688	3.4%	2,904	3.7%
Black	2,180	2.8%	3,497	4%	5,677	7.2%
Hispanic	282	0.4%	5,750	7.3%	6,032	7.7%
Multi-racial	0	0.0%	2,157	2.7%	2,157	2.7%
Native American	0	0.0%	1,844	2.3%	1,844	2.3%
Not Specified	0	0.0%	4,176	5.3%	4,176	5.3%
White	3,496	4.4%	52,519	66.6%	56,015	71.1%

*Based on workforce data from LCP Tracker Reports. Women, People of Color and Indigenous People (POCI) participation from 12/1/18 – 6/30/21

DBE & Workforce Committee Discussions

- How MnDOT used small contracts to advance equity
- Lessons learned from MnDOT's Results and Transparency Committee
- How San Diego Association of Government's Bench Program is creating partnerships between large and small firms

Communications & Outreach Update

Sophia Ginis
Manager, Community Outreach

Communications & Outreach Update

- Weekly construction updates:
 - 17,000+ subscribers, 46% open rate
- Twitter: 1,400+ followers
- Construction Information Workgroups
- Property owner meetings
- Corridor tours



Hopkins Raspberry Festival

Stay Updated!

Online:

SWLRT.org

Twitter:

@SouthwestLRT

Flickr:

[flickr.com/photos/metcouncil/albums](https://www.flickr.com/photos/metcouncil/albums)

Facebook:

@MetropolitanCouncil

Instagram:

@southwest_lrt

