

Chanhassen Interceptor Rehabilitation Project

Construction Update July 19, 2021

Issue 10

Please note: The construction timeline is subject to change pending weather conditions and ongoing coordination efforts with various contractors and agencies working in the project area.

Site 1 Activity Update

Site restoration along Wynsong Lane will be completed in September 2021.

Site 2 Upcoming Activity

Work in Site 2 will include repairing the existing sewer liner and maintenance hole (MH) 62. This work has been scheduled to start Monday, July 26, 2021.

Temporary Conveyance System to Start Week of July 26

The contractor will set up the temporary conveyance system the week of July 26th. It will take approximately a week to set-up the construction site.


Lining and Maintenance Hole Repairs to Start Week of August 2

Once the temporary conveyance system is activated, pumps will run continuously to maintain sewer service. While the pumps will be enclosed to mitigate noise, additional noise and nighttime lighting near the pump pit site is expected. The temporary conveyance system will be monitored 24 hours a day. After the temporary conveyance system is activated the cured-in-place-pipe (CIPP) lining will be used to fix the existing pipe. Excavations will be needed at select maintenance holes to insert the lining. Tree removal is likely near MH 63 to excavate the pump pit. Any trees removed will be planted post construction in coordination with the city of Chanhassen.

Along with the sewer lining, maintenance hole (MH) 62 is being repaired. This work will require removal and replacement of a portion of the existing retaining wall located near MH 62 to access and fix it. Tree removal is also a potential in this location. The contractor and Metropolitan Council staff will coordinate with the city on the retaining wall and site restoration. Lake Lucy Road will remain open during construction but there will traffic control in place to get around the pumps and the maintenance hole/retaining wall work.

Work to fix the sewer pipe and MH 62 is expected to take approximately one week. Dry weather is needed to complete this work, so there is the potential for construction to be extended. Once the work is completed, it will take another week to take down the construction site.

Site 2

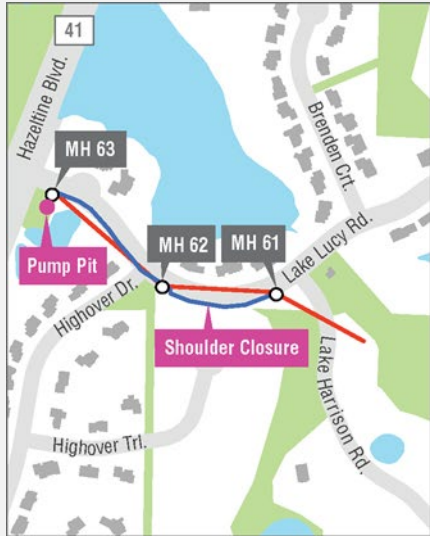

Site 1



Key to Symbols

- Maintenance Hole (MH)
- Building
- Temporary Conveyance Pipe
- Sewer Pipe

Stay Informed

If you have any questions or concerns about this project, please contact us.

Phone: 952.491.6499

Email: info@chaninterceptorrehab.com

Web: www.metrocouncil.org/sewerconstruction/chaninterceptorrehab
