



July 21, 2022











### **Today's Topics**


- Project Update
- DBE Achievement Reporting
- Workforce Participation Reporting
- Committee Focus Discussion
- Public Invitation



### **Project Office Update**


### **Civil Construction Work**

### **SouthWest Station, Eden Prairie**

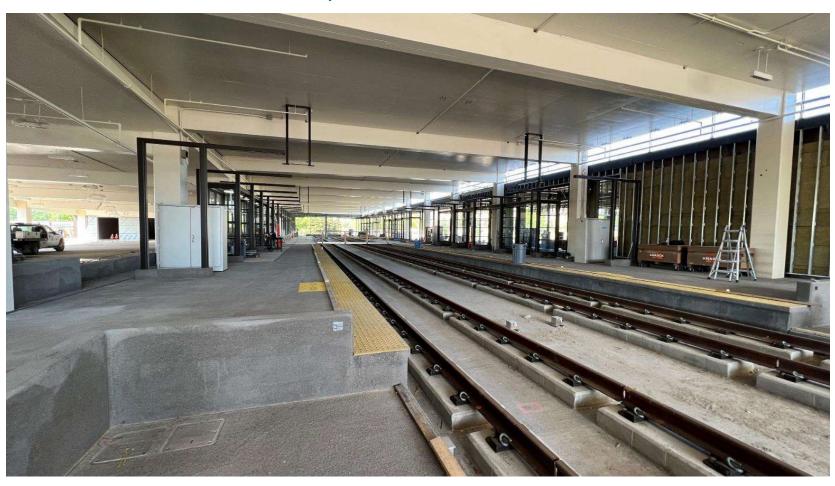



### Track Installation at SouthWest Station, Eden Prairie

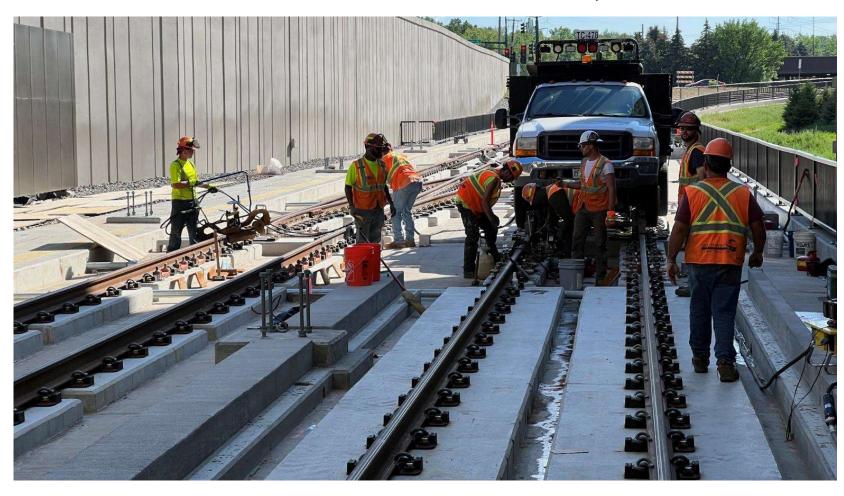



### West 70<sup>th</sup> Street LRT Grade Crossing Panels, Eden Prairie





### Highway 212/Shady Oak Road LRT Bridge, Eden Prairie





### **Opus Station, Minnetonka**






### Feltl Road Bridge, Minnetonka





### **Excelsior Boulevard LRT Bridge, Hopkins**

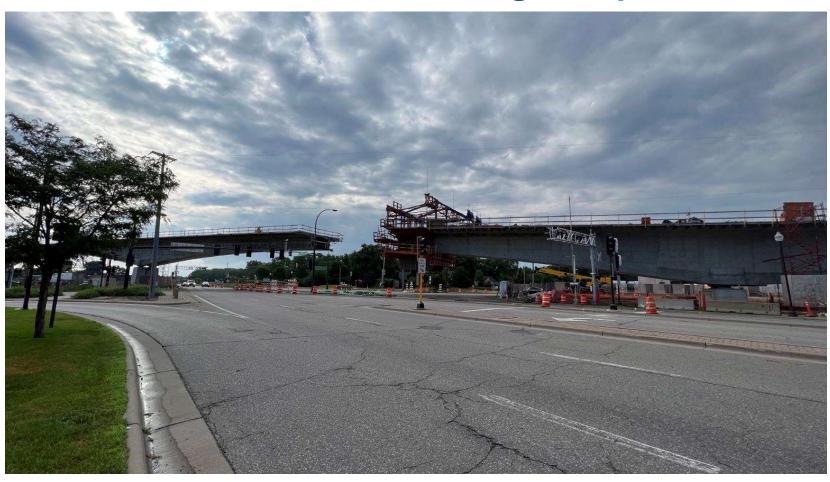




#### Pile Driving Near Louisiana Avenue LRT Bridge, St. Louis Park






### **Southerly Connector, St. Louis Park**

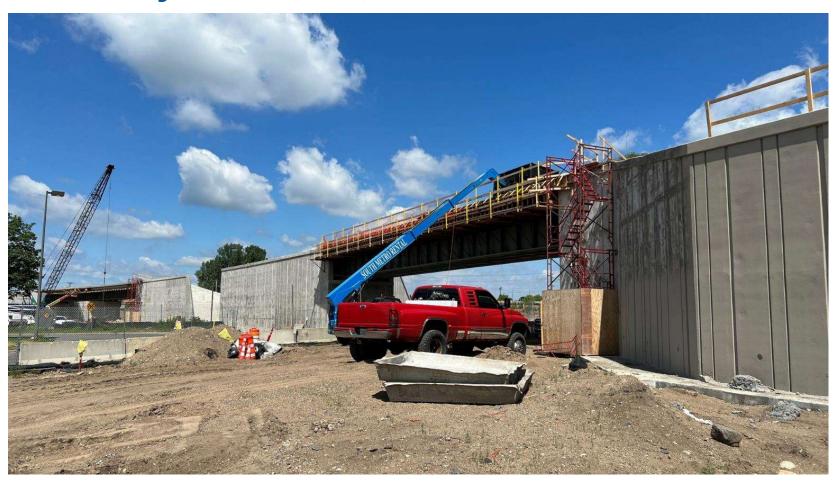



### **Secant Piles at Kenilworth LRT Tunnel, Minneapolis**





### **Kenilworth LRT Tunnel, Minneapolis**





### Cedar Lake Channel LRT Bridge, Minneapolis





### Glenwood Avenue LRT Bridge, Minneapolis





### **Systems Construction Work**

# TPSS SW308 DC Switchgear House Delivered to the Local Systems Storage Facility



# TPSS SW308 AC Switchgear House Delivered to the Local Systems Storage Facility



### **TPSS 15B Short Circuit Testing**



# Wooddale Station Signal House Foundation Backfilling and Completion



## **DBE Achievement Report**

### **DBE Achievement as of May 31, 2022**

Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	DBE Date %	As of Date
LMJV 16% Goal	Civil	\$1,010,365,292	\$740,932,753	\$151,350,454	20.4%	5/31/22
APJV 12% Goal	Systems	\$206,548,690	\$80,925,536	\$14,293,402	17.7%	5/31/22
LS Black 15% Goal	Franklin O&M Exp.	\$41,009,266	\$40,982,781	\$7,786,429	19.0%	5/31/22
17% Goal	Closed Contracts	\$404,992	\$404,992	\$74,610	18.4%	
		Cantuant		¢ DDE	0/ [	)DE
		Contract Amount	Billed to Date	\$ DBE to Date	% DBE to Date	
15% Goal		\$1,258,328,240	\$863,246,062	\$173,504,895	20.1%	

### Lunda/CS McCrossan Joint Venture: Civil DBE Activities Update

### LMJV DBE Updates: Removal of Contract

#### Dionne Construction

- Scope of work: Landscape (plant/maintain trees)
- ≥ 2<sup>nd</sup> tier subcontractor for Hoffman & McNamara
- Cancelled due to multiple items main being no workers compensation insurance
- Hoffman & McNamara exceeded all good faith effort expectations in working with/mentoring Dionne.
- ➤ JL Theis (DBE firm) will now be working with Hoffman & McNamara

### LMJV DBE Updates: Upcoming Activities

### DBE/Subcontractor Education Opportunities

- August Safety & Security
- September Quality
- October Finance
- November Networking

### **LMJV Update on Change Orders**

- Owner Change Orders approved thru 06/15: \$213,352,838
  - DBE Job To Date Participation: 20.19%

<sup>\*</sup>Does not take into account LMJV directed change orders with Subcontractors

# Aldridge Parsons Joint Venture: Systems DBE Activities Update

### **Anticipated DBEs: One Month Look Ahead**

- Maintenance of TPSS in storage Golden Valley Warehouse
- Gunnar Electric
- Public Solutions


### **APJV Update On Change Orders**

- Owner change orders approved thru 6/1/22: \$12,576,433
- DBE change order participation:
- Gunnar Electric: \$2,130,738.00
- Generation Cable: \$413,311 (\$247,986: 60% material only)
- Carlo Lachmansingh Sales \$279,390 (\$167,634: 60% material only)
- DBE change order participation: 20.2%
- DBE job to date participation: 17.7%
- Negotiating CO With Elite FO \$97.9K
- Negotiating CO With Gunnar \$850K Communication Work

## **Workforce Participation Report**


### **Civil Workforce Participation Percentage\***

- May 2022: 78,201 hrs
- Civil Construction Total: 2,090,807 hrs

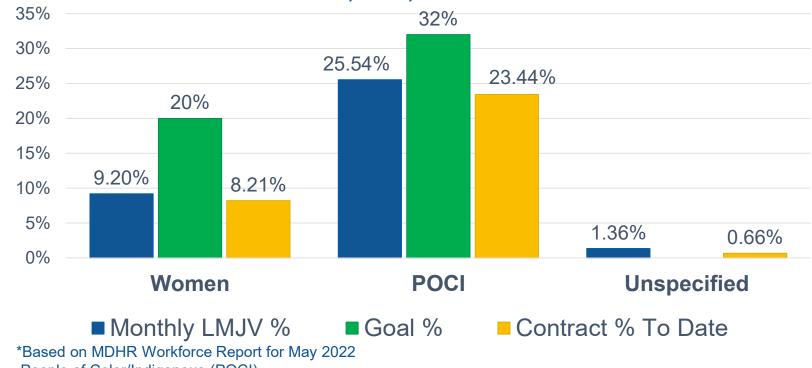

### **Civil Workforce Participation\***

May 2022: 78,201 hrs

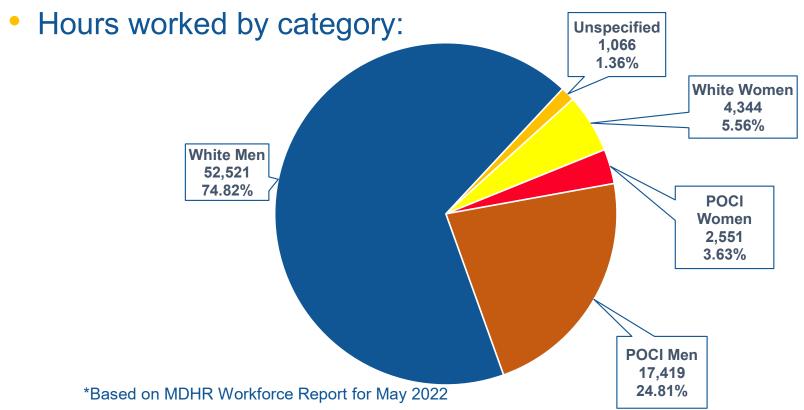

### **Civil Workforce Trucking Participation\***

Trucking participation on Project being counted:

• MBE: 27,560 hours


• ZTS: 4,482 hours

Rock-On Trucks: 1,808 hours

\*Based on MDHR Workforce Reports: Project Start through May 2022


### Franklin O&M Workforce Participation Percentage\*

- May 2022: 183 hrs
- Franklin O&M Construction Total: 112,682 hrs

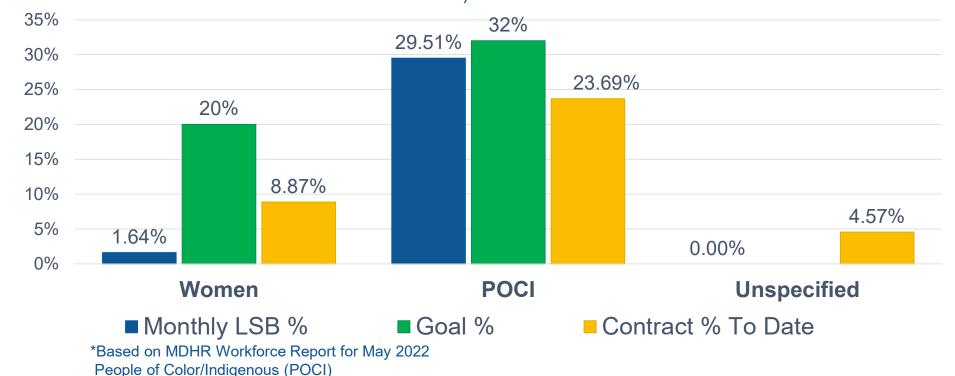

#### Franklin O&M Workforce Participation\*


• May 2022: 183 hrs

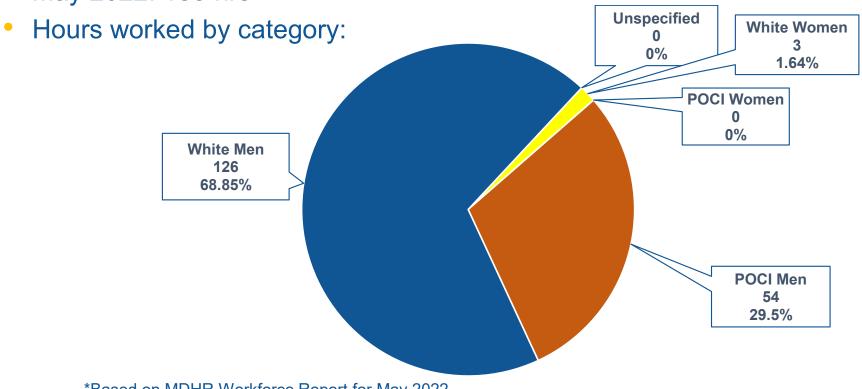

\*Based on MDHR Workforce Report for May 2022

### Systems Workforce Participation Percentage\*


- May 2022: 243 hrs
- Systems Construction Total: 3,660 hrs

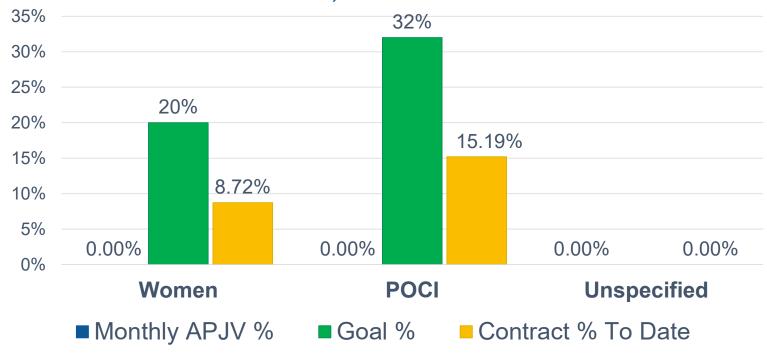

\*Based on MDHR Workforce Report for May 2022 People of Color/Indigenous People (POCI)

#### **Systems Workforce Participation\***

April 2022: 243 hrs

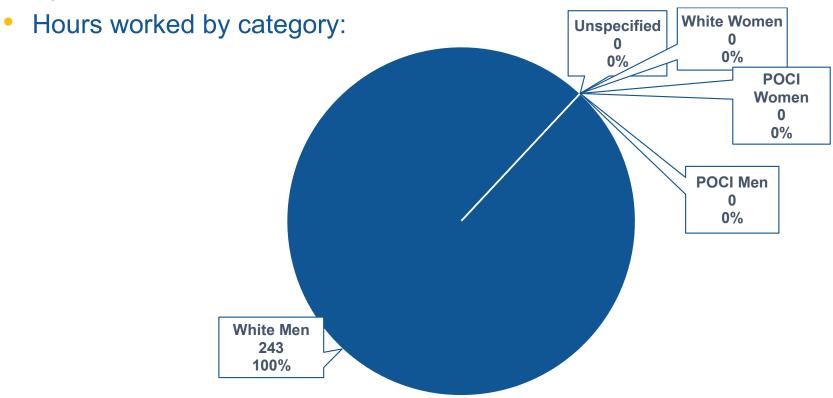


\*Based on MDHR Workforce Report for May 2022

## Lunda/CS McCrossan Joint Venture: Civil Workforce Activities Update


# POCI WORKFORCE PARTICIPATION COMPARISON

SWLRT Civil Project - Metro Area MnDOT Projects

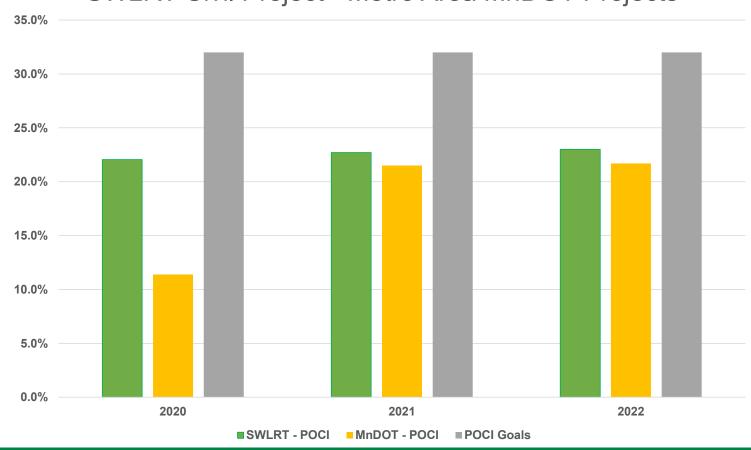

# WOMEN WORKFORCE PARTICIPATION COMPARISON

SWLRT Civil Project - Metro Area MnDOT Projects

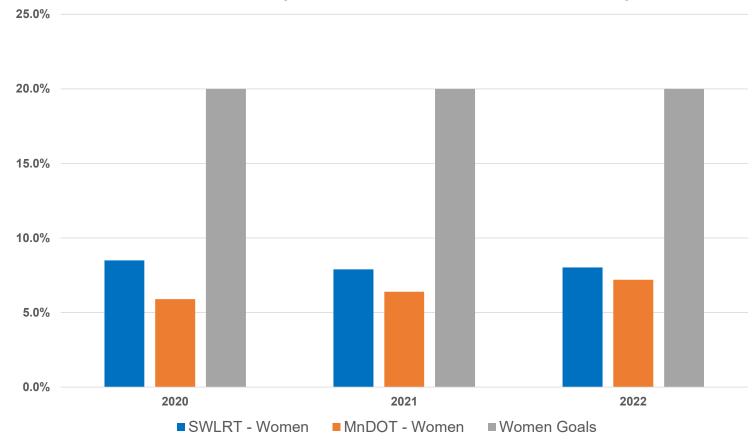

#### **LMJV Workforce Highlights:**

- Continue to Assisted LMJV & Subcontractors with their onboarding of the new BSC apprentices
- Continue to Assisted multiple subcontractors with their EEO/Respectful Workplace practices.
- Meetings with LMJV workforce leads updates on new apprentices, upcoming workforce needs
- EEO/Respectful workplace education training for subcontractors – Followed July's Subcontractor Workforce Review meeting (July 13<sup>th</sup>)
- Meetings with BSC representative regarding review of previous year and discussions re upcoming year

Continued....

#### **LMJV Workforce Highlights:**

#### Continued...

- Meeting with union representative regarding the partnership of contractors/unions on project workforce outreach participation
- Meeting with newly appointed BSC Executive Director, Rick Martagon
- Attended the Carpenters Pile Driving Program Graduation
- Participated in the 2022 Carpenters Hiring Event
- Begin work on SWLRT Civil CBO Connection Resource Guide

### LMJV Workforce Highlights: BSC Apprentice Mentoring





## LMJV Workforce Highlights: Regular Site Visits





### LMJV Workforce Highlights: Carpenters Careers Event



#### **LMJV Workforce – Upcoming Highlights:**



A group from the SWLRT Civil Team has Sponsored a bay at this great event! Thanks LMJV, Egan & PWS!!

#### New Hires/Rehires/Transfers – June 2022

Transfers

White Male: 5

White Female: 0

POCI Male: 6

POCI Female: 0

Lay-Offs

White Male: 2

White Female: 0

POCI Male: 2

POCI Female: 1

**Rehires** (Returning from furlough)

White Male: 0

White Female: 0

POCI Male: 0

POCI Female: 0

**Voluntary Leaves** 

White Male: 1

White Female:

**POCI Male:** 

**POCI Female:** 

New Hires

White Male: 2

White Female: 0

POCI Male: 2

POCI Female: 1

## Aldridge Parsons Joint Venture: Systems Workforce Activities Update

#### **Systems Workforce Activities Update**

- Plan to meet the workforce goal:
  - APJV limited scopes available for craft labor through 2022. Work at the TPSS Stations has been put on hold for much of 2022. Bulk of craft labor will begin until Spring of 2023.
  - On Wednesday, October 13, 2022 APJV will provide a day of hands on training with Summit Academy for the fall cohort. This training will include hands activities with Aldridge' Traveling Utility Training Trailer and Incident and Injury Free (IIF) Safety Training. Subcontractors and Unions will be invited to meet the Cohort.

## **Committee Focus Discussion**

#### **Public Invitation**

- Each speaker is limited to a three-minute presentation
- Pre-register as you sign in for attendance at the start of the meeting



#### Closing

- Next Meeting date: August 18, 2022, and will be virtual
  - Agenda topics
  - Actions items for the next meeting
- Adjourn

#### **MORE INFORMATION**

Website: GreenLineExt.org

Email: <a href="mailto:swlrt@metrotransit.org">swlrt@metrotransit.org</a>

Twitter: @GreenLineExtMN

Instagram: @GreenLineExtMN
