

Central Corridor Light Rail Transit Cash Flow Financing Plan 4Q13 Status Report

March 26, 2014



Today's Topics

- Reporting Requirements
- All Funding Sources
- FFGA Funding Status
- Projected Cash Balances—w/o GANs
- Grant Anticipation Notes (GANs) Issued
- GANS to be Issued
- Projected Cash Balances—w/GANs
- GANs Interest Expenses
- Interest on Internal Borrowing



CCLRT Cash Flow Reporting Requirements (See Mgmt. Comm. 2011-124)

- Status of G.O. GANs issuances
- Internal borrowing activity (\$60MM max/occurrence)
- Internally funded interest expense
- Report results & expectations



All Funding Sources

<u>Amount</u>	Pledged	Rec'd*	Source
\$478.5	50.0%	56.6%	FTA
283.9	29.7%	100.0%	CTIB
94.2	9.8%	100.0%	State MN
66.4	6.9%	79.4%	RCRRA
28.2	2.9%	80.2%	HCRRA
5.2	0.5%	100.0%	St. Paul
0.5	0.1%	100.0%	Collaborative
\$956.9	100.0%	76.3%	Totals

^{*}Cash Receipts Through Dec 31, 2013.



FFGA Revised Schedule of Funding (\$ Millions)

Federal Fiscal

Year*	Amount	Approved	Rec'd
2007-11	\$39.68	\$39.68	100.0%
2011	45.00	45.00	100.0%
2012	93.14	93.14	100.0%
2013	93.04	93.04	100.0%
2014	98.44	Pending	
2015	109.15	Pending	
Total	\$478.45		

^{*}Receipt assumed to be January following conclusion of Federal fiscal year.



Cash Balance, Sans GANs





GANs Issued: \$90 MM, 2011C

 Proceeds received September 28, 2011, at a rate of 0.39%.

Principal Due (\$MM):

```
3-1-12 $25.0 Paid
```



GANs Issued: \$100 MM, 2012**G**

 Proceeds received November 8, 2012, at a rate of 0.67%.

• Principal Due (\$MM):

```
3-1-14 $15.0 Paid
```



GANs Issued: \$100.8 MM, 2014A

 Proceeds received February 6, at a rate of 0.30%.


• Principal Due (\$MM):

3-1-15 \$52.1

3-1-16 \$48.7



Cash Balance, With GANs

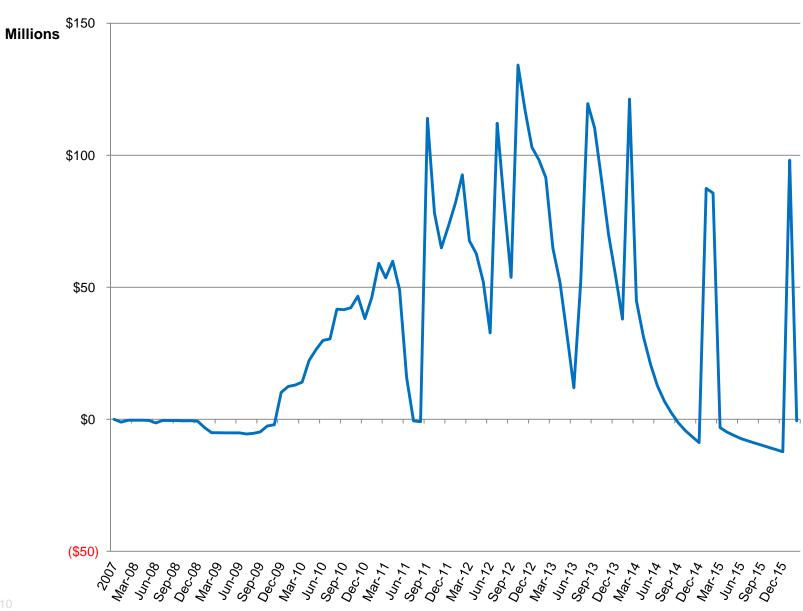

GANs Interest & Issuance Expenses (in Millions)

	FFGA	Thru 12-31-13
GANs Interest & Issuance Exp.	\$8.1	\$1.4*
Less: GANs Interest Revenue	0.0	\$ <u><2.6></u>
Net GANs Expense	\$8.1	\$ <u><1.2></u>

^{*}Reflects amortized premium



Interest Expense on Internal Borrowing, Thru 4Q13

Pre-GANs (<9-28-11) \$0.5mm

Cum. During all GANs \$0.0mm*

Total-to-Date

\$0.5mm



^{*}Expect \$500,000 by Jan. 2016, for total internal interest cost of \$1mm.



Easing congestion

Central Corridor Light Rail Transit



Strengthening our communities

Questions?
