



Disadvantaged Business Enterprise and Workforce Advisory Committee

August 18, 2022



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

Today's Topics


- Project Update
- DBE Achievement Reporting
- Workforce Participation Reporting
- Committee Open Discussion
- Announcements
- Public Invitation




Project Office Update

Civil Construction Work

Wooddale Avenue Station, St. Louis Park

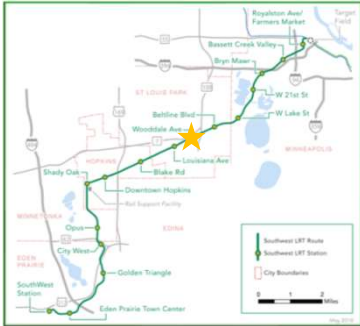

Beltline Boulevard Station, St. Louis Park

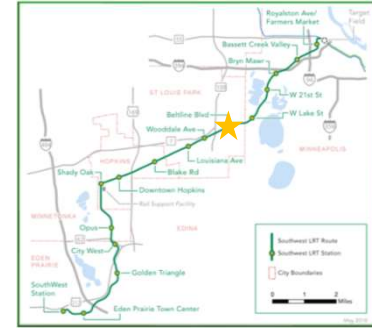

Secant Wall Drilled Shafts, Minneapolis



Kenilworth LRT Tunnel, Minneapolis



Temporary Trail Over Kenilworth LRT Tunnel, Minneapolis



Cedar Lake Channel Pedestrian Bridge, Minneapolis



Corridor Protection Barrier and Luce Line Pedestrian Bridge, Minneapolis



Glenwood Avenue LRT Bridge, Minneapolis



Glenwood Avenue LRT Bridge, Minneapolis



Royalston Avenue/Farmers Market Station, Minneapolis



Systems Contract Work

Opus Station Signal House Delivered to Storage Facility



Eden Prairie Town Center Station, Opus Station, and Opus Interlocking Signal Houses in Storage



DBE Achievement Report

DBE Achievement as of June 30, 2022

Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	DBE Date %	As of Date
LMJV 16% Goal	Civil	\$1,012,867,177	\$768,647,692	\$155,260,864	20.2%	6/30/22
APJV 12% Goal	Systems	\$206,548,690	\$83,333,535	\$14,916,143	17.9%	6/30/22
LS Black 15% Goal	Franklin O&M Exp.	\$41,009,266	\$40,982,781	\$7,786,429	19.0%	6/30/22
17% Goal	Closed Contracts	\$404,992	\$404,992	\$74,610	18.4%	
		Contract Amount	Billed to Date	\$ DBE to Date	% DBE to Date	
15% Goal		\$1,260,830,125	\$893,369,000	\$178,038,046	19.9%	

Lunda/CS McCrossan Joint Venture: Civil DBE Activities Update

LMJV DBE Updates:

■ DBE/Subcontractor Education Opportunities

- August – Safety & Security

UPCOMING

- September – Quality followed by CBO Networking
- October – Finance
- November – Close Outs
- December – Networking Event

LMJV Update on Change Orders

- Owner Change Orders approved thru 07/15: \$216,352,838
 - DBE Job To Date Participation: 20.31%

**Does not take into account LMJV directed change orders with Subcontractors*

Aldridge Parsons Joint Venture: Systems DBE Activities Update

Anticipated DBEs: One Month Look Ahead

- Bryn Mawr Station – Communications Work Gunnar Electric
- West Lake Street Station - Communications Work Gunnar Electric

- Gunnar Electric
- Public Solutions


APJV Update On Change Orders

- Owner change orders approved thru 7/1/22: \$12,256,997
- DBE change order participation:
 - Gunnar Electric: \$2,990,693
 - Generation Cable: \$413,311 (\$247,986: 60% material only)
 - Carlo Lachmansingh Sales \$279,390 (\$167,634: 60% material only)
 - Fully Executed CO With Elite Fiber Optic Cable: \$97,944
 - Fully Executed CO With Gunnar: \$859,955 Communication Work
- DBE change order participation: 35.6%
- DBE job to date participation: 17.9%

Workforce Participation Report

Civil Workforce Participation Percentage*


- June 2022: 72,610 hrs
- Civil Construction Total: 2,164,745 hrs

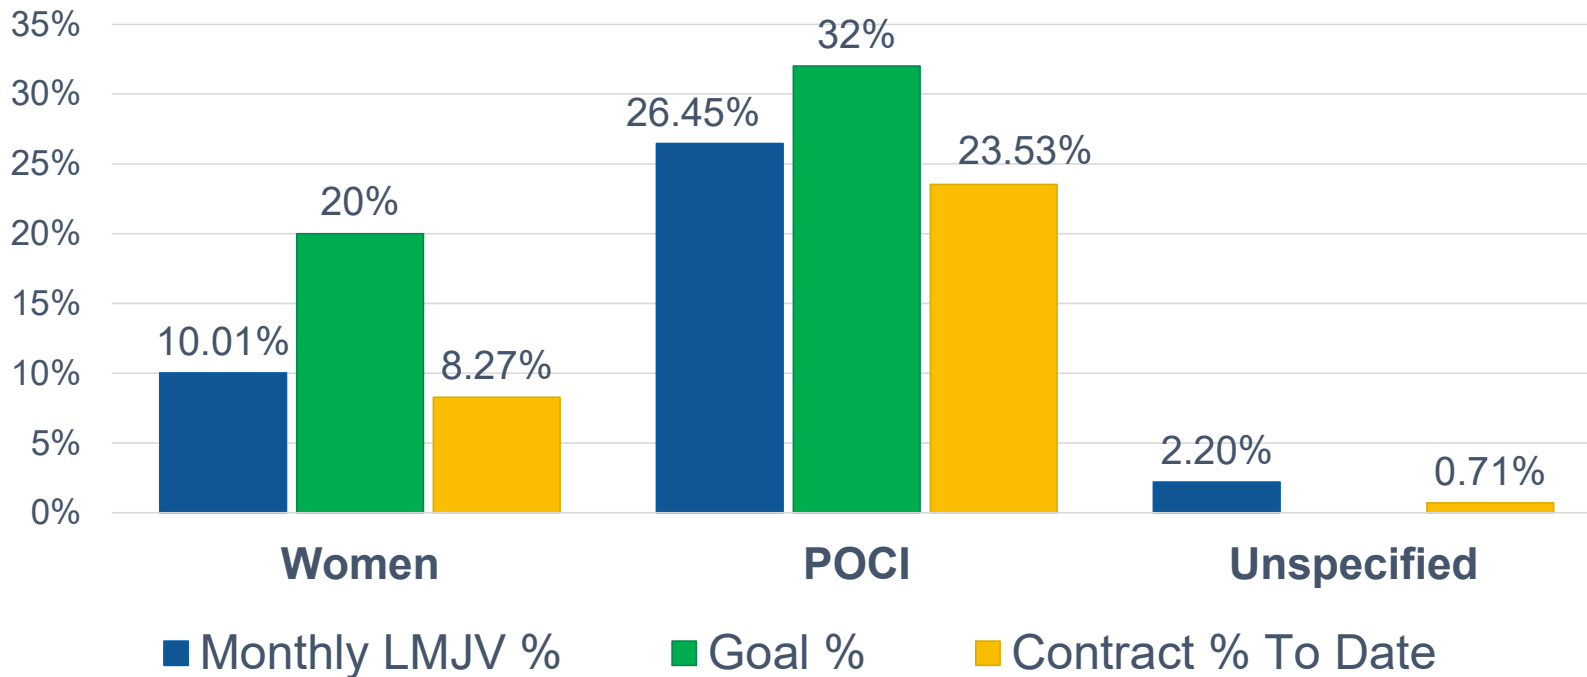

*Based on MDHR Workforce Report for June 2022
People of Color/Indigenous (POCI)

Civil Workforce Participation*

- June 2022: 72,610 hrs
- Hours worked by category:

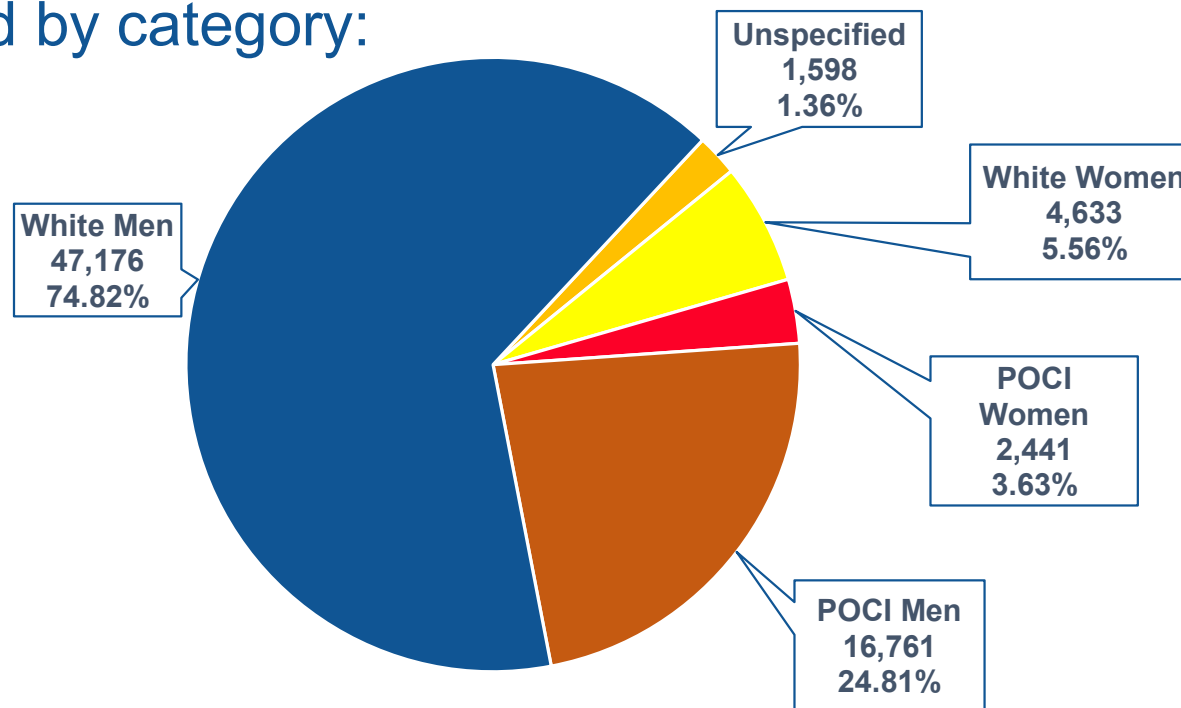

*Based on MDHR Workforce Report for June 2022

Civil Workforce Trucking Participation*


Trucking participation on Project being counted:

- MBE: 27,916 hours
- ZTS: 4,482 hours
- Rock-On Trucks: 2,016 hours

*Based on MDHR Workforce Reports: Project Start through June 2022

Franklin O&M Workforce Participation Percentage*


- June 2022: 97 hrs
- Franklin O&M Construction Total: 112,779 hrs

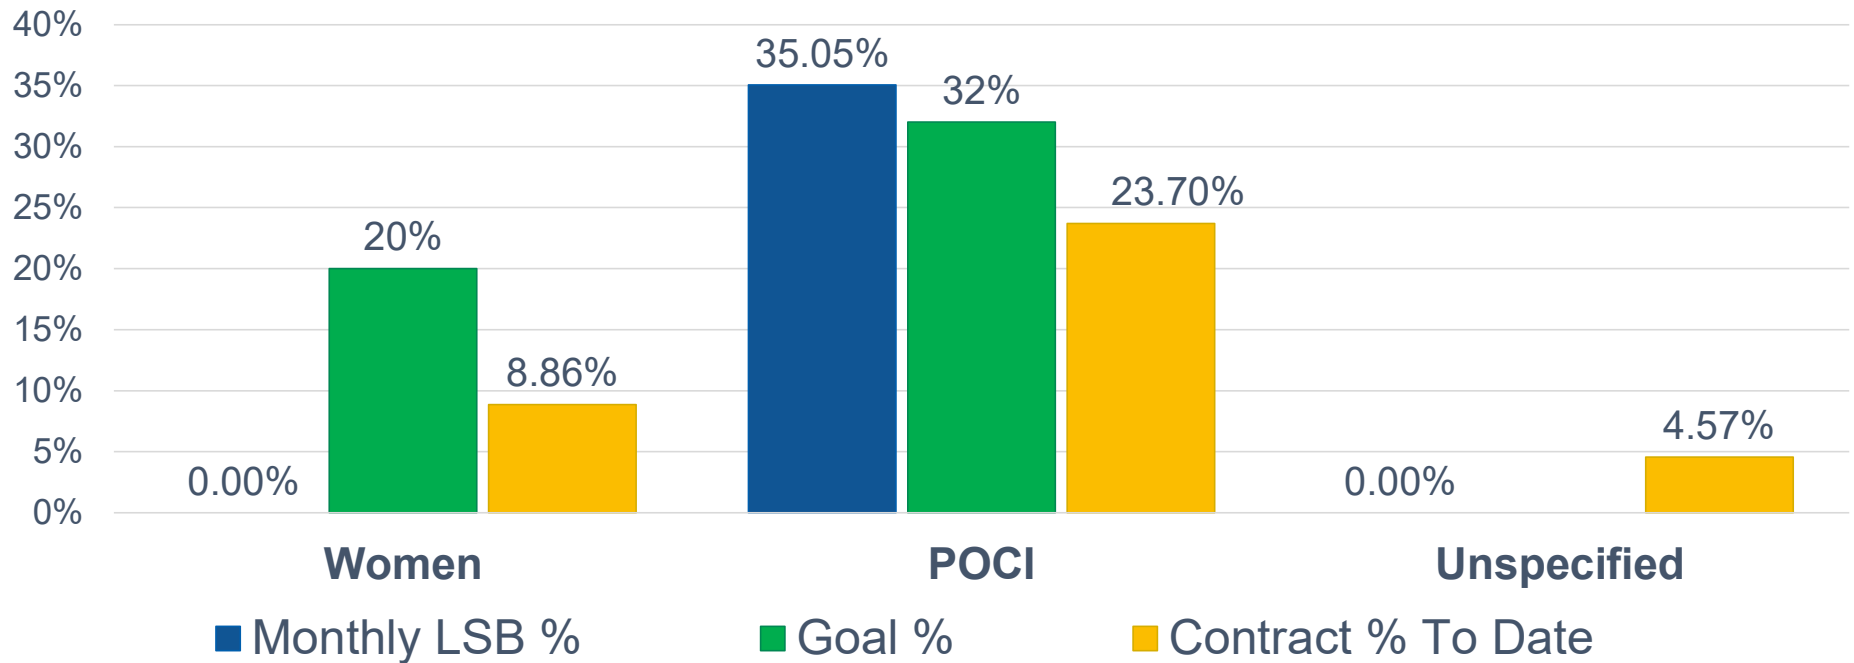

*Based on MDHR Workforce Report for June 2022
People of Color/Indigenous (POCI)

Franklin O&M Workforce Participation*


- June 2022: 97 hrs
- Hours worked by category:

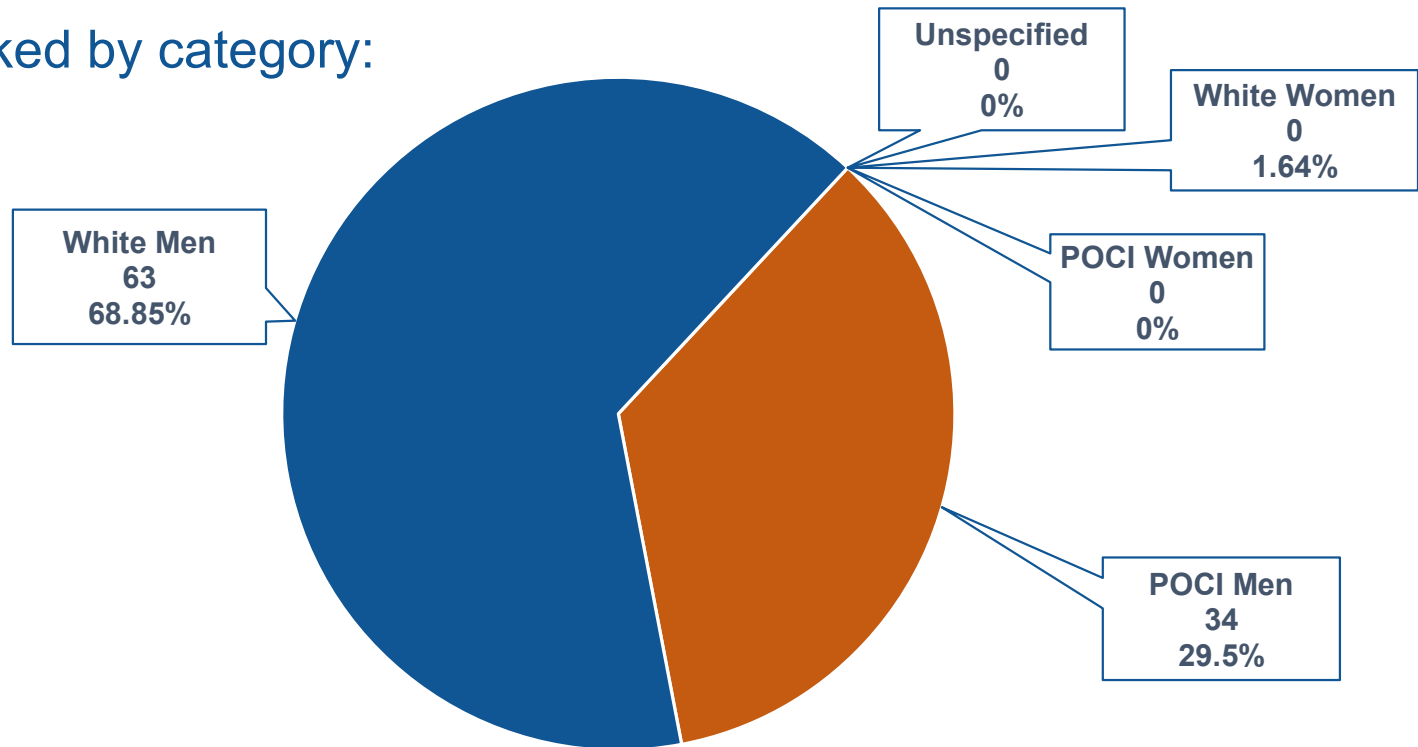

*Based on MDHR Workforce Report for June 2022

Systems Workforce Participation Percentage*


- June 2022: 294 hrs
- Systems Construction Total: 3,954 hrs

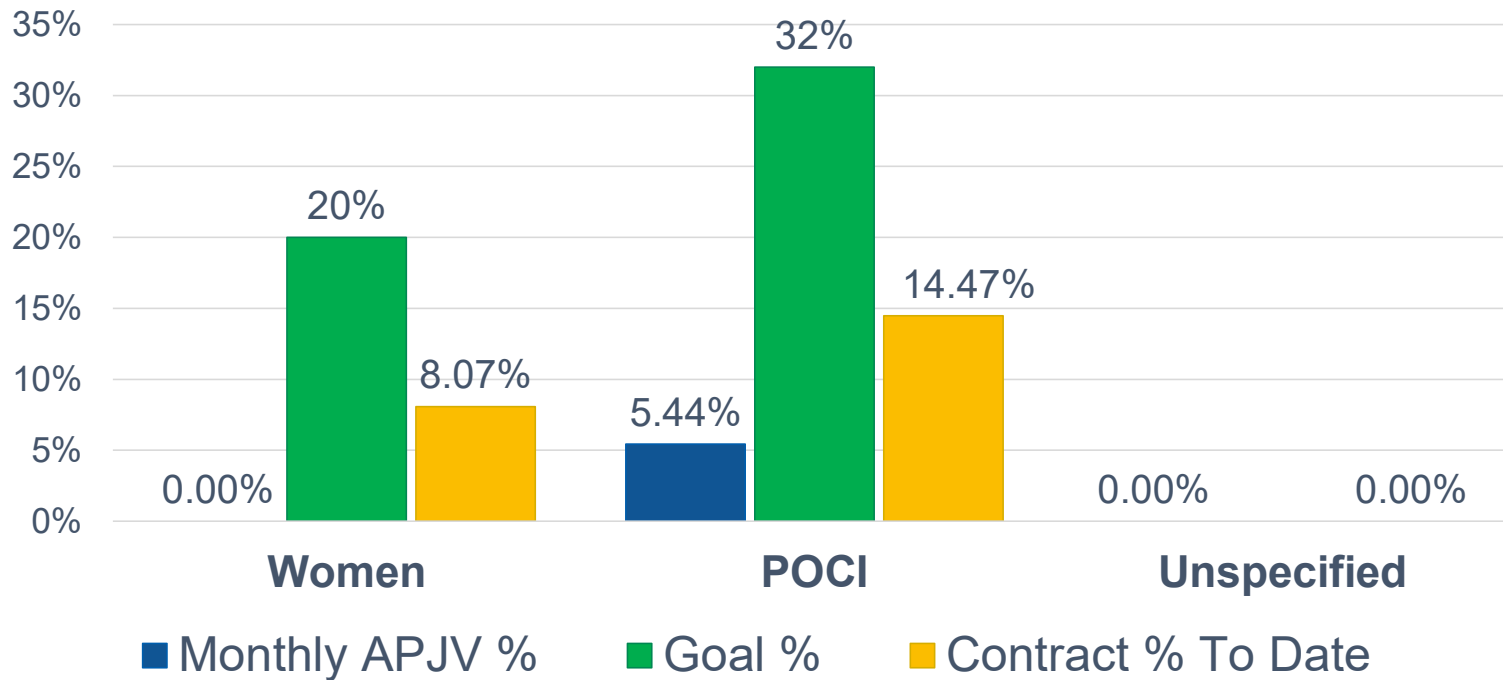

*Based on MDHR Workforce Report for June 2022
People of Color/Indigenous People (POCI)

Systems Workforce Participation*

- June 2022: 294 hrs
- Hours worked by category:

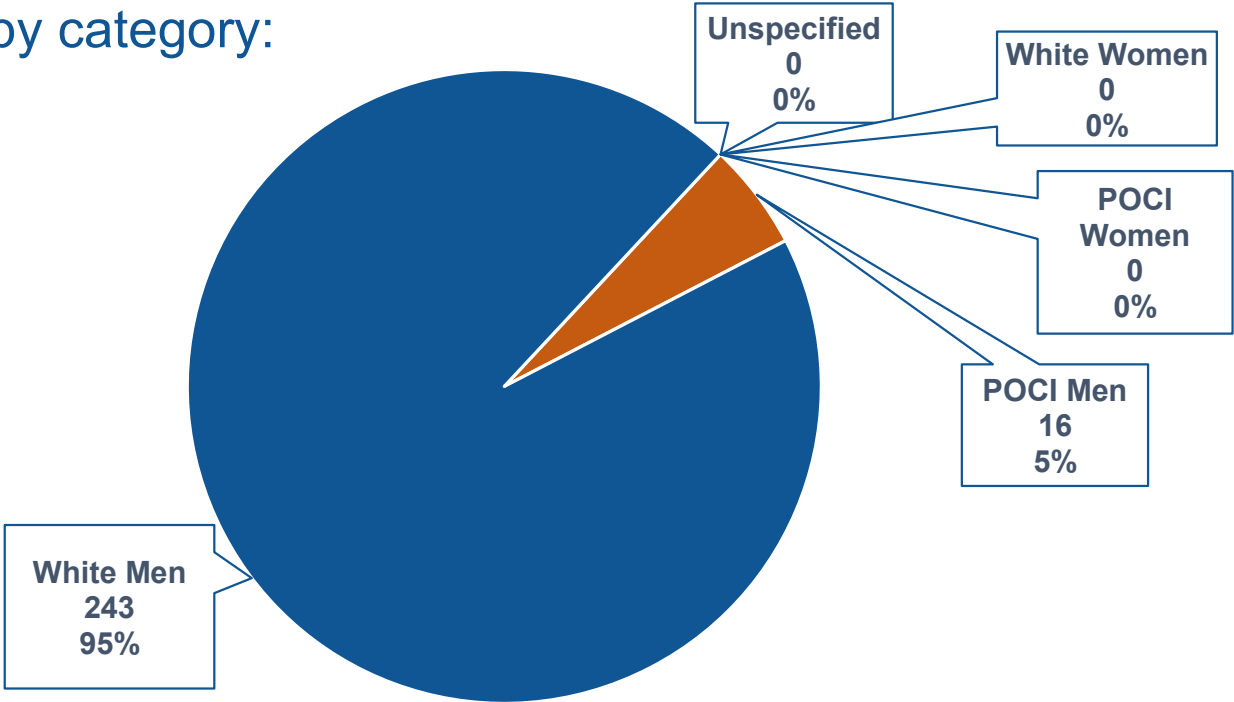

*Based on MDHR Workforce Report for June 2022

Lunda/CS McCrossan Joint Venture: Civil Workforce Activities Update


LMJV Workforce Highlights:

- Continue to Assisted LMJV & Subcontractors with their on-boarding of the new BSC apprentices
- Continue to Assisted multiple subcontractors with their EEO/Respectful Workplace practices.
- Meetings with LMJV workforce leads – updates on new apprentices, upcoming workforce needs, & mentorship program
- EEO/Respectful workplace education continuing for LMJV team – 1st staff meeting of each month
- Job Site Visit @ Blake - LMJV crews along with Egan & North Country Concrete (upcoming slide)

LMJV Workforce Highlights:

- Attended Construct Tomorrow's fundraising event (upcoming slide)
- Look ahead at major industry calendar & SWLRT Civil's involvement (upcoming slide)
- Planning stages of SWLRT lead trades awareness event Schedule reoccurring meetings with union representative regarding the partnership of contractors/unions on project workforce outreach participation
- Schedule in person Meeting with newly appointed BSC Executive Director, Rick Martagon
- Schedule review meetings with CBOs

LMJV Workforce – Jobsite Visit - Blake

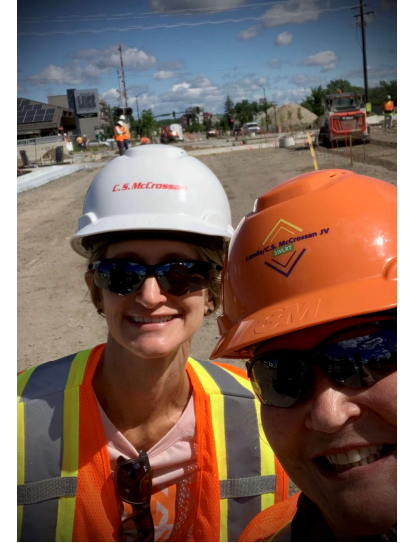

LMJV Workforce – Construct Tomorrow Fundraiser



LMJV, Egan & PWS sponsored our Civil Teams Bay for the fundraiser



LMJV Workforce – Upcoming Industry Involvement

MINNESOTA CONSTRUCTION INDUSTRY

- **AUGUST** NAWIC National Conference
- **OCTOBER** Construction Inclusion Week
- **NOVEMBER** National Apprenticeship Week
- **JANUARY** MN Construction Summit
- **MARCH** Women in Construction Week

SWLRT CIVIL PROJECT

- **SEPTEMBER** Contractor/CBO Networking Event
- **FEBRUARY** TBD
- **APRIL** Trades Awareness Event

New Hires/Rehires/Transfers – July 2022

- **Transfers**

White Male: 3
White Female: 0
POCI Male: 6
POCI Female: 0

- **Rehires** (Returning from furlough)

White Male: 0
White Female: 0
POCI Male: 0
POCI Female: 0

- **New Hires**

White Male: 0
White Female: 0
POCI Male: 2
POCI Female: 0

- **Lay-Offs**

White Male: 4
White Female: 0
POCI Male: 0
POCI Female: 0

- **Voluntary Leaves**

White Male: 2
White Female: 0
POCI Male: 0
POCI Female: 0

Aldridge Parsons Joint Venture: Systems Workforce Activities Update

Systems Workforce Activities Update

- Plan to meet the workforce goal:
 - APJV limited scopes available for craft labor through 2022. Work at the TPSS Stations has been put on hold for much of 2022. Bulk of craft labor will begin until Spring of 2023.
 - APJV will participate in Mock Interview at Summit Academy on Friday, August 26, 2022.
 - On Wednesday, October 13, 2022 APJV will provide a day of hands on training with Summit Academy for the fall cohort. This training will include hands activities with Aldridge' Traveling Utility Training Trailer and Incident and Injury Free (IIF) Safety Training. Subcontractors and Unions will be invited to meet the Cohort.

Committee Open Discussion

Announcements

Public Invitation

- Each speaker is limited to a three-minute presentation
- Pre-register as you sign in for attendance at the start of the meeting



Closing

- Next Meeting date: September 15, 2022

In-Person at Hopkins:

Green Line EXTENSION Civil Field Office

LMJV Conference Room (2nd floor)

11400 K-Tel Drive

Hopkins, MN 55343

- Adjourn

MORE INFORMATION

Website: GreenLineExt.org

Email: swlrt@metrotransit.org

Twitter: [@GreenLineExtMN](https://twitter.com/GreenLineExtMN)

Instagram: [@GreenLineExtMN](https://www.instagram.com/GreenLineExtMN)
