

# Disadvantaged Business Enterprise and Workforce Advisory Committee

November 17<sup>th</sup> , 2022



# Today's Topics


- Project Update
- DBE Achievement Reporting
- Workforce Participation Reporting
- Survey Results
- Committee Discussion
- Announcements
- Public Invitation




# Project Office Update

# Civil Contract Work


# SouthWest Station, Eden Prairie

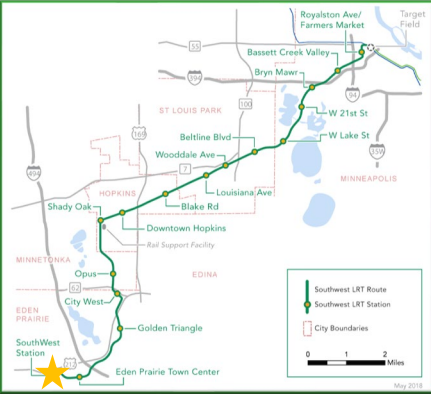


# 70<sup>th</sup> Street Grade Crossing near Golden Triangle Station, Eden Prairie

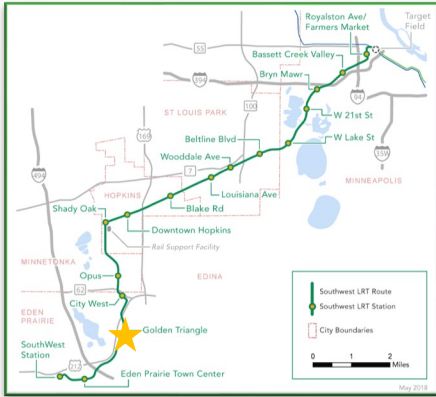

# City West Station, Eden Prairie

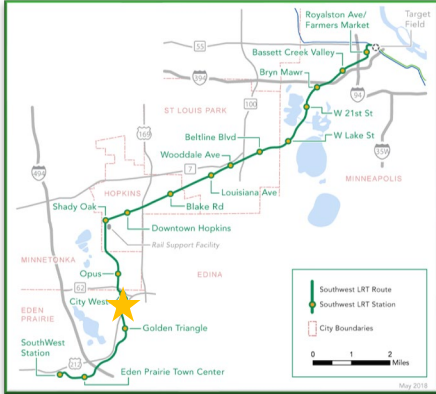


# Thermite Welding at City West Station, Eden Prairie

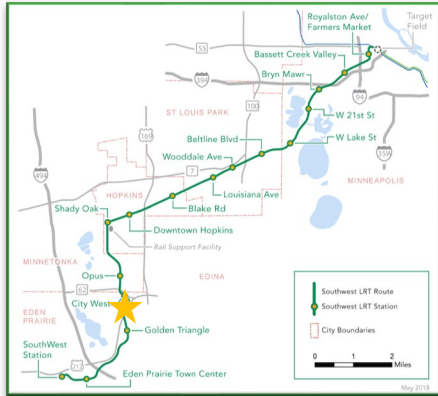





# Ballast Track in Minnetonka

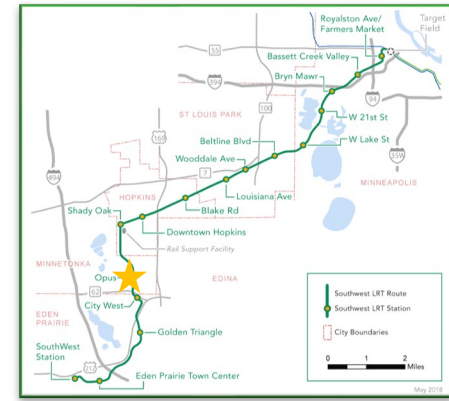


# OCS Foundation and Feltl Road Bridge in Minnetonka

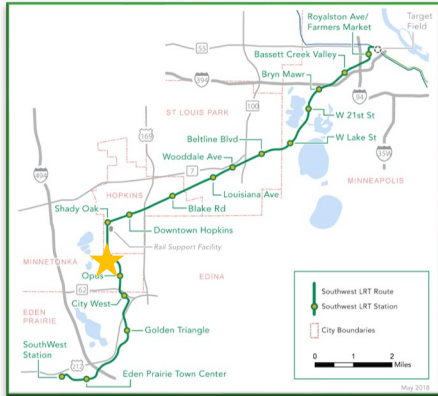


# Excelsior Boulevard LRT Bridge, Hopkins

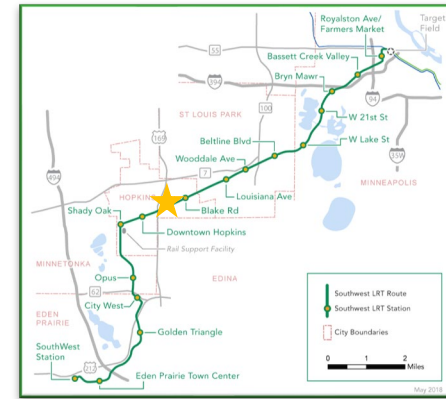


# Blake Road Station, Hopkins

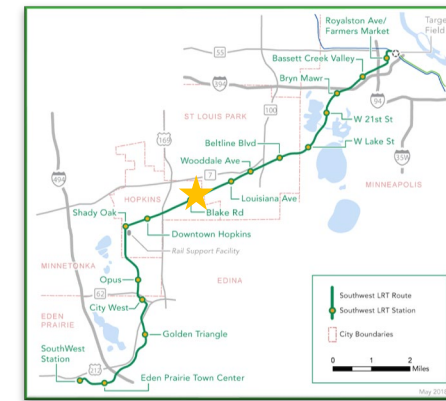


# Louisiana Avenue LRT Bridge, St. Louis Park

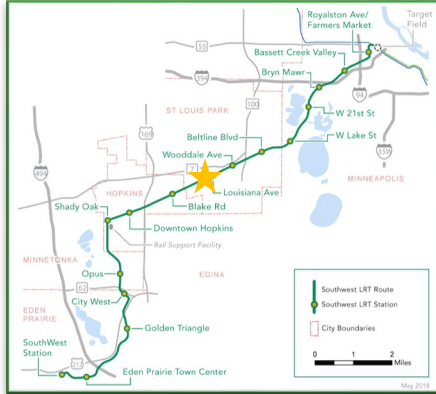


# Louisiana Avenue Station, St. Louis Park

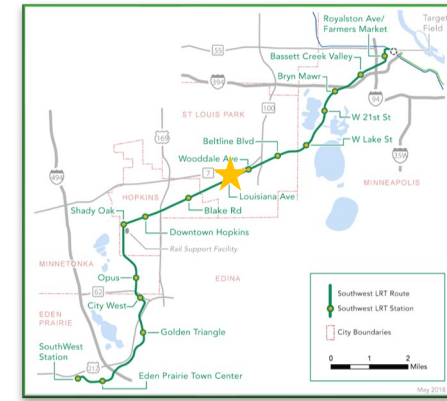

# Wooddale Avenue Station, St. Louis Park

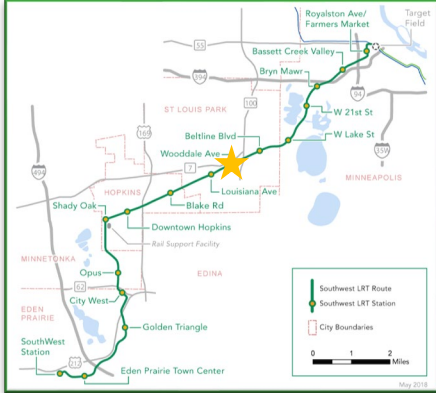


# Secant Wall Construction, Minneapolis

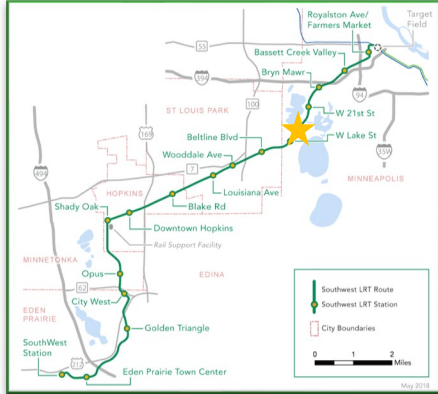





# Kenilworth LRT Tunnel, Minneapolis

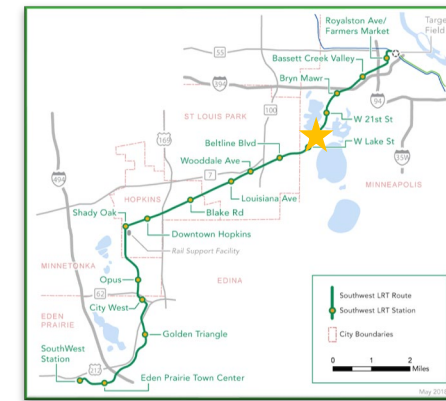


# Cedar Lake Channel Pedestrian Bridge, Minneapolis

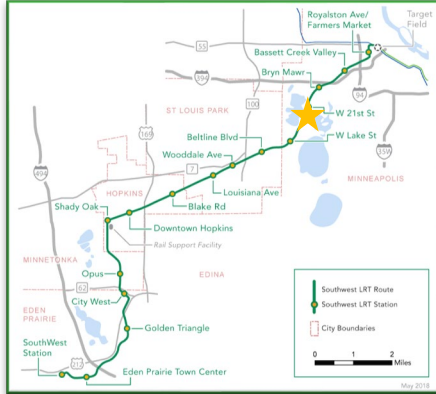


# WPA Wall Work at Cedar Lake Channel, Minneapolis

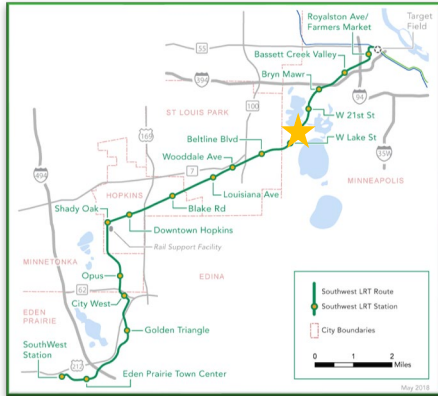


# Bryn Mawr Station, Minneapolis

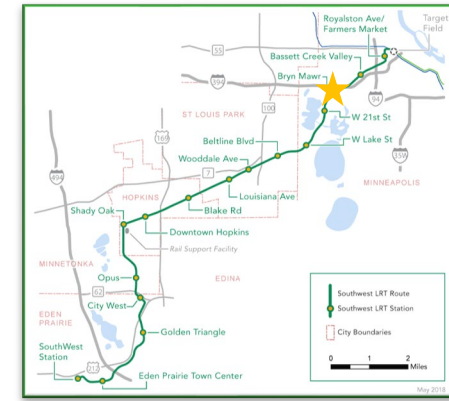


# Bassett Creek Valley Station, Minneapolis

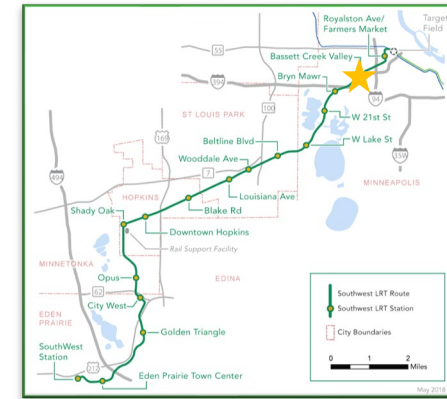

# Glenwood Avenue LRT Bridge, Minneapolis

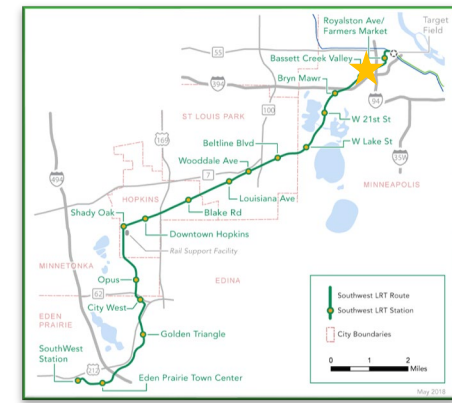


# Royalston Avenue/Farmers Market Station, Minneapolis

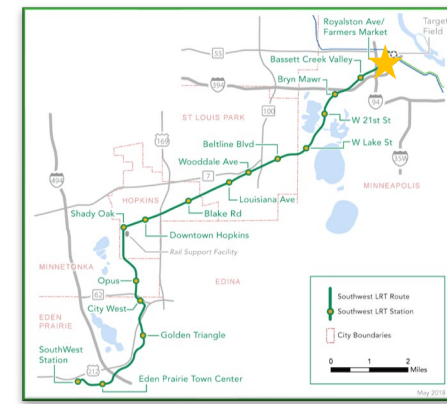


# Systems Contract Work




# TPSS SW301 Site Work and Signal House Foundations, Eden Prairie

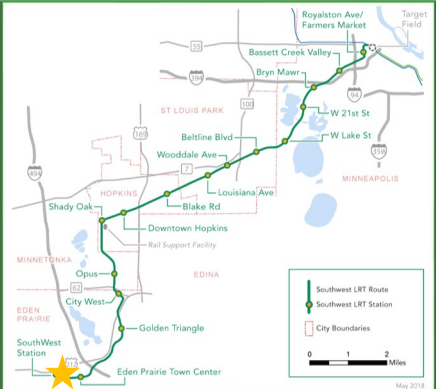


# TPSS SW302 Foundation Base Pour, Eden Prairie

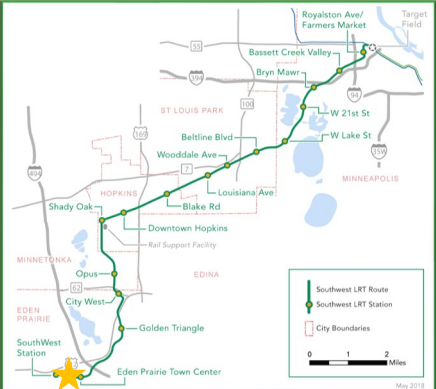


# TPSS SW304 Foundation Base Pour, Eden Prairie

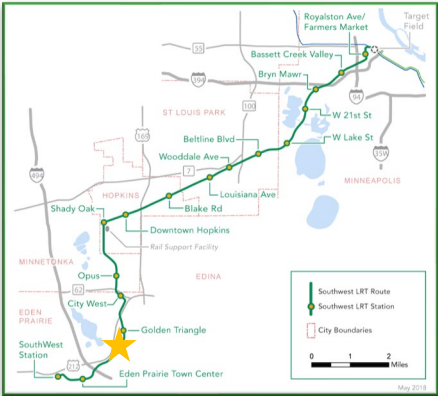

# First OCS Poles Installed at SouthWest Station, Eden Prairie

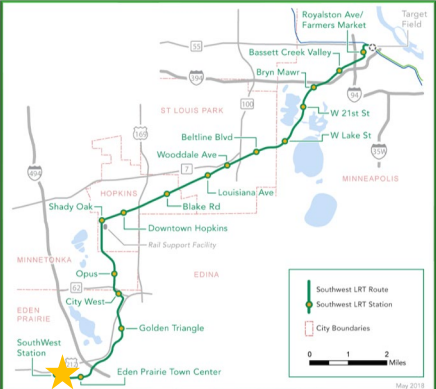

# Signal House Foundations at Beltline Boulevard Station, St. Louis Park

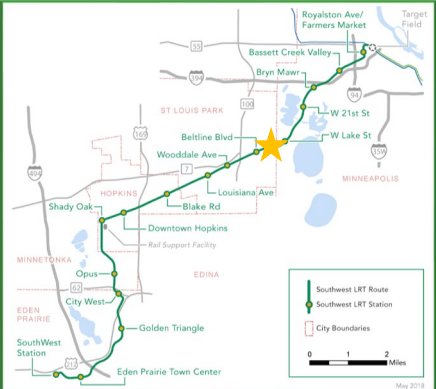

# Systems Contract Work

# DBE Achievement Report

# DBE Achievement as of September 30, 2022

| Contractor           | Contract Description | Contract Amount        | Contractor Billed to Date | DBE Billed to Date    | DBE Date %           | As of Date |
|----------------------|----------------------|------------------------|---------------------------|-----------------------|----------------------|------------|
| LMJV<br>16% Goal     | Civil                | \$1,018,914,600        | \$824,422,359             | \$170,696,420         | 20.7%                | 9/30/22    |
| APJV<br>12% Goal     | Systems              | \$206,667,997          | \$93,779,105              | \$16,337,460          | 17.4%                | 9/30/22    |
| LS Black<br>15% Goal | Franklin O&M<br>Exp. | \$41,221,774           | \$41,221,774              | \$7,787,910           | 18.9%                | 9/30/22    |
| 17% Goal             | Closed<br>Contracts  | \$404,992              | \$404,992                 | \$74,610              | 18.4%                |            |
|                      |                      |                        |                           |                       |                      |            |
|                      |                      | <b>Contract Amount</b> | <b>Billed to Date</b>     | <b>\$ DBE to Date</b> | <b>% DBE to Date</b> |            |
| 15% Goal             |                      | \$1,267,209,363        | \$959,828,230             | \$194,896,400         | 20.3%                |            |



# **Lunda/CS McCrossan Joint Venture: Civil DBE Activities Update**

## LMJV DBE Updates:

- **DBE Appreciation Lunch last month**
- **Continued team meetings with the individual DBEs regarding the Change Order process and other items to assist the DBE in their participation on the project**
- **Meeting with AWC (Association of Women Contractors) re**
  - 1. The project & the various meetings for the project and what value do they bring**

**What is being done? What can be done better?**
  - 2. How can the LMJV assist the AWC with their members?**

**Project presentations, education sessions, etc**

# LMJV Update on Change Orders

- Owner Change Orders approved thru 10/15: \$220,191,290
  - DBE Job To Date Participation: 20.59%

*\*Does not take into account LMJV directed change orders with Subcontractors*

# **Aldridge Parsons Joint Venture: Systems DBE Activities Update**

# Anticipated DBEs: One Month Look Ahead

- Louisiana Ave. Station – Communications Work Gunnar Electric
- Blake Road - Communications Work Gunnar Electric
- Meyer/MBE (Trucking) will continue work off and on at TPSS 304 & TPSS 301 until mid December. TPSS 302 has been completed.
- Meyer/Moltron (Labor) will be continuing station foundation work at TPSS 304 & TPSS 301. Completed foundation at 302 last month
- Bald Eagle is following Moltron installation at TPSS 304 and 301 with Rebar installation. TPSS 302 Rebar work did complete last month
- Public Solutions – Weekly Construction Update


# APJV Update

- Owner change orders approved thru 11/8/22: \$ 12,587,754.41
- Public Solutions for Manhole dewatering figured to take place at TPSS 304&301
- Carlo Lachmansingh Sales will have the remaining Wide Flange poles on site by the end of this quarter. One Shipment arrived last month as part of their final release
- DBE change order participation: 17.49%
- DBE job to date participation: 15.36%

# Workforce Participation Report

# Civil Workforce Participation Percentage\*

- September 2022: 66,532 hrs
- Civil Construction Total: 2,401,320 hrs

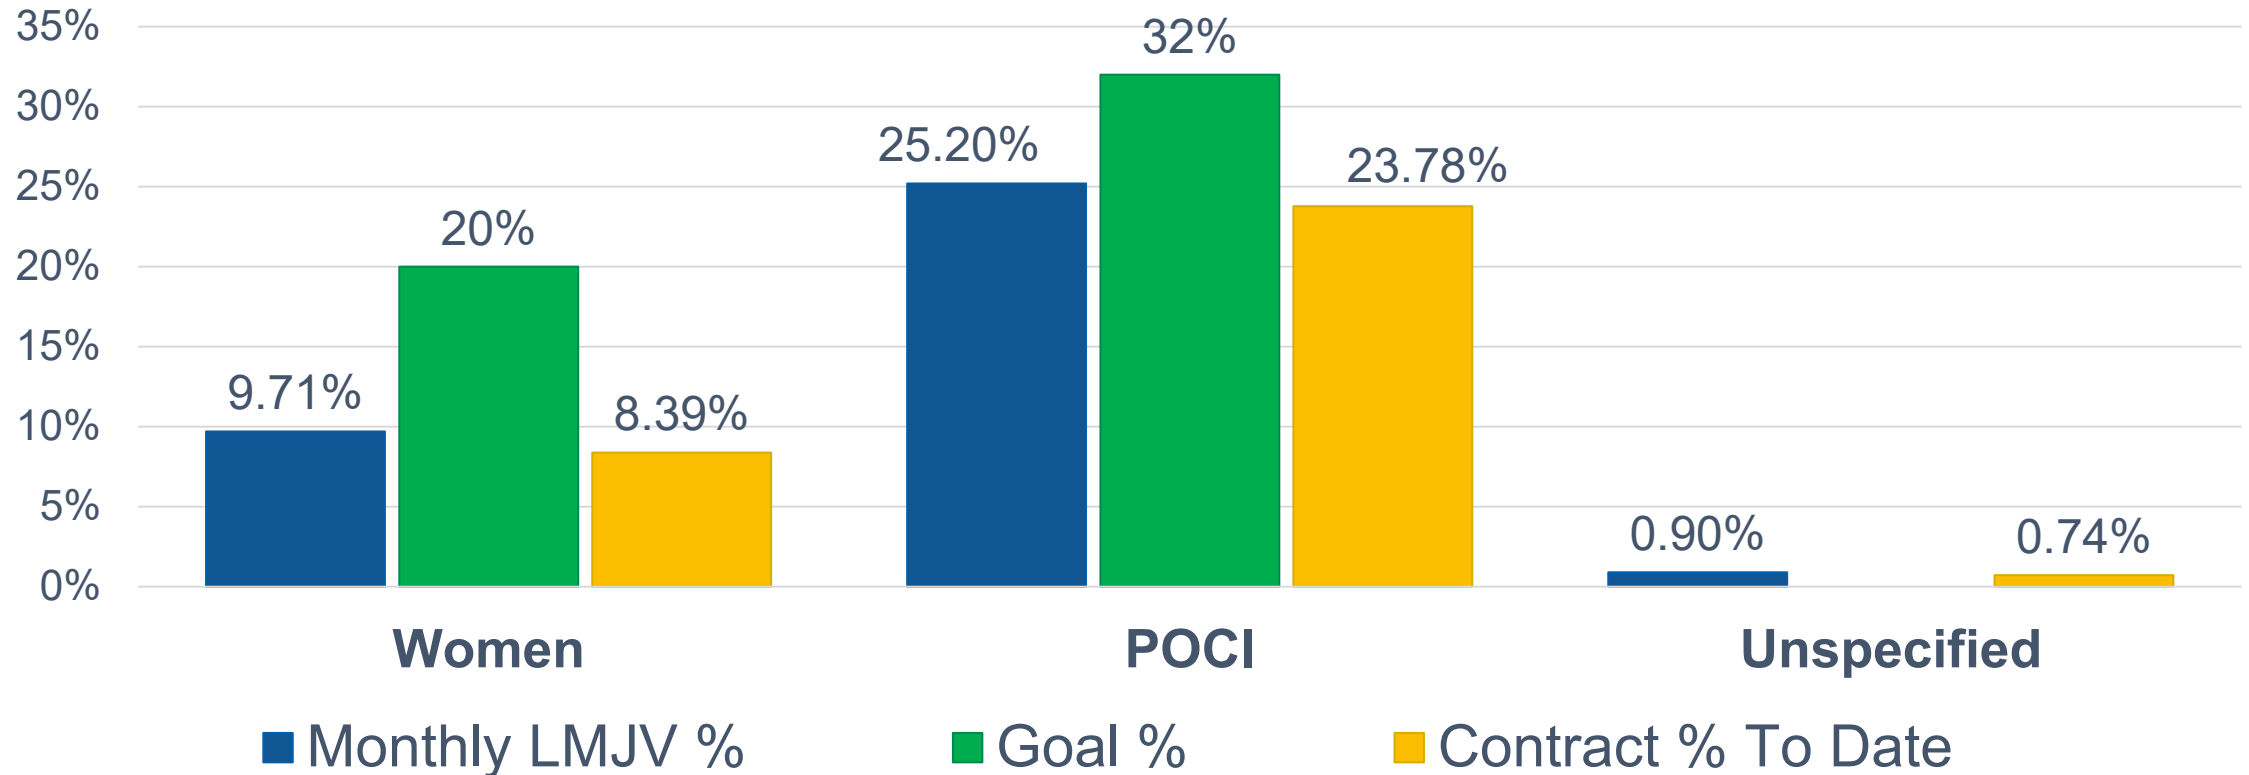


\*Based on MDHR Workforce Report for September 2022  
People of Color/Indigenous (POCI)



# Civil Workforce Participation\*

- September 2022: 66,532 hrs
- Hours worked by category:

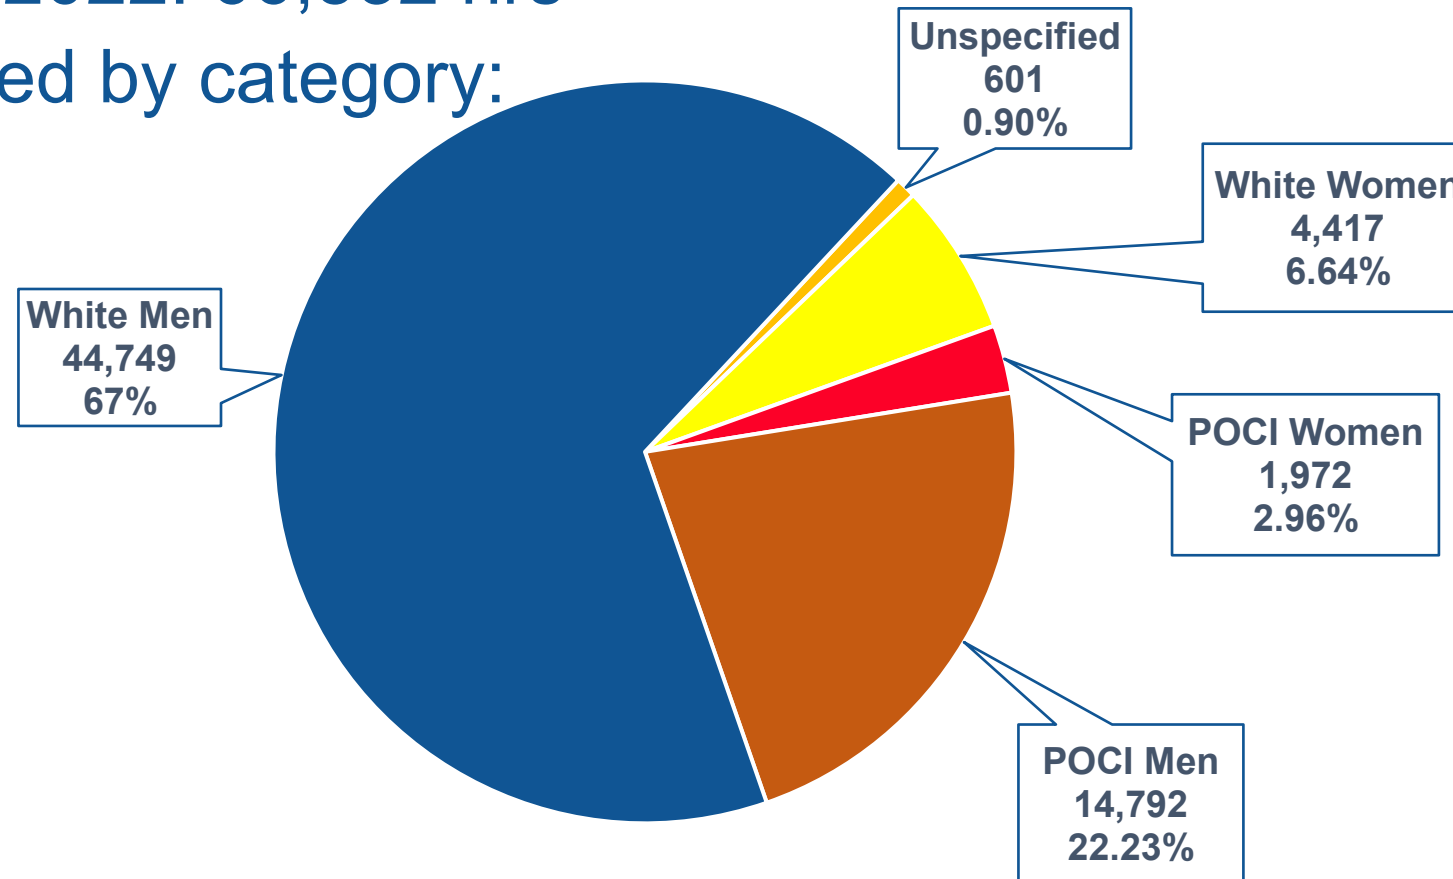

\*Based on MDHR Workforce Report for September 2022

# Civil Workforce Trucking Participation\*


Trucking participation on Project being counted:

- MBE: 28,933 hours
- ZTS: 4,640 hours
- Rock-On Trucks: 3,350 hours

\*Based on MDHR Workforce Reports: Project Start through September 2022

# Systems Workforce Participation Percentage\*


- September 2022: 428 hrs
- Systems Construction Total: 4,578 hrs

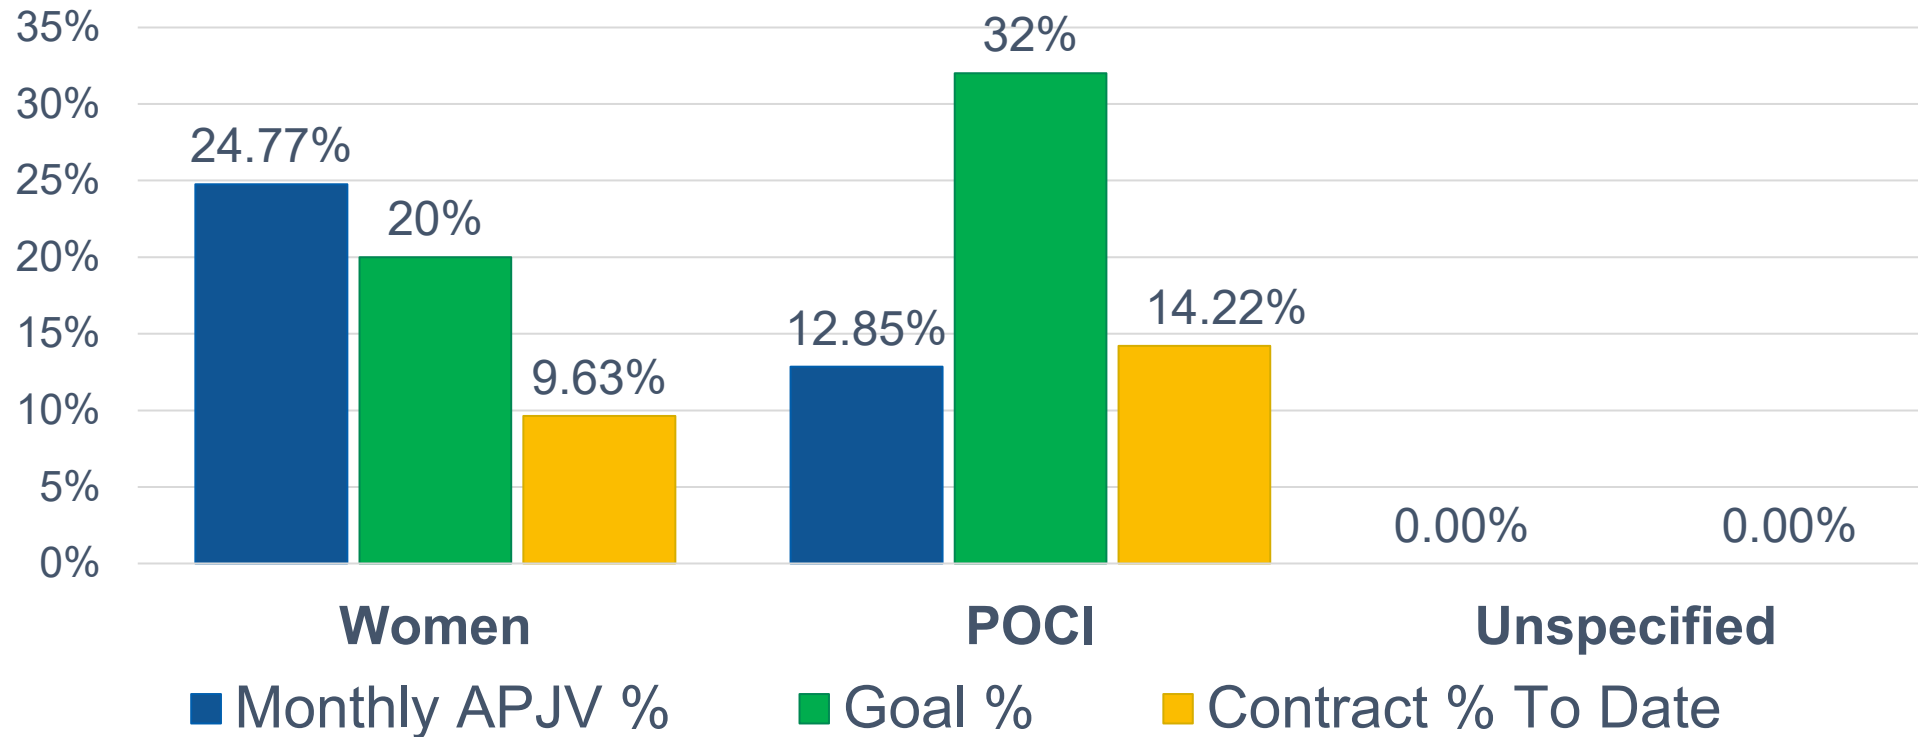

\*Based on MDHR Workforce Report for September 2022  
People of Color/Indigenous People (POCI)

# Systems Workforce Participation\*

- September 2022: 428 hrs
- Hours worked by category:

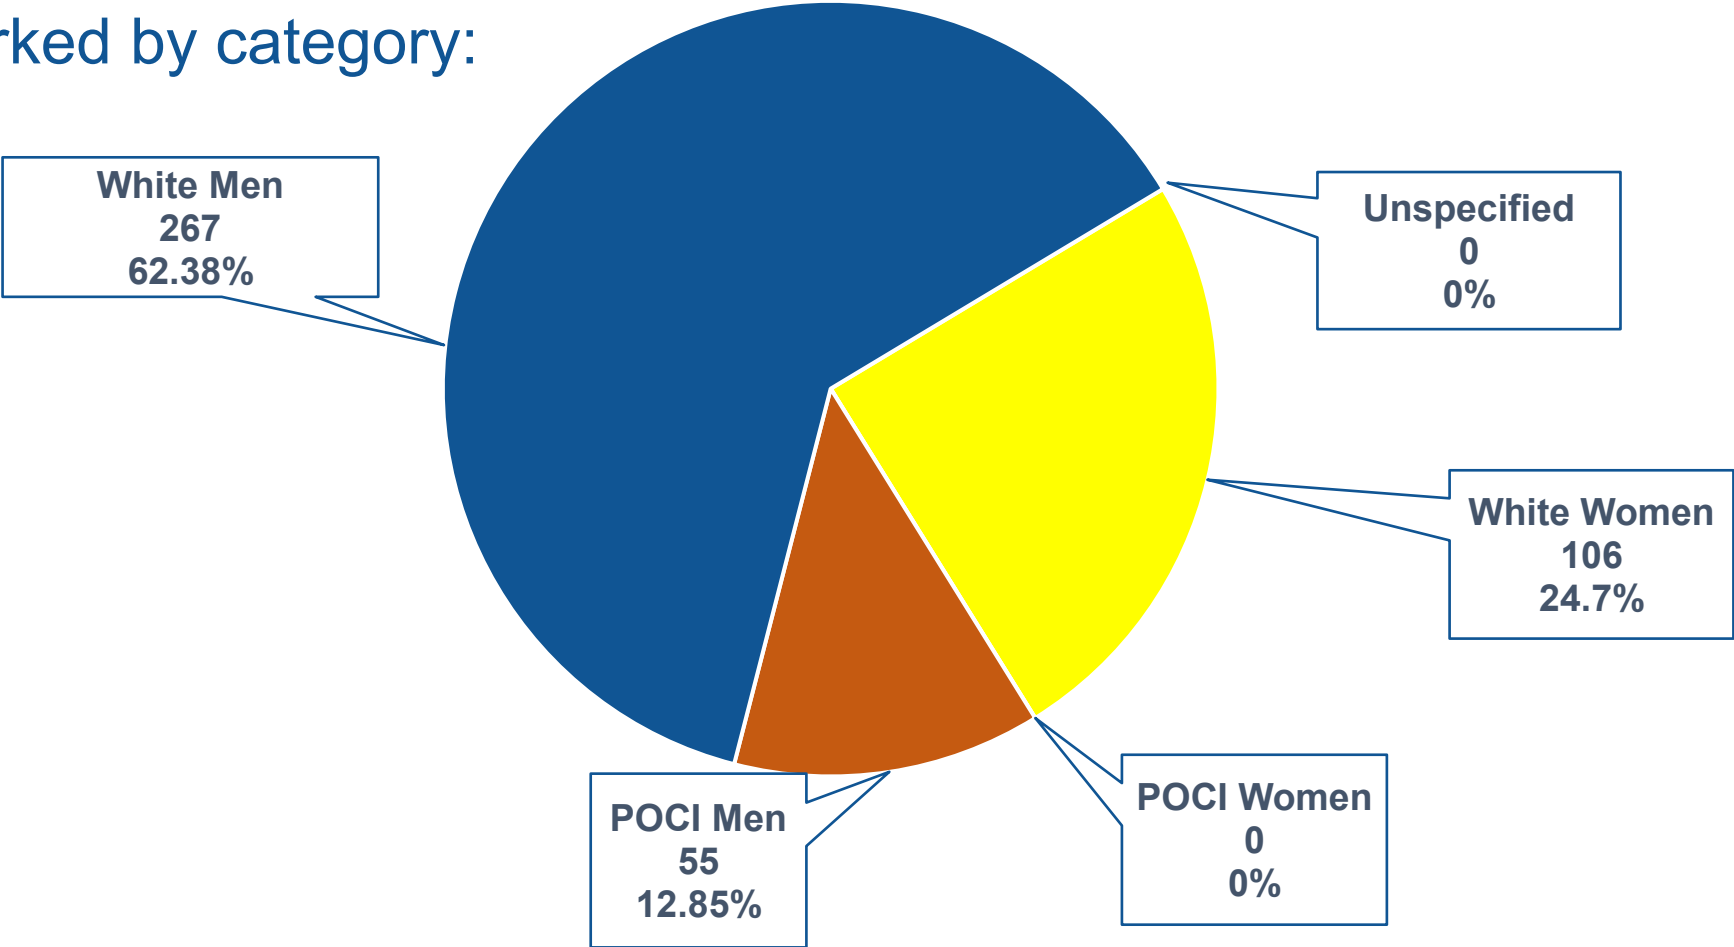

\*Based on MDHR Workforce Report for September 2022

# **Lunda/CS McCrossan Joint Venture: Civil Workforce Activities Update**

# New Hires/Rehires/Transfers – October 2022

- **Transfers**

White Male:  
White Female: 0  
POCI Male:  
POCI Female: 0

- **Rehires** (Returning from furlough)

White Male: 0  
White Female: 0  
POCI Male: 0  
POCI Female: 0

- **New Hires**

White Male: 0  
White Female: 0  
POCI Male: 0  
POCI Female: 0

- **Lay-Offs**

White Male:  
White Female: 0  
POCI Male:  
POCI Female: 0

- **Voluntary Leaves**

White Male: 0  
White Female: 0  
POCI Male: 0  
POCI Female: 0

# LMJV Workforce Highlights from October:

- ✓ Internal LMJV Workforce Meeting – Enter/Exit & Projections
- ✓ Meetings w/ Carpenters Reps re – Mentor Program & Training
- ✓ Weekly Staff Meetings – DBE & Workforce Education & Updates
- ✓ Bi-Weekly G.E.A.R.S. Team Meetings
- ✓ Job Site Walks – Respectful Workplace/Culture of CARE
- ✓ Meetings with MDHR to review efforts and participation
- ✓ Ongoing Planning with Building Strong Communities
- ✓ Meetings w/ Urban League of TC
- ✓ Subcontractor Meeting & Education Series – Inclusion & CARE
- ✓ Virtual DWAC Meeting
- ✓ Construction Inclusion Week – See next slide

# LMJV Workforce Highlights - October:

October 17<sup>th</sup>-21<sup>st</sup>



- Culture of CARE Pledge
- Booth at Career Connection Day
- DBE Appreciation Luncheon
- Culture of CARE continued training  
- table & toolbox talks
- Winter Wear Drive w/ Urban League





# **Aldridge Parsons Joint Venture: Systems Workforce Activities Update**

# Systems Workforce Activities Update

- Plan to meet the workforce goal:
  - APJV limited scopes available for craft labor through 2022. Work at the TPSS started in the first week of October. A small OCS crew will start next week in segments 2 & 3. Bulk of craft labor will begin until Spring of 2023.
  - APJV and Lower Tier Subcontractors will attend CBO Outreach Event hosted by LMJV on Wednesday, September 21<sup>st</sup>.
  - On Thursday, October 13, 2022 APJV will provide a day of training with Summit Academy for the fall cohort of 40 students. This training will include hands activities with Aldridge' Traveling Utility Training Trailer, discussion with Union Reps & Subcontractors, and Incident and Injury Free (IIF) Safety Training. Subcontractors and Unions will be invited to meet the Cohort.




# Survey Results

# Proposal A Responses

## Meeting Every Other Month: Starting in November 2022

- Cancel meetings in December 2022 and February 2023
- Return to monthly meetings in March 2023
- Achievement reports to be sent out monthly as normal




\*No strong preference for either option

# Proposal B

## Meeting Monthly Starting in January 2023

- Cancel meeting in December 2022
- Return to monthly meetings in January 2023
- Achievement reports to be sent out monthly as normal



\*No strong preference for either option

# Subcommittee Preferences to Meet: Week and Day

Which week of the month and which day of the week would work best for you to participate in the subcommittee on a monthly basis?

1. 1<sup>st</sup> Thursday of the month (6 votes)
2. 4<sup>th</sup> Thursday of the month (5 votes)
3. 3<sup>rd</sup> Friday of the month (4 votes)

Next steps:

- Meeting in the morning or afternoon?
- Length of the meeting?
- Should the subcommittee be led by a member?

# Committee Discussion



# Discussion of Potential Committee Changes in 2023

What changes to the meeting format may help this committee?

Previous suggestions:

- Having the DBE and Workforce achievements be consent items
- An invitation call for presentations on DBE or Workforce topics
- Splitting the meeting into a DBE portion and a Workforce portion

Other ideas or suggestions?

# Announcements

# Public Invitation

- Each speaker is limited to a three-minute presentation
- Pre-register as you sign in for attendance at the start of the meeting



# Closing

- Next Meeting date: January 19<sup>th</sup>, 2023, from 2:00 – 4:00 PM
  - The meeting in December 2022 will be cancelled
- Adjourn

## **MORE INFORMATION**

**Website:** [GreenLineExt.org](https://GreenLineExt.org)

**Email:** [swlrt@metrotransit.org](mailto:swlrt@metrotransit.org)

**Twitter:** [@GreenLineExtMN](https://twitter.com/GreenLineExtMN)

**Instagram:** [@GreenLineExtMN](https://www.instagram.com/GreenLineExtMN)
