

## Disadvantaged Business Enterprise and Workforce Advisory Committee

October 19<sup>th</sup>, 2023





EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

## **Today's Topics**

- Project Update
- Consent Business
- Non-consent Business
- Committee Discussion
- Announcements
- Public Invitation



## **Project Office Update**

## **Civil Construction Update**

# Passenger drop-off and access ramp at SouthWest Station in Eden Prairie









#### **Completed station, plaza, and parking area at Golden Triangle Station in Eden Prairie**



#### **City West Station in Eden Prairie**





#### **Trackwork north of Opus Station in Minnetonka**





#### Removal of the haul route and restoration of wetlands under the Minnetonka-Hopkins LRT bridge





#### Special trackwork north of Minnetonka/Hopkins LRT Bridge





# Park and Ride construction at Louisiana Avenue Station in St. Louis Park








#### LRT grade crossing at Wooddale Avenue in St. Louis Park





# LRT track at Beltline Boulevard Station in St. Louis Park





Green Line EXTENSION

#### Vertical circulation steel at West Lake Street Station in Minneapolis







#### Kenilworth LRT Tunnel west heading in Minneapolis










#### **Bryn Mawr Station in Minneapolis**





#### Trackwork west of Bassett Creek Valley Station in Minneapolis

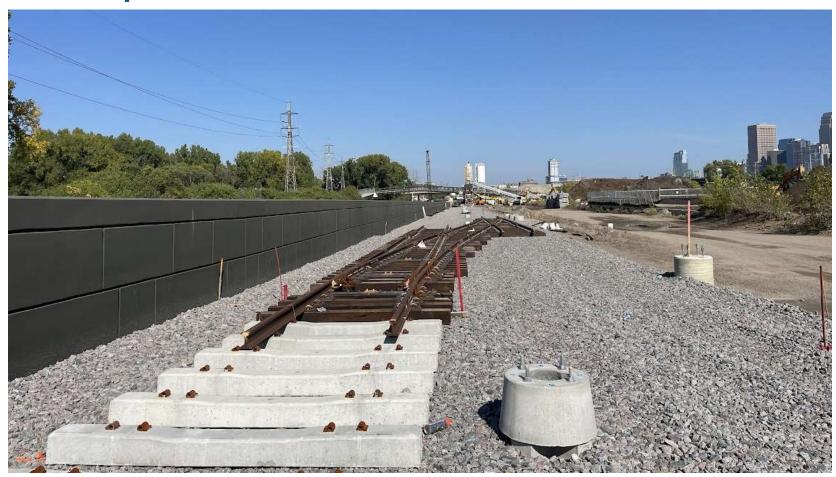




#### Vertical circulation steel at Bassett Creek Valley Station in Minneapolis





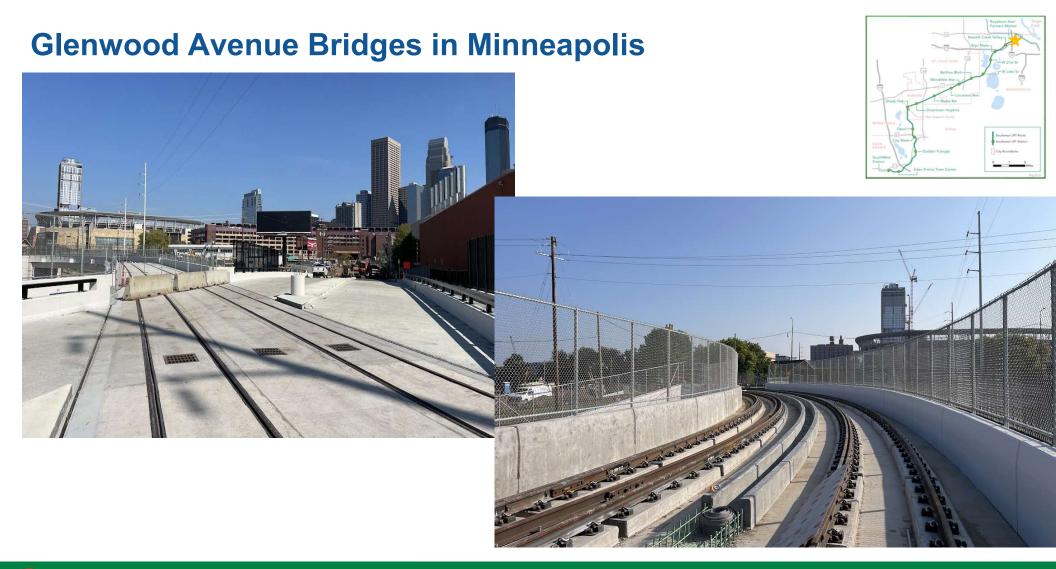

#### **Royalston Avenue/Farmers Market Station in Minneapolis**





#### Duct bank installation on 5th Avenue/7th Street LRT Bridge in Minneapolis









## **Systems Contract Work**

#### **Overhead Catenary System (OCS) Poles and Wire Installation**

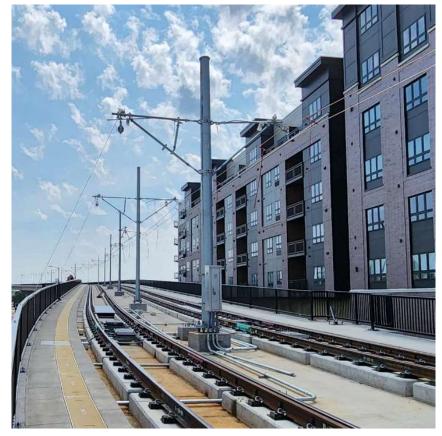

Prairie Center Drive Bridge in Eden Prairie

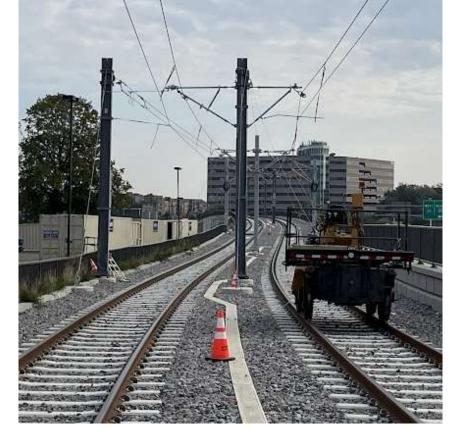

Flying Cloud Drive in Eden Prairie

#### **Traction Power Substation (TPSS) Installation**



TPSS SW305 Installation in Eden Prairie



#### **Traction Power Substation (TPSS) Installation**



TPSS SW305 Installation in Eden Prairie

#### TPSS 307 & signal house set on foundations in Minnetonka





## **Consent Business**

## **DBE Achievement Report**

### **DBE Achievement as of August 31, 2023**


Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	% DBE to Date	As of Date
LMJV 16% Goal	Civil	\$1,040,380,762	\$917,956,487	\$212,217,036	23.1%	8/31/23
APJV 12% Goal	Systems	\$209,159,681	\$136,227,099	\$22,672,068	16.6%	8/31/23
	Closed Contracts	\$41,626,766	\$41,626,766	\$6,539,604	15.7%	
		Contract Amount	Billed to Date	DBE Billed to Date		
15% Goal		\$1,291,167,209	\$1,095,810,351	\$241,428,708	22.0%	

# **Workforce Participation Report**


## **Civil Workforce Participation Percentage\***

• August 2023: 49,806 hrs.

#### • Civil Construction Total: 2,921,070 hrs.

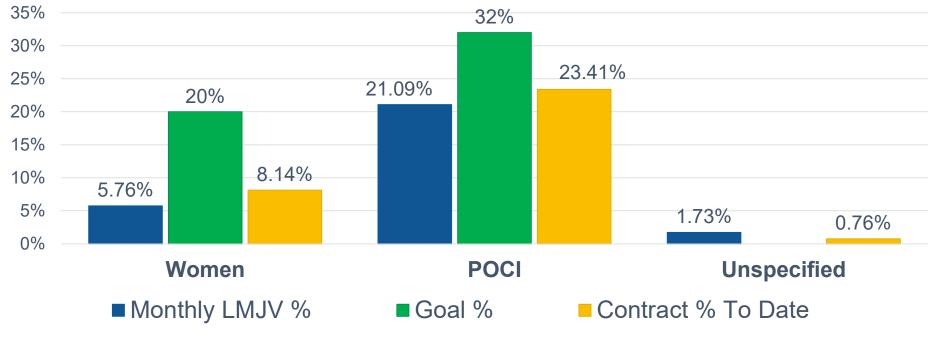

\*Based on MDHR Workforce Report for August 2023 People of Color/Indigenous (POCI)

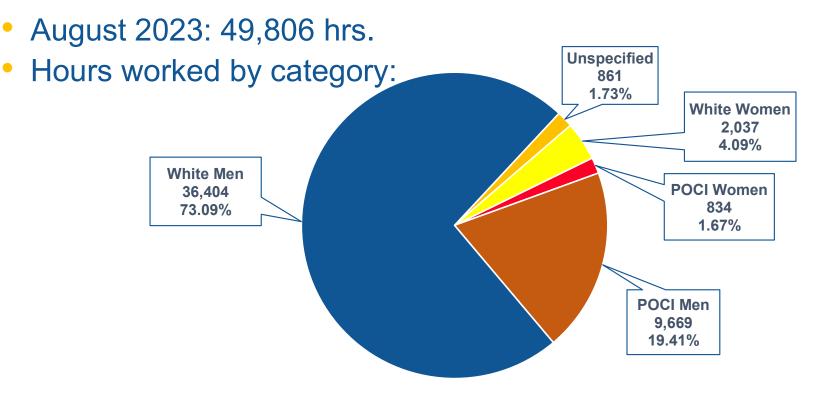

### **Civil Workforce Participation\***


\*Based on MDHR Workforce Report for August 2023

## **Civil Workforce Trucking Participation\***

- Trucking participation on Project being counted:
  - MBE: 32,130 hours
  - Rock-On Trucks: 4,900 hours
  - ZTS: 4,647 hours (no change)


## **Systems Workforce Participation Percentage\***

- August 2023: 4,254 hrs.
- Systems Construction Total: 38,266 hrs.

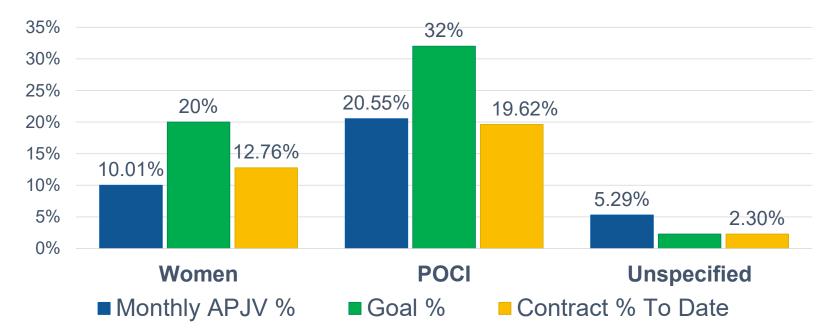

\*Based on MDHR Workforce Report for August 2023 People of Color/Indigenous People (POCI)

## **Systems Workforce Participation\***

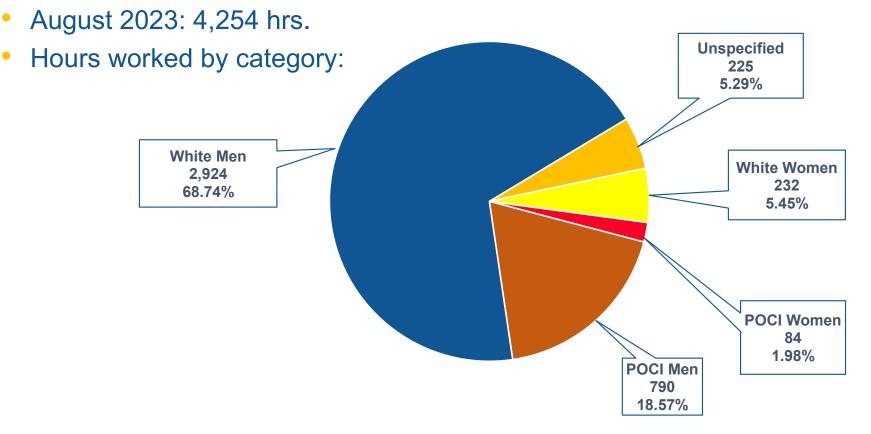

\*Based on MDHR Workforce Report for August 2023

## **Non-Consent Business**

### **Civil Contract Work**

# **Civil Contract DBE Updates**



**METRO** Green Line EXTENSION

08/2023 DWAC Meeting

39



## **SEPTEMBER – DBEs working on project**

- All Phase
- Blackstone
- E&J Rebar
- Gunnar Electric
- JL Theis
- MBE
- On Call Pavement Sweepers
- PWS

- Public Solutions Group
- Reiner
- Rock On
- Safety Signs
- Standard Contracting
- Stonebrook Fence
- Sun Mechanical

## Civil Contract Workforce Achievement Updates



**METRO** Green Line EXTENSION



SWLRT Civil Project	Sep-23	
TRADES	Female %	POCI %
BrickLayers	0.00%	18.65%
Carpenters	1.83%	32.67%
Cement Masons	0.00%	30.05%
Electricians	8.15%	20.85%
Equipment Operators	6.15%	8.70%
Glaziers	0.00%	0.00%
Ironworkers	5.15%	27.49%
Laborers	6.98%	29.91%
Other (Sheetmetal)	0.00%	0.00%
Painters	23.73%	61.91%
Pile Drivers	0.00%	24.50%
Plumbers	0.00%	0.00%
Roofer	9.40%	9.77%
Truck Drivers	5.00%	28.40%
	5.82%	23.43%

**METRO** Green Line EXTENSION



MONTHL						
IN & OUT BREAKDOWN (LMJV/Lunda/CS McCrossan)						
IN REPORT		WHITE	WHITE	MINORITY	MINORITY	
	TOTAL	MALE	FEMALE	MALE	FEMALE	
TRANSFERS	7	7	0	0	0	
REHIRE/						
RETURN	0	0	0	0	0	
NEW HIRE	0	0	0	0	0	
OUT		WHITE	WHITE	MINORITY	MINORITY	
REPORT	TOTAL	MALE	FEMALE	MALE	FEMALE	
TRANSFERS	0	0	0	0	0	
Lay-Off	0	0	0	0	0	
Voluntary						
Leave	0	0	0	0	0	

**METRO** Green Line EXTENSION

#### **GOOD FAITH EFFORT Updates**



CONSTRUCTION INCLUSION WEEK – Happening This Week!

Each day is a main topic to help guide participants with themes & activities We have Toolbox Talks & Webinars that are distributed each day to both the field & office Monday - Commitment & Accountability <u>https://youtu.be/2g88Ju6nkcg?si=k19mjVB5KBLZXFxL</u> Tuesday – Belonging <u>https://youtu.be/dKggA9k8DKw?si=akxGOQHd7ZaZ7iuS</u> Wednesday – Supplier Diversity <u>https://youtu.be/Nh0fsaUDINw?si=RytyI9zh6IsRbE3h</u> Thursday – Workplace Culture <u>https://youtu.be/\_SeiA14tSKI</u> Friday – Community Engagement <u>https://youtu.be/mTsvSAltPqA?si=QGTIe5z0sdonSyDp</u>

Page 1 of 2

44

**GRETRO** Green Line EXTENSION

#### **GOOD FAITH EFFORT Updates**



#### **CONSTRUCTION INCLUSION WEEK – Happening This Week!**

TUESDAY LMJV & Lunda have a booth at the **Career Connection Day** @ St Paul River Center

- WEDNESDAY AM Education on **"Be More Than a Bystander"** brought to us by the NCSRCC PM 4<sup>th</sup> Rosies & Robbies of the Rail Roundtable Put Me in Coach
- THURSDAY Team Building Activity @ LMJV Office
- FRIDAY **Project Tour/Talks/Lunch** for Lake Street Works Program

COMMUNITY SUPPORT **Spare Change Challenge** – between LMJV & Trade Partners Funds raised will be supporting Lake Street Works with supplies/materials/tools

Page 2 of 2

45

#### **Systems Contract Work**

### **Systems Updates**

- APJV and Premier Electric participated in Mock Interviews at Summit Academy On September 15, 2023.
- APJV will participate in "Construction Inclusion Week" activities October 18, 2023 "Rosies on the Rail" & October 20, 2023 Lake Street Works

#### Workforce Achievement Update SWLRT – Systems Workforce August 2023 Trade Participation by Hours

TRADES Male Female Female % POCI POCI % Total Carpenter 238.50 189.00 49.50 20.75% 0.00% Electricians 3,194.50 1,033.00 3.693.75 499.25 13.52% 27.97% **Equipment Operators** 836.25 824.25 12.00 1.43% 113.00 13.51% Ironworkers 39.00 39.00 0.00% 4.00 -10.26% Laborers 376.00 353.00 23.00 6.12% 99.50 26.46% Painters ----Roofer 32.00 32.00 0.00% 75.00% 24.00 -Sprinkler Fitters 0.00% 493.00 493.00 0.00% --Surveyors 26.00 26.00 0.00% 0.00% --Traffic Control 18.25 18.25 0.00% 12.00 65.75% -Truck Driver 3.00% 158.50 153.75 4.75 18.75 11.83% TOTALS 5,911.25 588.50 9.96% 22.06% 5,322.75 1,304.25

# **Committee Discussion**

#### **Committee Meetings Look Ahead**

- Committee attendance
- Meeting in person vs. virtual
- Committee meeting frequency during Winter months
- Reporting DBE and Workforce data during this period

## Announcements

#### **Public Invitation**

- Each speaker is limited to a three-minute presentation
- Pre-register as you sign in for attendance at the start of the meeting



#### Closing

- Next Meeting date: November 16th, 2023, from 2:00 4:00 PM
  - Held Virtually
- Adjourn

#### **MORE INFORMATION**

Website: <u>GreenLineExt.org</u>

Email: <a href="mailto:swlrt@metrotransit.org">swlrt@metrotransit.org</a>

Twitter: @GreenLineExtMN

Instagram: @GreenLineExtMN
