

SOUTHWEST

Green Line LRT Extension



Disadvantaged Business Enterprise and Workforce Advisory Committee

April 15, 2021



EDEN PRAIRIE | MINNETONKA | EDINA | HOPKINS | ST. LOUIS PARK | MINNEAPOLIS

Today's Topics





- Building Strong Communities Update
- Project Update
- DBE Reporting
- Workforce Reporting





**Building Strong Communities
2021**

Building Strong Communities: April Update

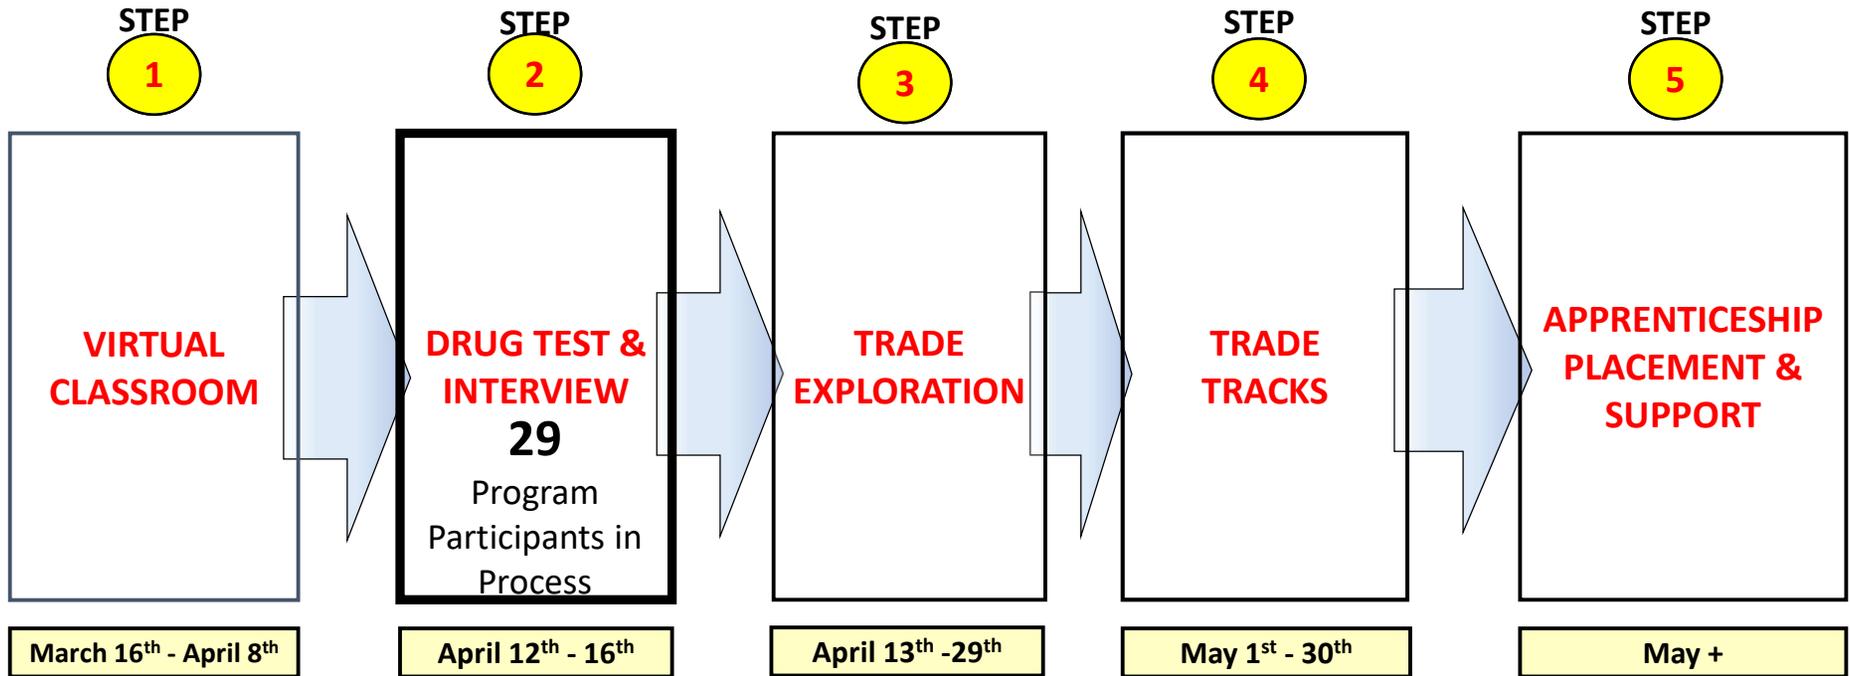

Building Strong Communities: April Update


BUILDING
Strong Communities

BSC Physical Exposure

Saturday April 10th

Iron Workers Local 512

Joint Apprenticeship Training Center

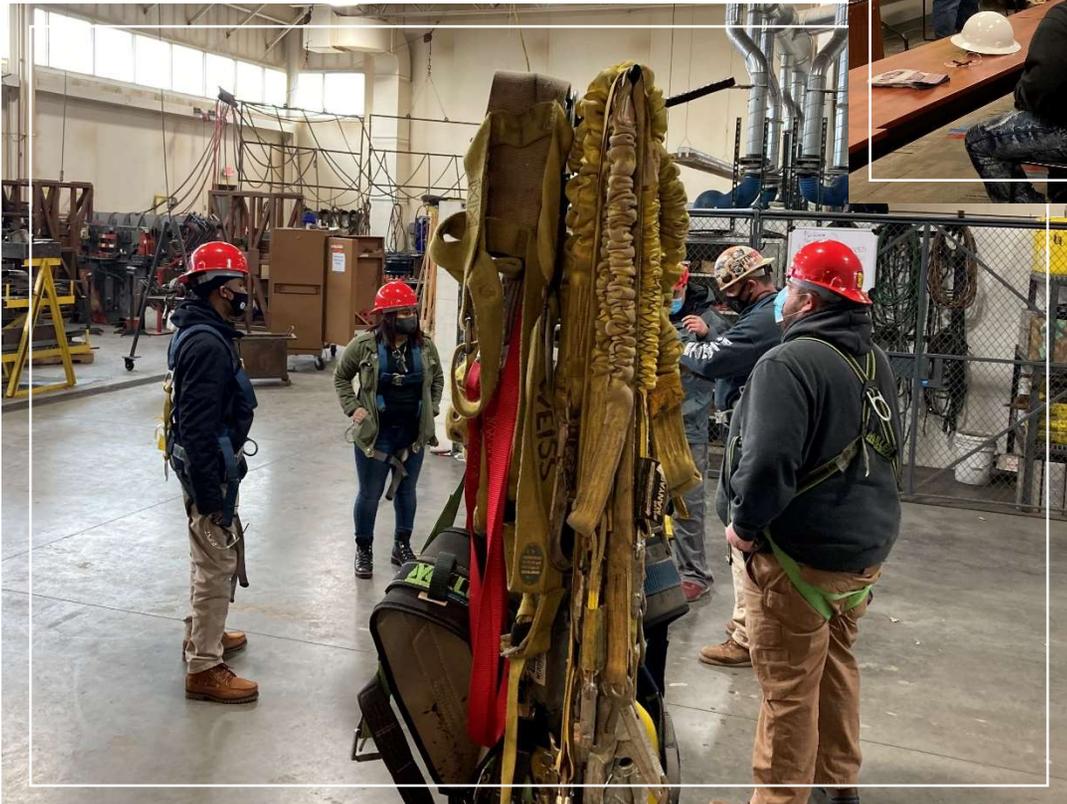

- Pre –work Stretching
- Ergonomics on a jobsite
- Proper Ladder ascension
- Lifting techniques
- Tape measure use
- Carrying techniques

Building Strong Communities: April Update

BUILDING
Strong Communities



Building Strong Communities: April Update

BUILDING
Strong Communities




SWLRT Project Update


SouthWest Station, Eden Prairie




Town Center Station, Eden Prairie

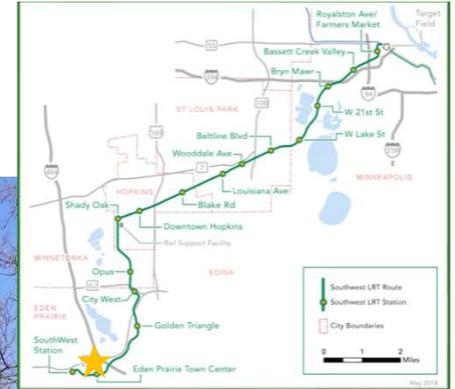


TH 62 LRT Tunnel, Minnetonka

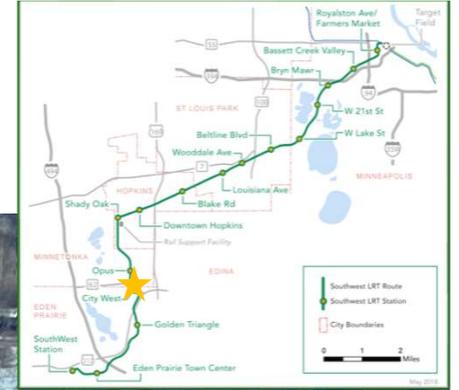


Smetana Roadway Bridge, Minnetonka

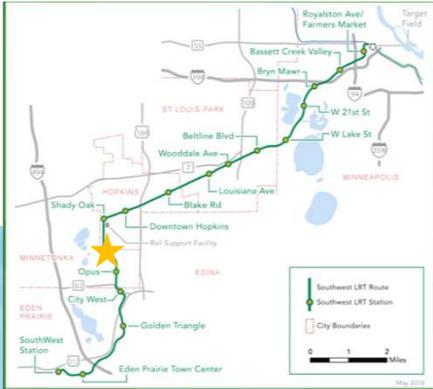

Beltline Blvd Pedestrian Bridge, St. Louis Park

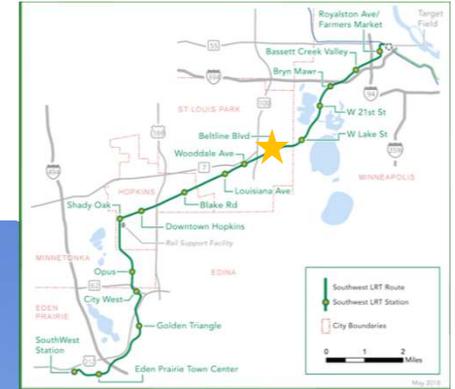

Tremmie Pour Kenilworth LRT Tunnel, Minneapolis

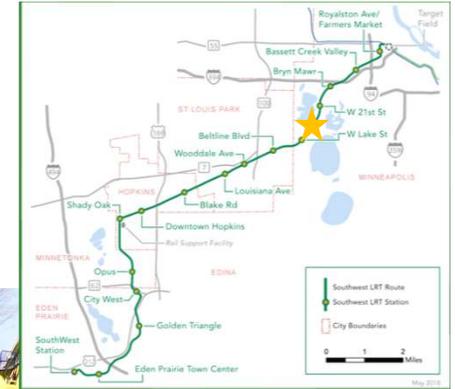

Glenwood Avenue LRT Bridge, Minneapolis



Franklin O&M Facility Modifications



Car wash equipment is installed

Franklin O&M Facility Modifications



TPSS 15B Enclosure in factory production.

DBE Achievement Report

DBE Achievement as of Feb. 28, 2021

Contractor	Contract Description	Contract Amount	Contractor Billed to Date	DBE Billed to Date	DBE Date %	As of Date
LMJV 16% Goal	Civil	\$840,085,835	\$427,030,459	\$87,579,030	20.5%	2/28/21
APJV 12% Goal	Systems	\$193,819,580	\$48,981,775	\$7,623,628	15.6%	2/28/21
LS Black 15% Goal	Franklin O&M Exp.	\$38,704,353	\$17,134,713	\$3,287,213	19.2%	2/28/21
17% Goal	Closed Contracts	\$404,992	\$404,992	\$74,610	18.4%	
		Contract Amount	Billed to Date	\$ DBE to Date	% DBE to Date	
15% Goal		\$1,073,014,760	\$493,551,939	\$98,564,481	20.0%	

Lunda/CS McCrossan Joint Venture: Civil DBE Activities Update

DBE Participation on the SWLRT – March & April

Civil Contract

- Airfresh Industries
 - Blackstone
 - Big G Tech Support
 - Boys Contracting
 - E&J Steel Erectors
 - HHA
 - IMO Consulting Group
 - Mac's Roll-Off Service Inc
 - On Call Pavement Sweeping
 - Pete's Water & Sewer
 - Public Solutions Group
 - Safety Signs
 - Standard Contracting Inc
 - Stonebrooke Fence Inc.
 - Zaczkowski Trucking Service
 - MBE Inc
 - Biffs Inc
 - CI Utilities LLC
 - M&J Trucking
 - AmTec
- Sanitary Facilities
 - Retaining Walls
 - Project Offices and Support
 - Pipe Supply
 - Steel Erection
 - Scheduling Consultant
 - Surveying
 - Dumpsters
 - Street Sweeping
 - Utility Work
 - Public Info and Site Prep.
 - Maintenance of Traffic
 - Erosion Control and Miscellaneous Civil
 - Fencing
 - Project Trucking
 - Project Trucking
 - Sanitary Facilities
 - Electrical Testing
 - Project Trucking
 - Structural Steel (SUPPLY ONLY)

Stations Contract

- Amtec
- Econ Placers
- Biffs
- Sun Mechanical

LMJV DBE Highlight

IMO Consulting Group

Scope of work:

Pre & Post Condition Surveys	\$760,000
Construction Surveying	\$5M
Total Contract to Date	\$5.8M
Total Complete to Date	\$4.9M

“IMO’s office and field staff are knowledgeable of the project, as well as being flexible to work around our needs, making them and integral part of our team”

Todd Banker, Lunda Superintendent

Aldridge Parsons Joint Venture: Systems DBE Activities Update

Anticipated DBEs: One Month Look Ahead

- APJV process meeting held on 3/25/21:
- Bald Eagle Erectors (Meyer sub)
- Moltron Builders (Meyer sub)
- IMO (Pre / Post Inspection)
- Dionne Construction
- Topics
 - - DBE tracking
 - - Certified payroll
 - - Workforce goals and tracking
 - - Monthly invoicing process
 - - Invoice documentation requirements and deadlines
 - - Tax reimbursement (AUA process)

APJV Systems Contract DBE Update

- Request for quotes (RFQ's) to following DBE's
 - Boys Water Products (material supplier to Minger Construction Companies)
 - Pumps for tunnel: Approximately \$81K WBE

APJV Update on Change Orders

- Owner change orders approved thru 3/1/21
 - \$1,005,600.10
- DBE Change Order Participation:
 - Gunnar Electric \$191,683
 - Generation Cable \$413,311 (\$247,986: 60% Material Only)
 - DBE change order participation 60%
 - DBE job to date participation: 15.6%

LS Black Constructors: Franklin O&M DBE Activities Update

LS Black Update on Change Orders

- Current contract amount thru 3/1: \$39,084,535.67
 - Committed DBE contracts: \$7,283,229.50
 - Anticipated DBE participation: 19%
- Overall billed to date thru 3/1: \$19,780,038.66
 - DBE billed to date thru 3/1: \$3,287,213.04
 - DBE achievement to date: 17%


LS Black Update on DBE Activity

- Continued participation from GoFetsch Mechanical
 - Installing ventilation
- Future work for Nakasone Painting
 - Painting
- Bald Eagle Erectors
 - Installing misc. metal work
- Camacho
 - Roofing

Workforce Participation Report

Civil Workforce Participation Percentage*


- February 2021: 21,690 hrs
- Civil Construction Total: 1,025,044 hrs

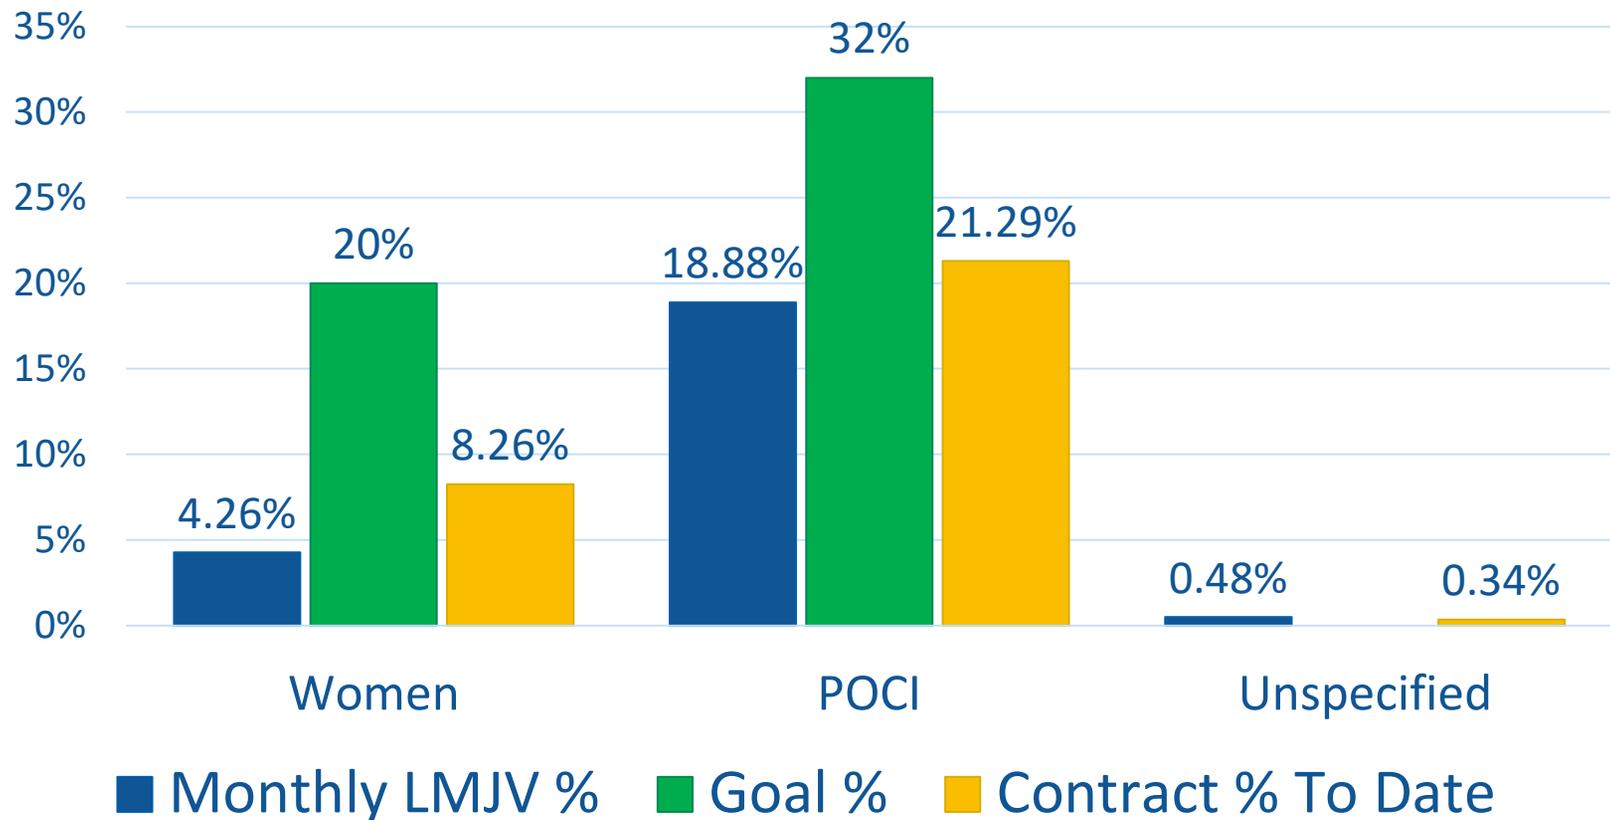

*Based on MDHR Workforce Report for February 2021
People of Color/Indigenous (POCI)

Civil Workforce Participation*

- February: 21,690 hrs
- Hours worked by category:

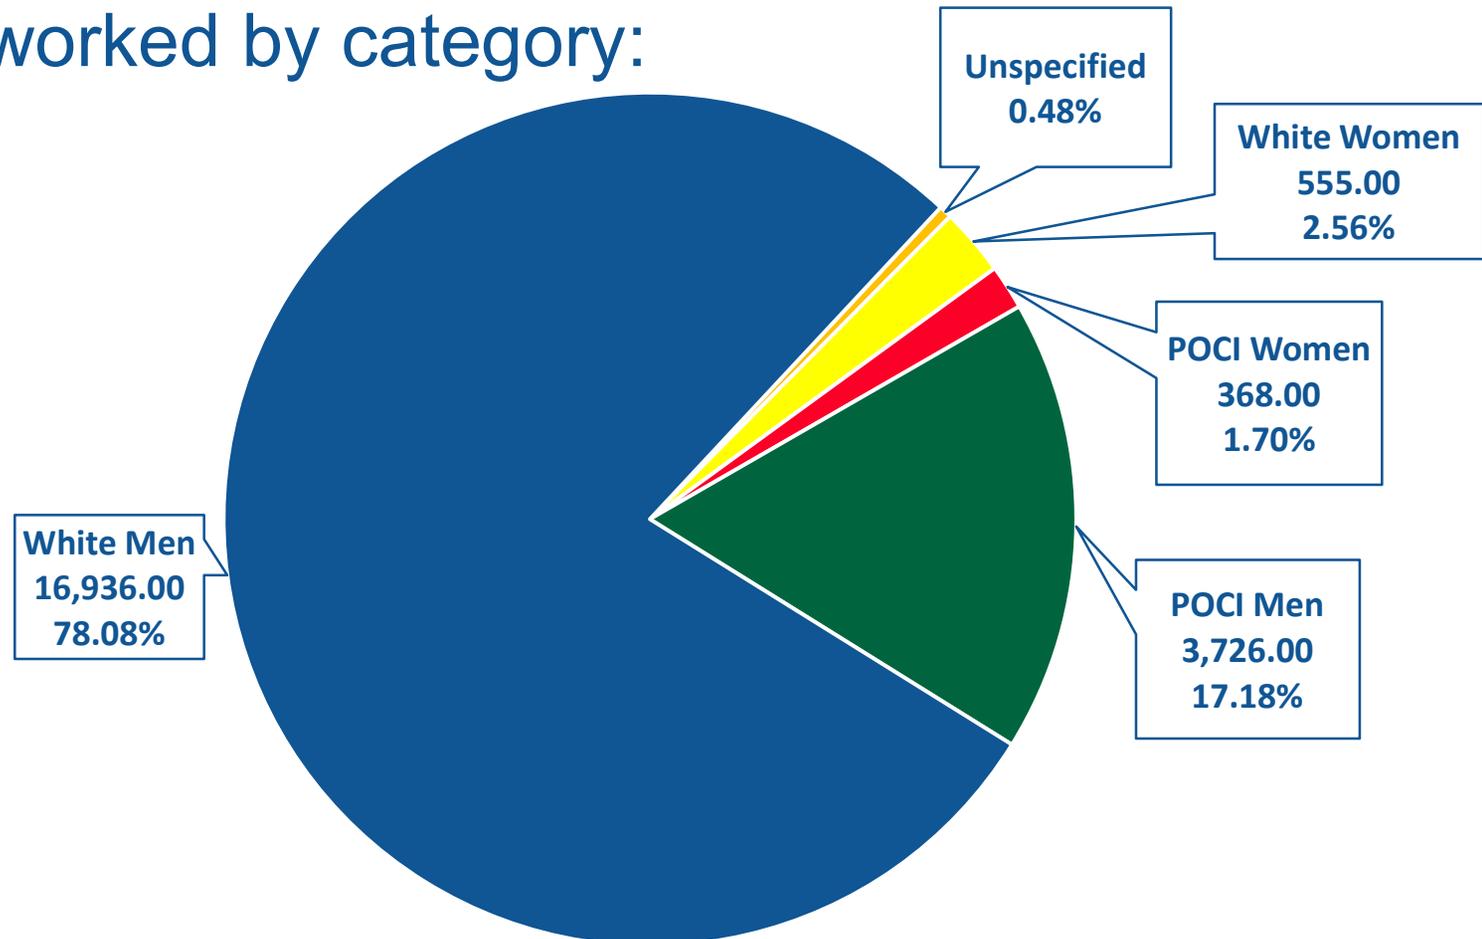

*Based on MDHR Workforce Report for February 2021


Civil Workforce Participation: Trucking

- Trucking participation on Project* being counted:
 - MBE: 18,850 hours
 - ZTS: 3,532 hours
 - Rock-On Trucks, Inc: 683 hours

* Based On Project To Date Hours:
(12/2018 – 2/2021)

Systems Workforce Participation Percentage*


- February 2021: 0 hrs
- Systems Construction Total: 261 hrs

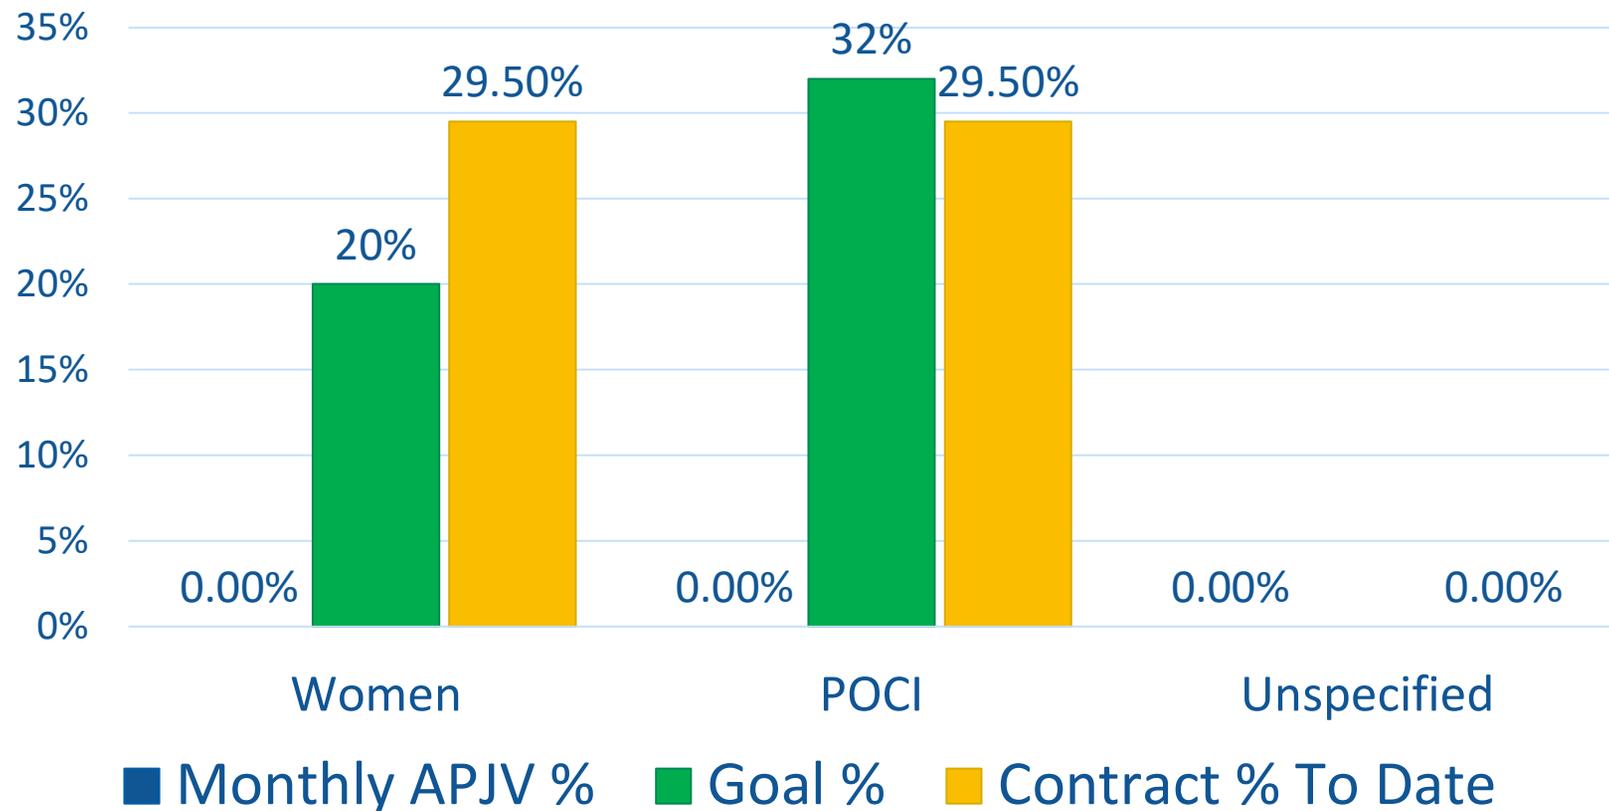

*Based on MDHR Workforce Report for February 2021
People of Color/Indigenous People (POCI)

Franklin O&M Workforce Participation Percentage*


- February 2021: 6,061 hrs
- Franklin O&M Construction Total: 31,921 hrs

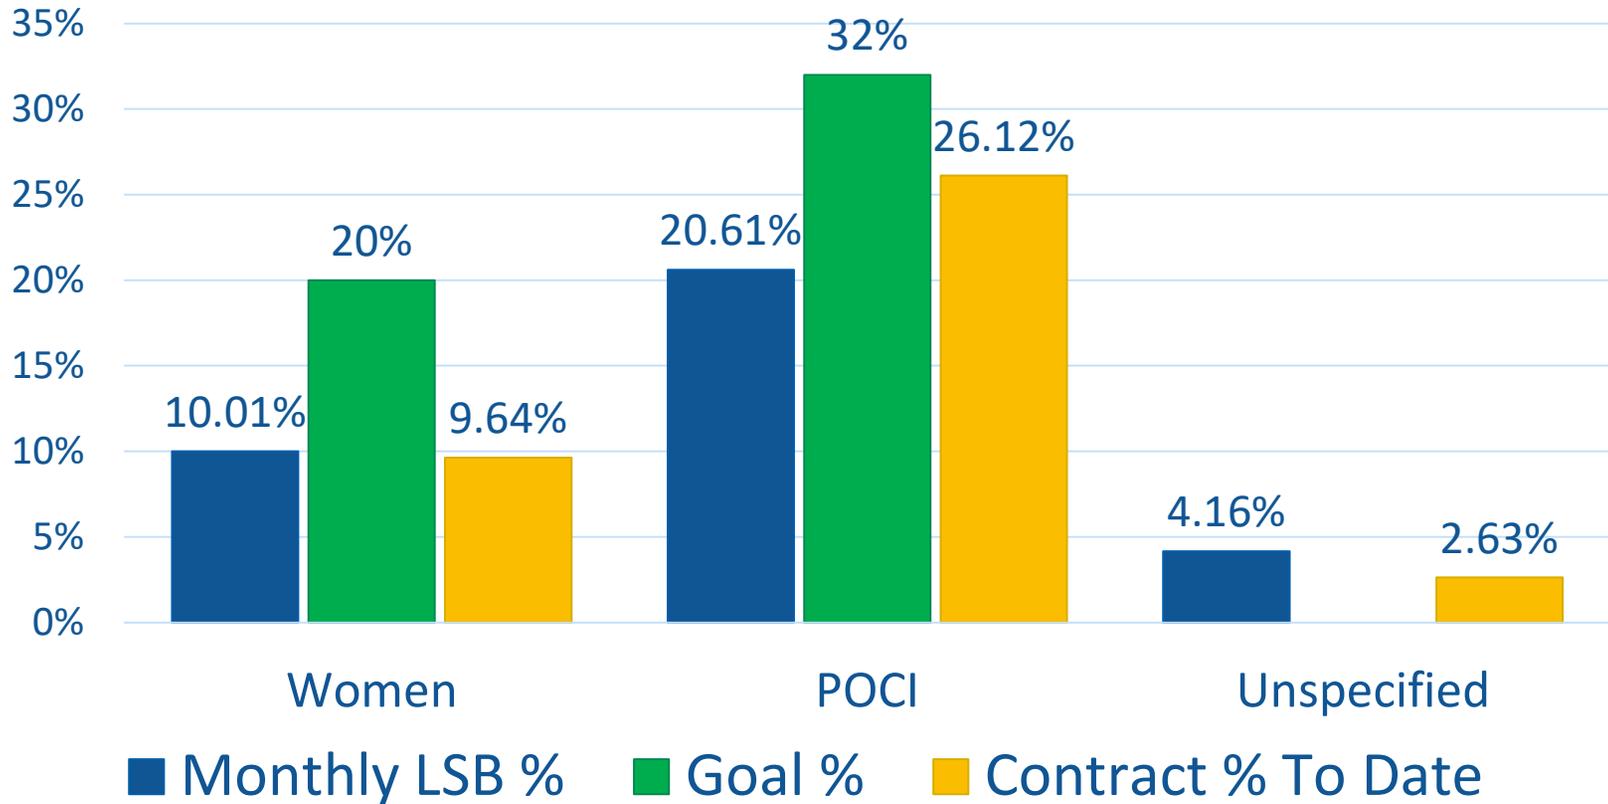

*Based on MDHR Workforce Report for February 2021
People of Color/Indigenous (POCI)

Franklin O&M Workforce Participation*

- February: 6,061 hrs
- Hours worked by category:

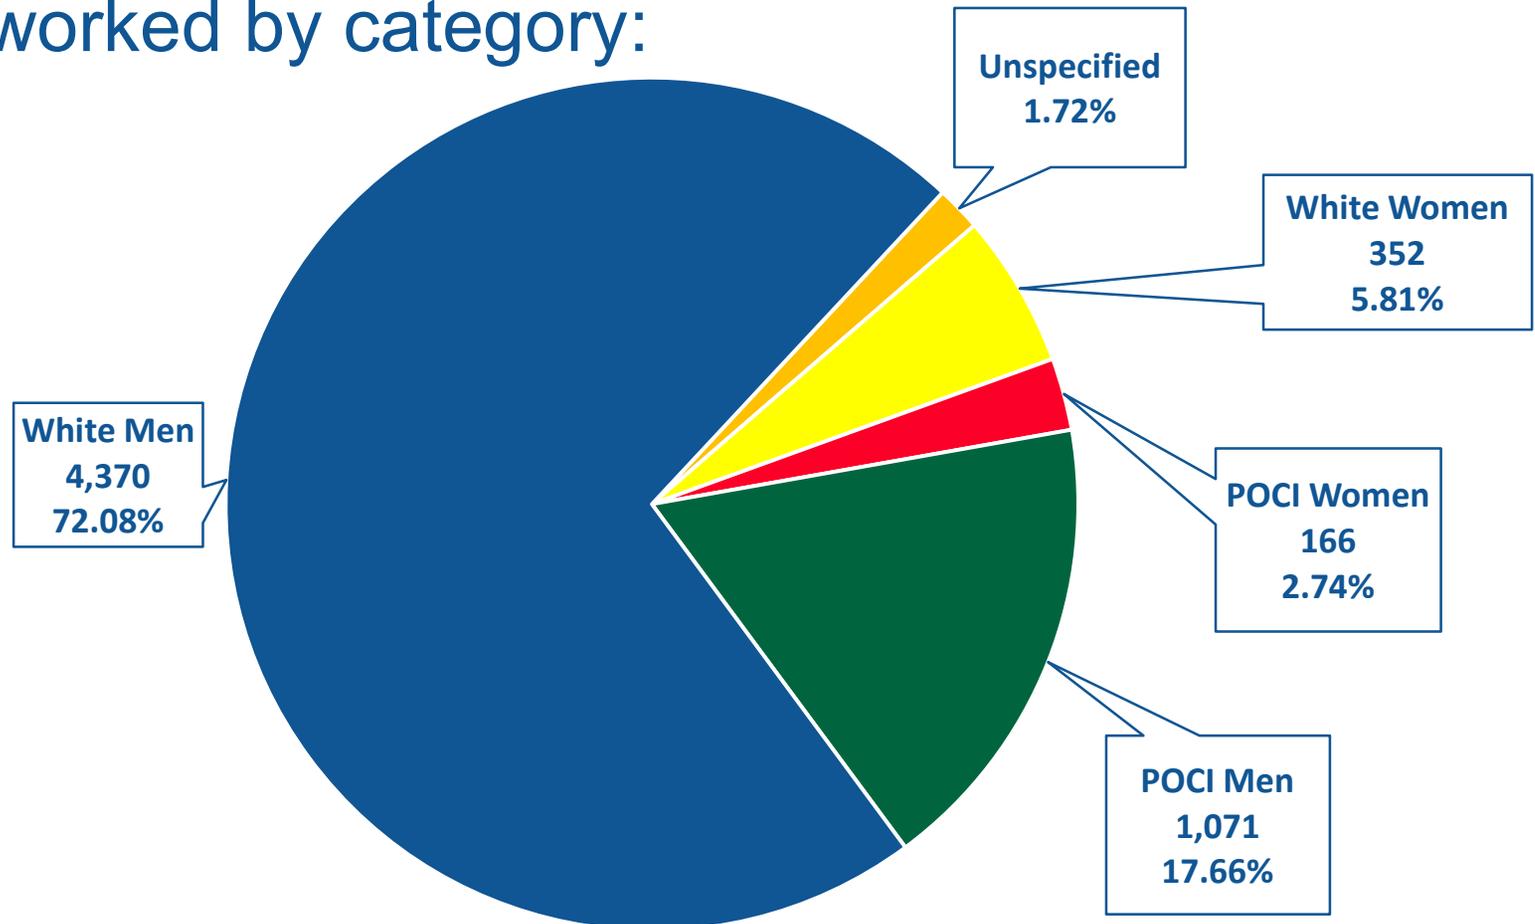

*Based on MDHR Workforce Report for February 2021

Lunda/CS McCrossan Joint Venture: Civil Workforce Activities Update

LMJV Workforce Activities – March 2021

- Monthly GFE meeting with MDHR & Met Council
- Monthly Subcontractor Workforce Participation Meeting
- Meeting with Building Strong Communities – How can Lunda AND the SWLRT project contribute to BSC?
- Continual update meetings with LMJV representatives & Lunda Field Operations on upcoming hiring needs
- SWLRT DBE Update Meeting
- Work on LMJVs Enter/Grow/Exit process
- Construction Trades Outreach planning – CBO Intro Meetings & BSC presentation to Subcontractors

Total New Hires/Transfers for LMJV: March 2021

- White Male: 2
- White Female: 0
- POCI Male: 1
- POCI Female: 0

* The 3 listed above are Rehires for Lunda at the stations.

No new hires for LMJV & CS McCrossan for the month of March.

Looking forward to report numbers at the next DWAC Meeting.

Aldridge Parsons Joint Venture: Systems Workforce Activities Update

Systems Contract Workforce

- Plan to meet the workforce goal
 - APJV Craft Labor will not begin until May 2021
 - Had meetings with Local 292, Local 160 & Local 49
 - Participated in Mock Interviews at Summit Academy, Nov 12, 2020, January 8, 2021 & March 19, 2021
 - Participated in Virtual Job Fair with Twin Cities Urban League March 9, 2021
 - ACE Mentoring Program – interviewing candidates for HS Summer Internship
 - March 25, 2021 held kickoff meeting with lower tier subcontractors including MDHR emphasized workforce inclusion.
 - Participated in Women in Construction Week meetings.

LS Black Constructors: Franklin O&M Workforce Activities Update

Franklin O&M Contract Workforce Activities

- Scheduled monthly GFE meetings with MDHR
- Met with Christa S. about outreach opportunities as well as scheduled some presentations with CBO's and will invite subs
- Reminder emails to trade partner teams about participation and plans to increase workforce as necessary

Closing

- Next Meeting Date: May 20th 2021
 - Agenda topics
 - Actions items for the next meeting
 - Adjourn

Stay Updated!

Online: SWLRT.ORG

Twitter: [@SouthwestLRT](https://twitter.com/SouthwestLRT)

Facebook: [@MetropolitanCouncil](https://www.facebook.com/MetropolitanCouncil)

Instagram: [@southwest_lrt](https://www.instagram.com/southwest_lrt)

