

Debris removal continues

Crews continue to make progress on the new tunnel access shaft on 4th Street at Hennepin Avenue.

As crews remove the sand from the tunnel, they will check the pipe under 4th Street and make repairs as needed.

In late August, the contractor will be adding a second crew to begin work on the new tunnel access shaft on 4th Street at Marquette Avenue.

Once sand removal and pipe repairs are complete, crews will begin grout work.


How much sand has been removed?

945 Cubic yards
(1 yd³ sand = 190 lbs)



That's equal to the weight of 15 elephants

5.5 from July alone

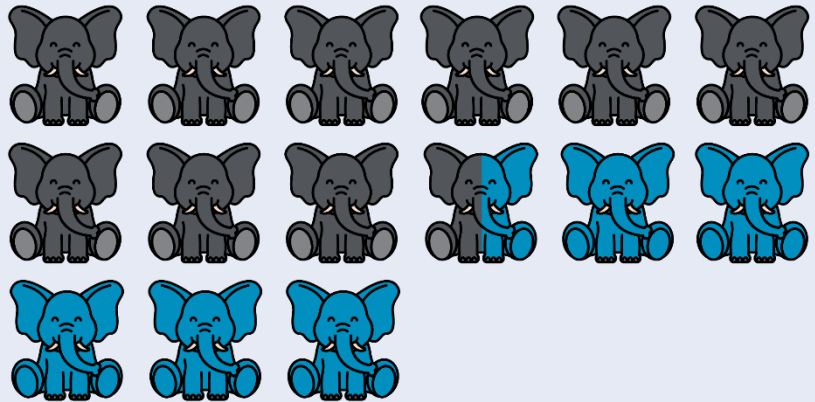

What's the status of sand removal?

50%

Complete



Information as of July 31, 2019

Contact us

Contact us with questions or concerns at any time during the project.

Email: info@4thStreetTunnelRepair.com

Hotline: 612-352-9774

Web:

metro council.org/sewerconstruction/4thStreetTunnel



SIGN UP FOR PROJECT UPDATES

Have updates delivered directly to your email or phone! Visit us online and enter your information:

metro council.org/sewerconstruction/4thStreetTunnel

When we update the website, you'll be the first to know.

ENEWSLETTER / TEXT

Subscribe to our newsletters, or text & email alerts.

Email

Enter Email or Phone #

SIGN UP
