


Green Line (Central Corridor) Update to the Transportation Committee

October 28, 2013



- Project- Construction Status
- Operational Readiness
- Green Line Launch Planning


General Central Corridor Project Schedule

	2010	2011	2012	2013	2014
Civil Construction Removal of existing infrastructure and build out of new roads, sidewalks, utilities, station, and tracks	█				
Systems Work Construct power substations, overhead power system, communications systems, and train control system			█		
Testing Trains will run along the alignment to test the line prior to opening to the public					█
Open to the Public Opening date in 2014 to be determined as testing nears completion					

Construction Complete Thru Aug. 2013



■ Total Construction
■ Systems Contract

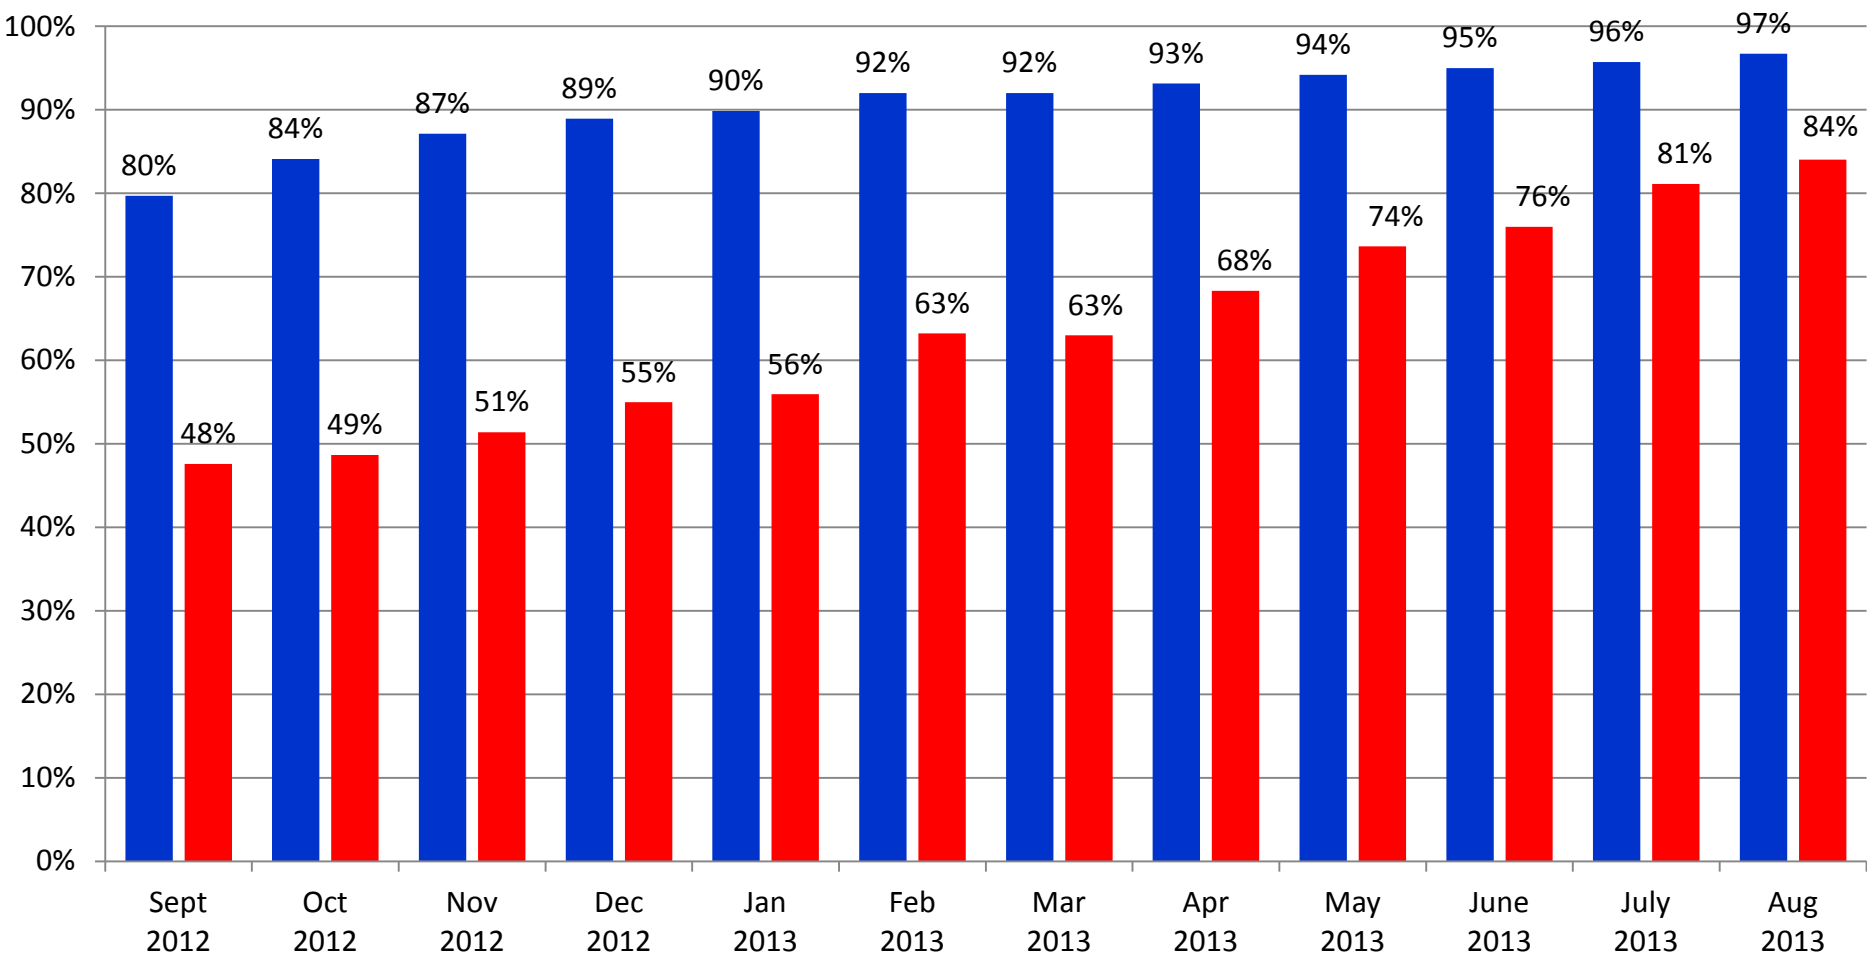


Cedar Street – St. Paul



March 2012



April 2013

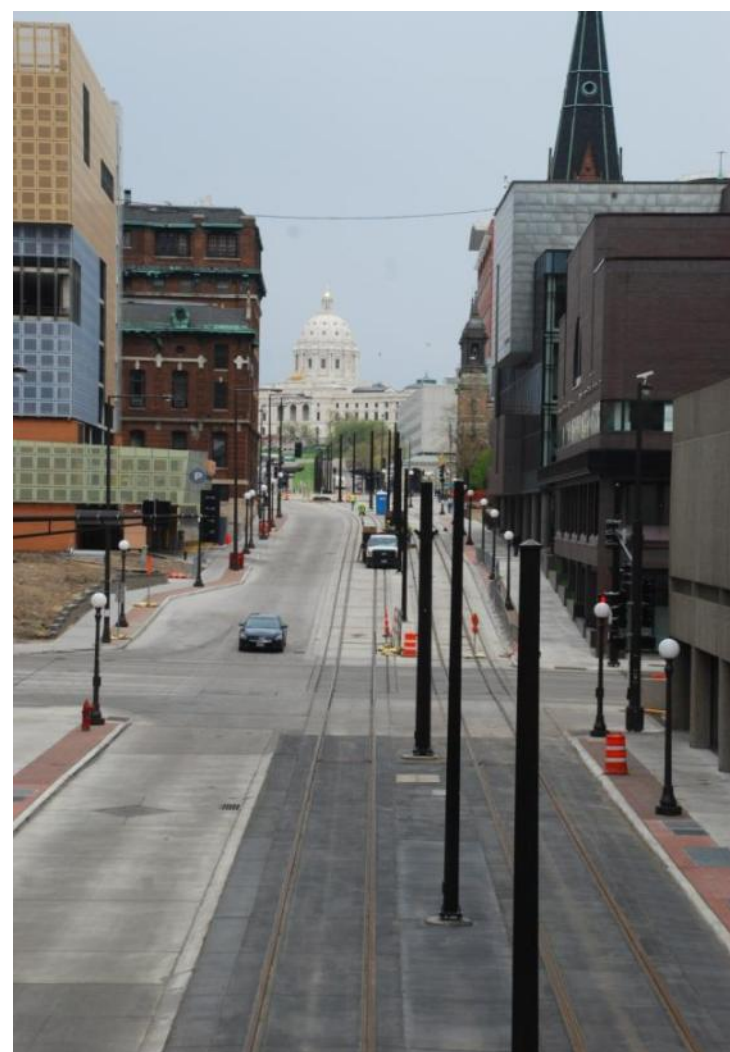

Washington Avenue – U of M



March 2012



May 2013



Clearance Testing



Integrated Testing



(Click Image to Play
Short Video Clip)



Operations and Maintenance Facility



New Train Inside OMF



- Being used to support project activities
- Operations staff move-in planned Dec 2013 pending OMF Yard Systems programming and Certificate of Occupancy.

Operational Readiness


- 18 Working Groups focused on various readiness activities such as:
 - Hiring
 - Opening Day Event Operations
 - Bus Service Changes
 - Safety, Security, Emergency Preparedness
 - Marketing/Communication
 - Target Field Station Project Coordination

Operations Staff Hiring Progress




(As of Oct. 18)

Oct. 2013 Hiring Goal

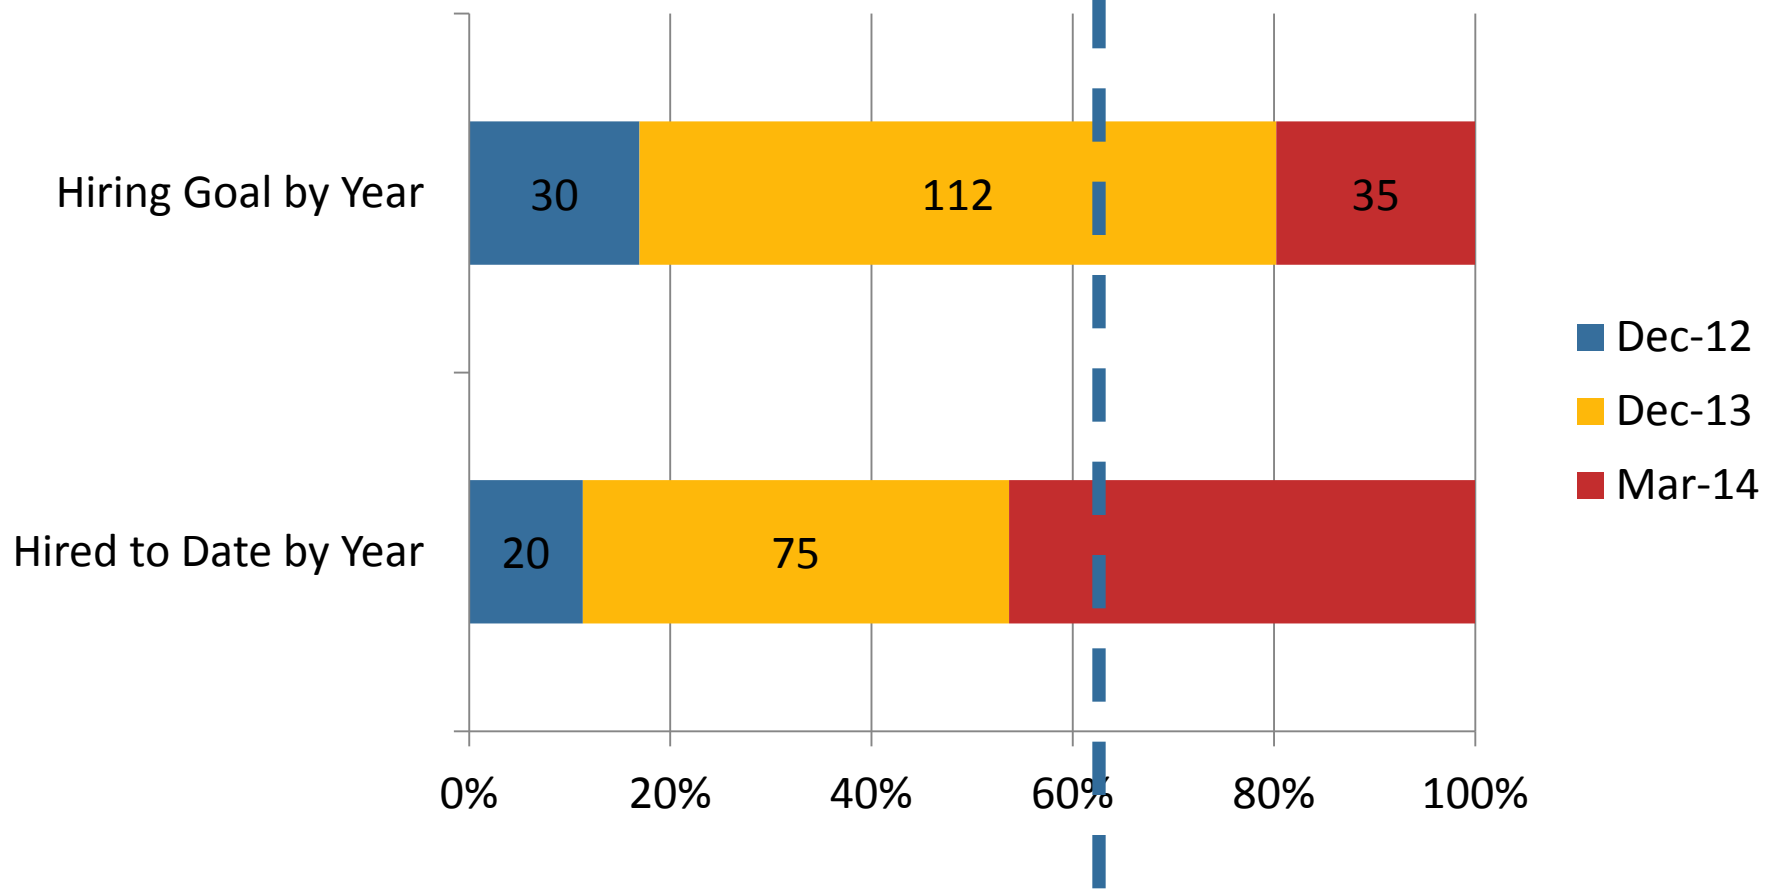

Light Rail Vehicle Status

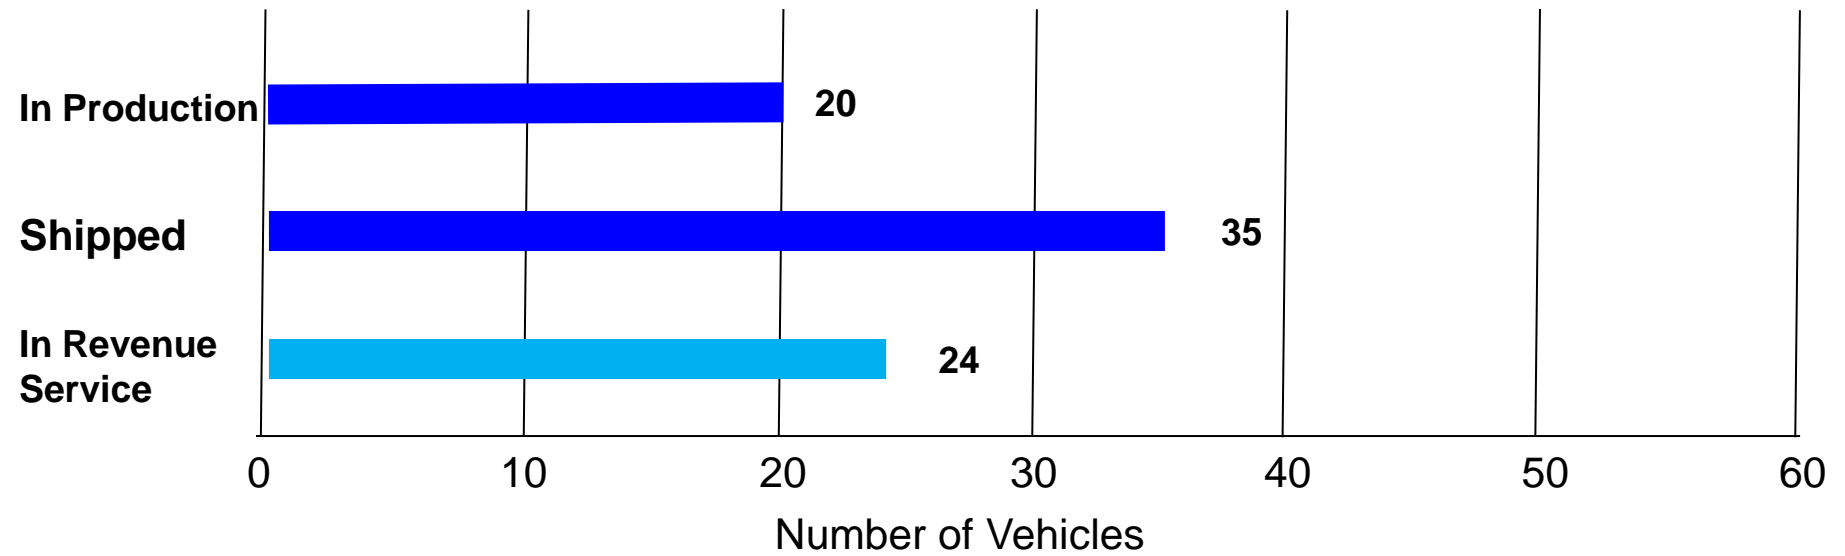

- Training

- Professional Operator Development (POD) Training at U of M-Washington Ave. Mall



- Familiarization Training for First Responders

- 120 St. Paul fire fighters have completed onsite/hands on Equipment Training (all in immediate response area)
- LRT Familiarization training sent out to 17 public safety agencies

- On-Track Safety Certification program launched on Line

- Public Safety Coordination
 - Fire Life Safety Committee
 - Special Event Planning (TCF Stadium)
 - Emergency Preparedness planning
- Public Safety Communication and Outreach



Safety Outreach and Communication



- Website
- Brochures
- Training
- Videos
- Posters
- Public Service Announcement
- State Fair Fans

LIGHT RAIL SAFETY STARTS WITH YOU!

The METRO Green Line is coming soon to your neighborhood.

Now is the time to learn about light rail safety.

T METRO
Green Line

- Stations
- Schools/Libraries
 - Gordon Parks
 - Rondo Library
- Businesses
 - McDonald's
 - Twin Cities Public Television



PSAs and Safety Quiz Show



- Pedestrians crossing the track
- Pedestrians in crosswalks
- Stations




Green Line Launch Opening Day Celebration Planning

- Coordinate events in each Green Line community/ business district
- Achieve mutual goals
 - Market the Green Line
 - Educate new riders
 - Promote businesses
 - Showcase the work of Central Corridor Funders Collaborative
 - Provide fun, safe community celebration

Coordinate Events By Business Districts



Implement and Communicate Bus Changes

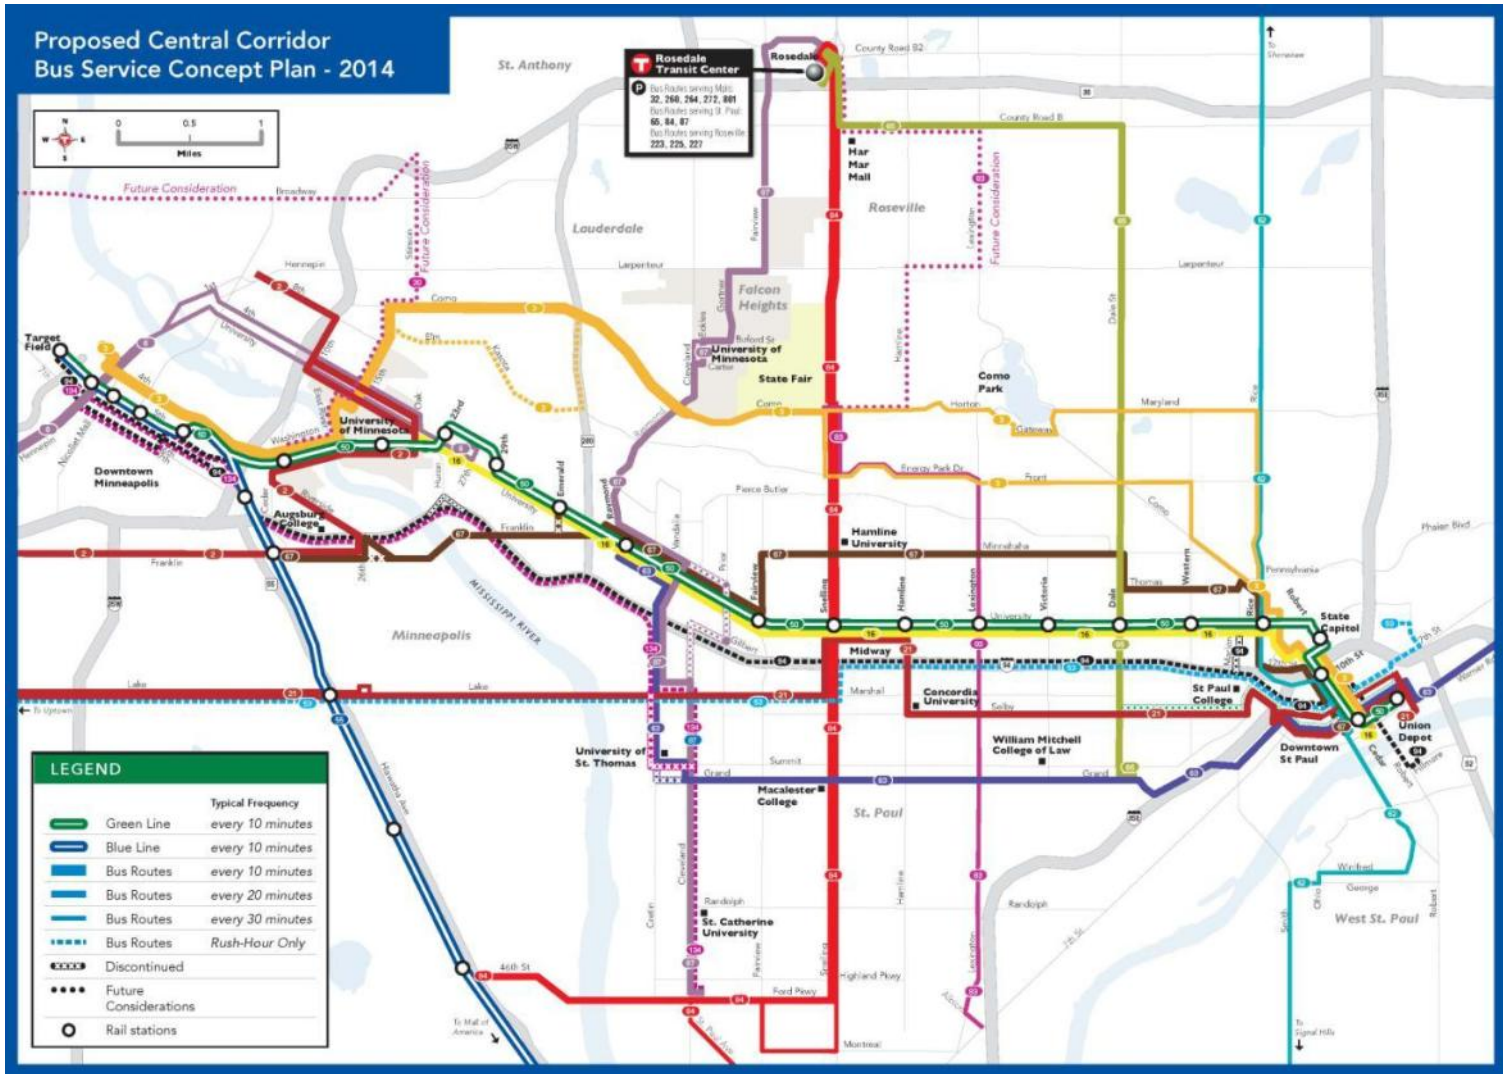

Check out our website:

- www.centralcorridor.org

Contact Central Corridor Project Office:

- 540 Fairview Avenue North
St. Paul, MN 55104
- Construction Hotline: 651-602-1404
- Comment Line: 651-602-1645
- Email: centralcorridor@metc.state.mn.us
