

# Vadnais Heights Area Regional Sewer Improvements Project

## APRIL 27, 2018 CONSTRUCTION UPDATE

(dates are approximate and dependent on weather/construction conditions)



### Ongoing Construction

#### Work Near Highway 36 & Highway 61


- Crews continue working on manhole repairs along Cope Ave. (frontage road near Menards). Lining work is anticipated to wrap up by early May.
- Sewer rehabilitation work on the west side of Hwy 61 and on the north side of Hwy 36 near Keller Regional Park is complete. Crews will continue to be on-site and equipment will remain in place to finish other construction activities and park restoration. **The park remains open during construction.**

### Upcoming Construction

#### Work Near Highway 61 & I-694

Early next week, crews will return to the site to start installing the temporary conveyance pipe east of Hwy 61 and both north and south of I-694. Please refer to the map below.

- **Expect temporary lane closures on Buerkle Rd. on Tuesday, May 1 through Wednesday, May 2** while crews bury the conveyance pipe underground. Flaggers will be on-site to direct traffic during this time. The conveyance pipes will temporarily convey wastewater during the sewer rehabilitation work.

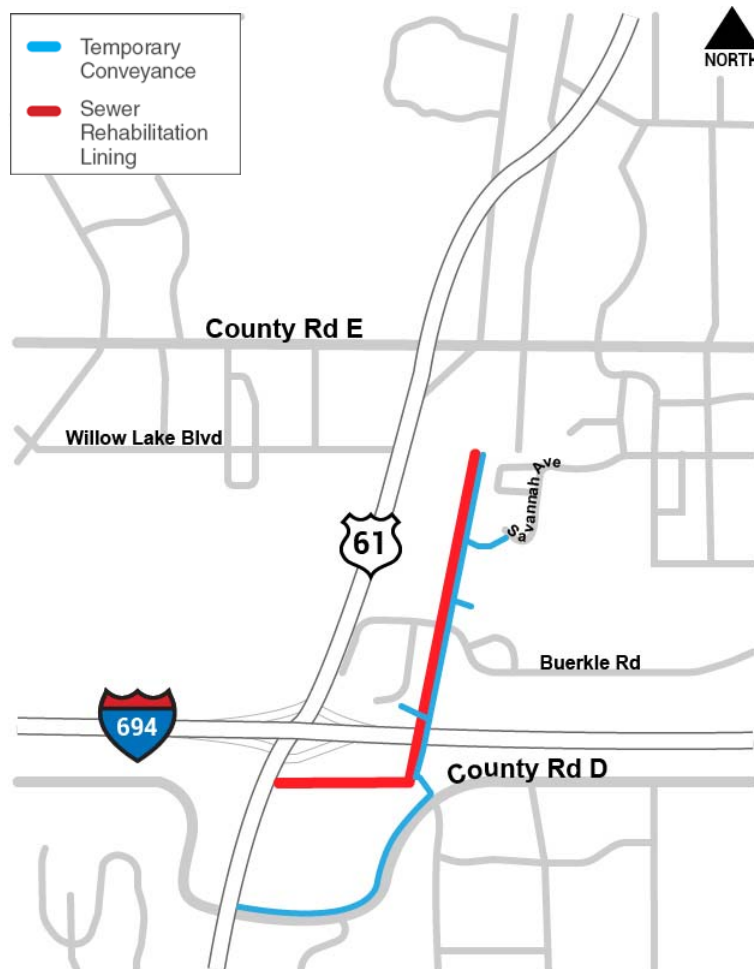

While we do our best to minimize impacts during construction, some temporary inconveniences such as odors, noise, and vibrations may occur as this work takes place.

# Vadnais Heights Area Regional Sewer Improvements Project

## Safety

Please also keep your distance from any materials and equipment – only authorized personnel are permitted in our work areas. We want you and our crews to stay safe during construction.

## About the Project

Metropolitan Council Environmental Services (MCES), operator of the metro-area wastewater collection and treatment system, is continuing construction on its Vadnais Heights Area Regional Sewer Improvements Project. This project will include making improvements to aging and deteriorating regional sanitary sewer facilities that serve the cities of Vadnais Heights, Maplewood, and White Bear Lake. The project is anticipated to be completed by fall 2019.

## Who Should You Contact?

For questions or concerns about this work, contact our project team:

- [info@VH-Maplewood-Sewer.com](mailto:info@VH-Maplewood-Sewer.com)
- 651.236.9221

## **STAY INFORMED:**

For project information, to sign up for project e-mail or text updates, or to view past updates, visit the project website at [metro council.org/sewerconstruction/VadnaisHeightsMaplewood](http://metro council.org/sewerconstruction/VadnaisHeightsMaplewood).
