



Business Item 2024-171:


Project 819025 – Trunk Highway 13
Change Order Authority Increase



Environment Committee: July 23, 2024

Tim Wedin

Location Map

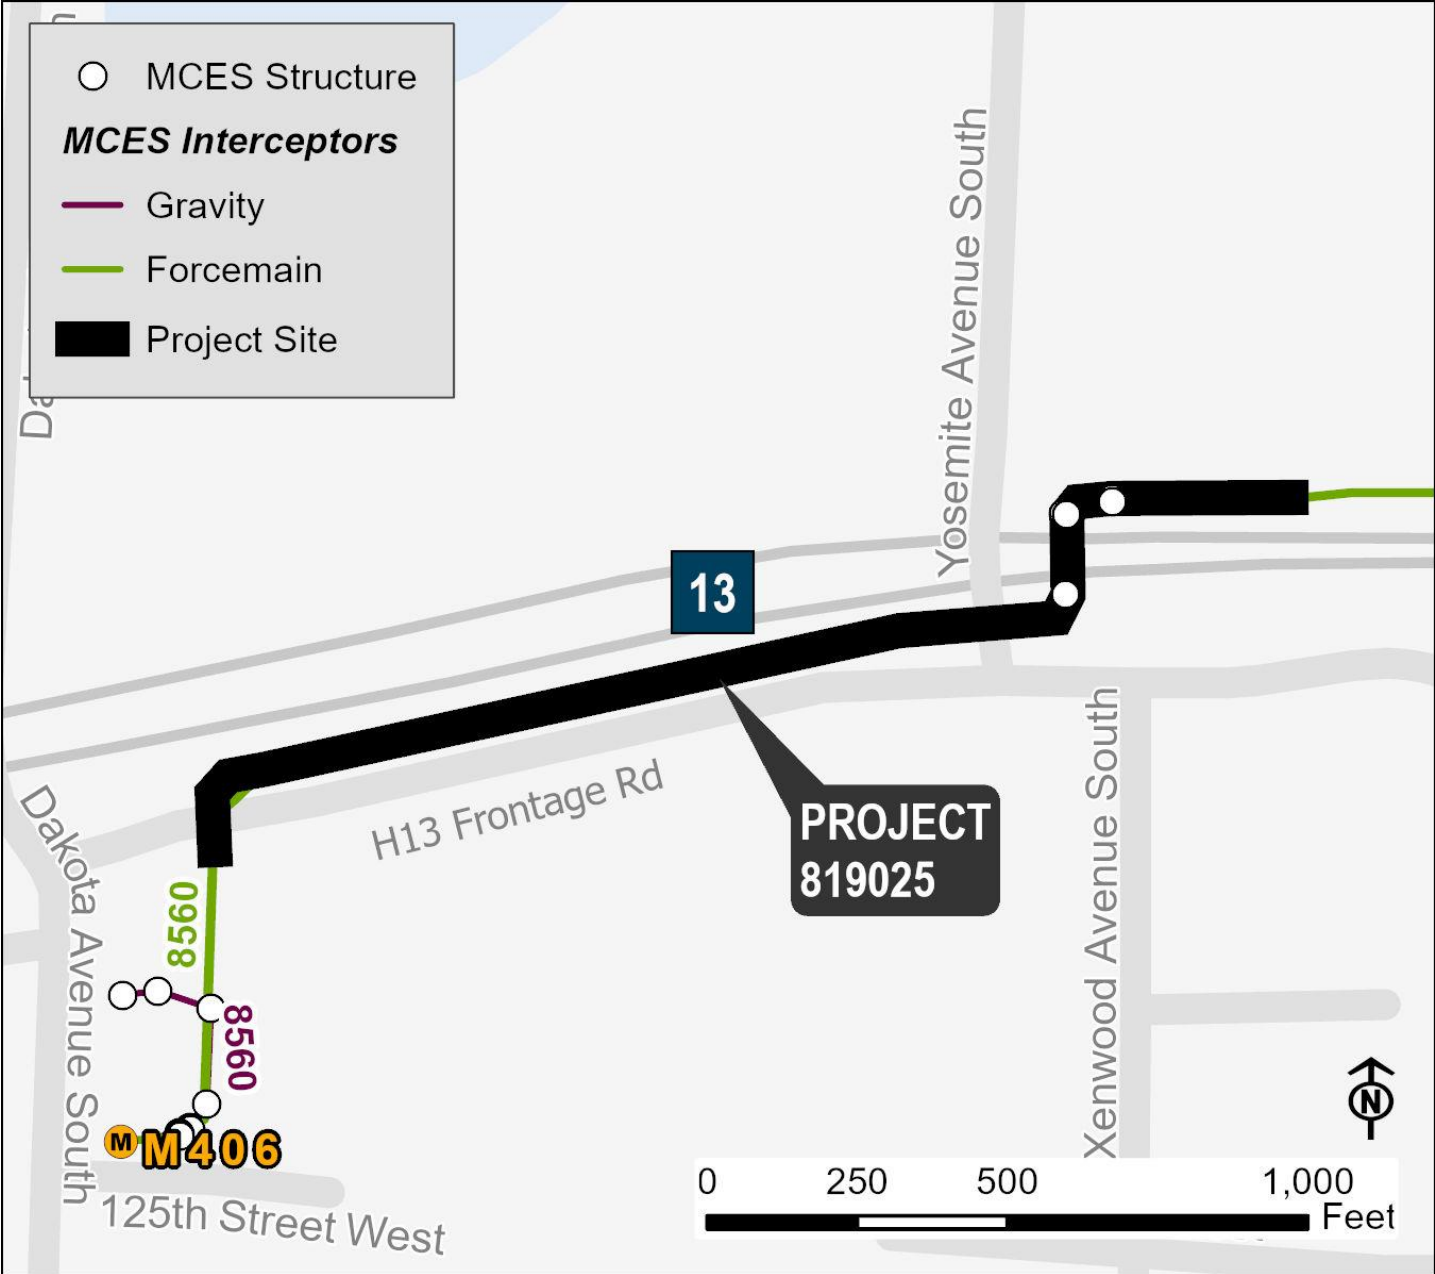

Project Background

Interceptor 8560

1. Project includes realignment of the forcemains to avoid conflicts with the new entrance ramp.
2. Supply chain challenges impacted the delivery of pipe to the project site extending the overall project completion time beyond what was included in the contract documents.
3. Construction schedule required the pipe to be installed during winter conditions, requiring more effort by the Contractor to complete the work that was not planned in the contracted work.
4. The weather conditions of the 2022-2023 season created a situation which resulted in increased quantities over what were in the original contract documents.
5. MCES worked with MnDOT to come to a mutual agreement on the final costs increase for these additional efforts.



Proposed Action

That the Metropolitan Council authorize an increase in the construction contract change order amount for the Master Utility Agreement 211069 with the Minnesota Department of Transportation (MnDOT) for Interceptor 8560, MCES Project No. 819025, by \$450,000 for a total amount not to exceed \$4,103,870.95.



Thank you

Tim Wedin

Assistant Manager
Interceptor Engineering
651-602-4571
timothy.wedin@metc.state.mn.us

