



Cedar Grove Transit Station Improvements

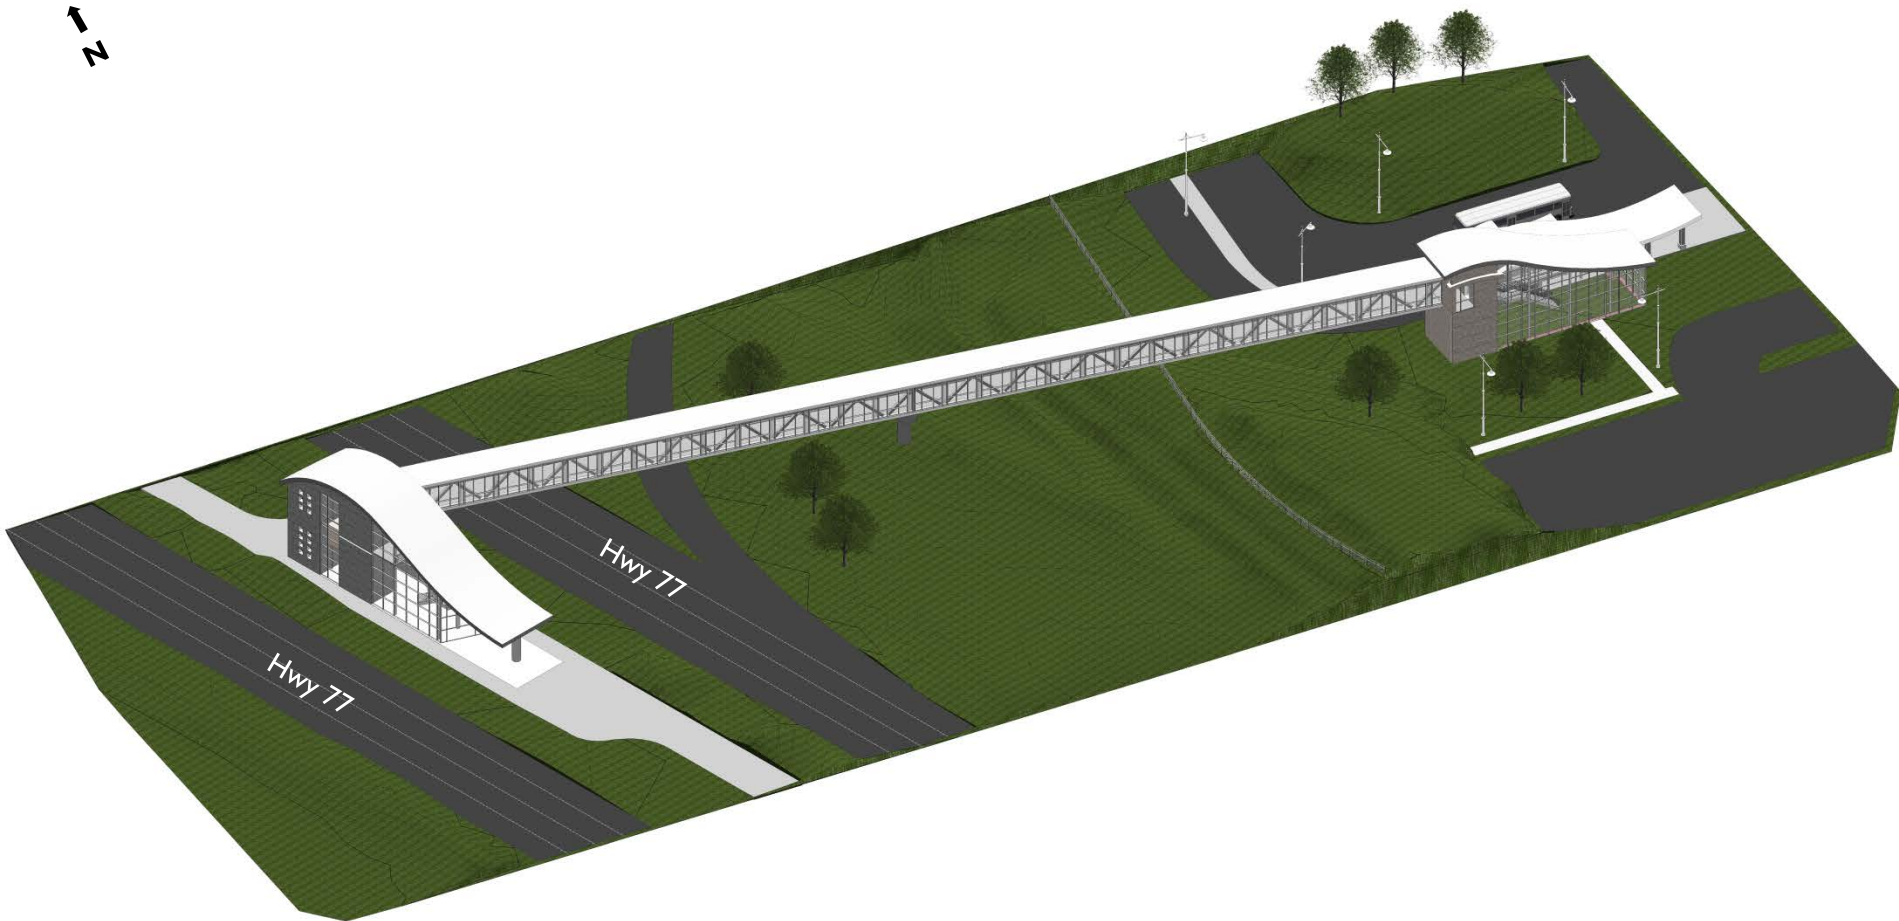

Cedar Grove Transit Station Improvements

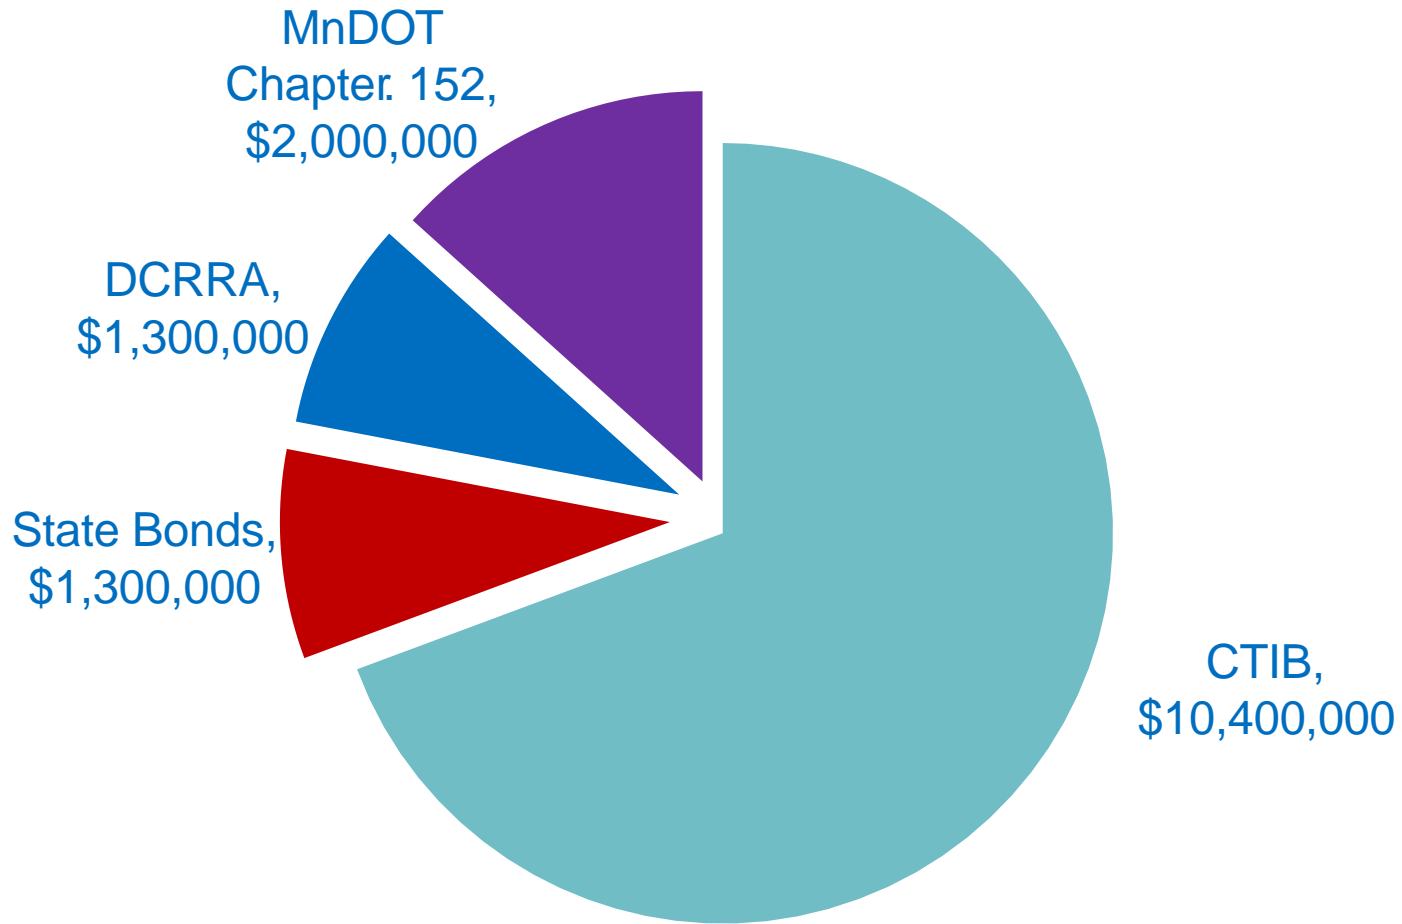

Total Project Budget: \$15,000,000

Cedar Grove Transit Station Improvements

Major Construction Elements

<input type="checkbox"/> TH 77 Road Construction	100%
<input type="checkbox"/> Busway Construction	100%
<input type="checkbox"/> Stations	40%
<input type="checkbox"/> Skyway	40%

Cedar Grove Transit Station Improvements

Overview Looking North



Overview Looking South



Midspan Pier Connection Cedar Grove Transit Station Improvements

Moment & Barrier Walls

East Station Skyway Connection



West Station Skyway Connection



Cedar Grove Transit Station Improvements



Cedar Grove Transit Station Improvements



Project Challenges



Cedar Grove Transit Station Improvements

Project Schedule

- Roadway Construction Completion **November, 2016**
- Station Construction Substantial Completion **April, 2017**
- Driver Training Starts **April, 2017**
- Station Construction Completion **May, 2017**
- Stations Opening **May, 2017**
