

Project Decision Board

August 21, 2024



BROOKLYN PARK | CRYSTAL | ROBBINSDALE | MINNEAPOLIS



Today's Topics

- Call to Order & Introduction
- Approval of July 17 Meeting Minutes
- SFEIS
- Municipal Consent
- Procurement Strategy



The public can submit written comments to Nkongo Cigolo (Nkongo.Cigolo@metrotransit.org)

Approval of July 17, 2024 Meeting Minutes



SFEIS Update



SFEIS Development – Mitigation Workplan

- Next steps to inform mitigation development
- Summary of next steps
- Outlines categories, expected timing, and steps to identify mitigation



Mitigation Workplan Next Steps

- Share with corridor Cities, Community Prosperity Program Board, and others
- Advance outreach
 - Geographically and topic area focused
 - Welcome input on outreach strategies



Municipal Consent




Municipal Consent Timeline


BLUE LINE LRT EXTENSION

Roadmap to Municipal Consent

R0-11

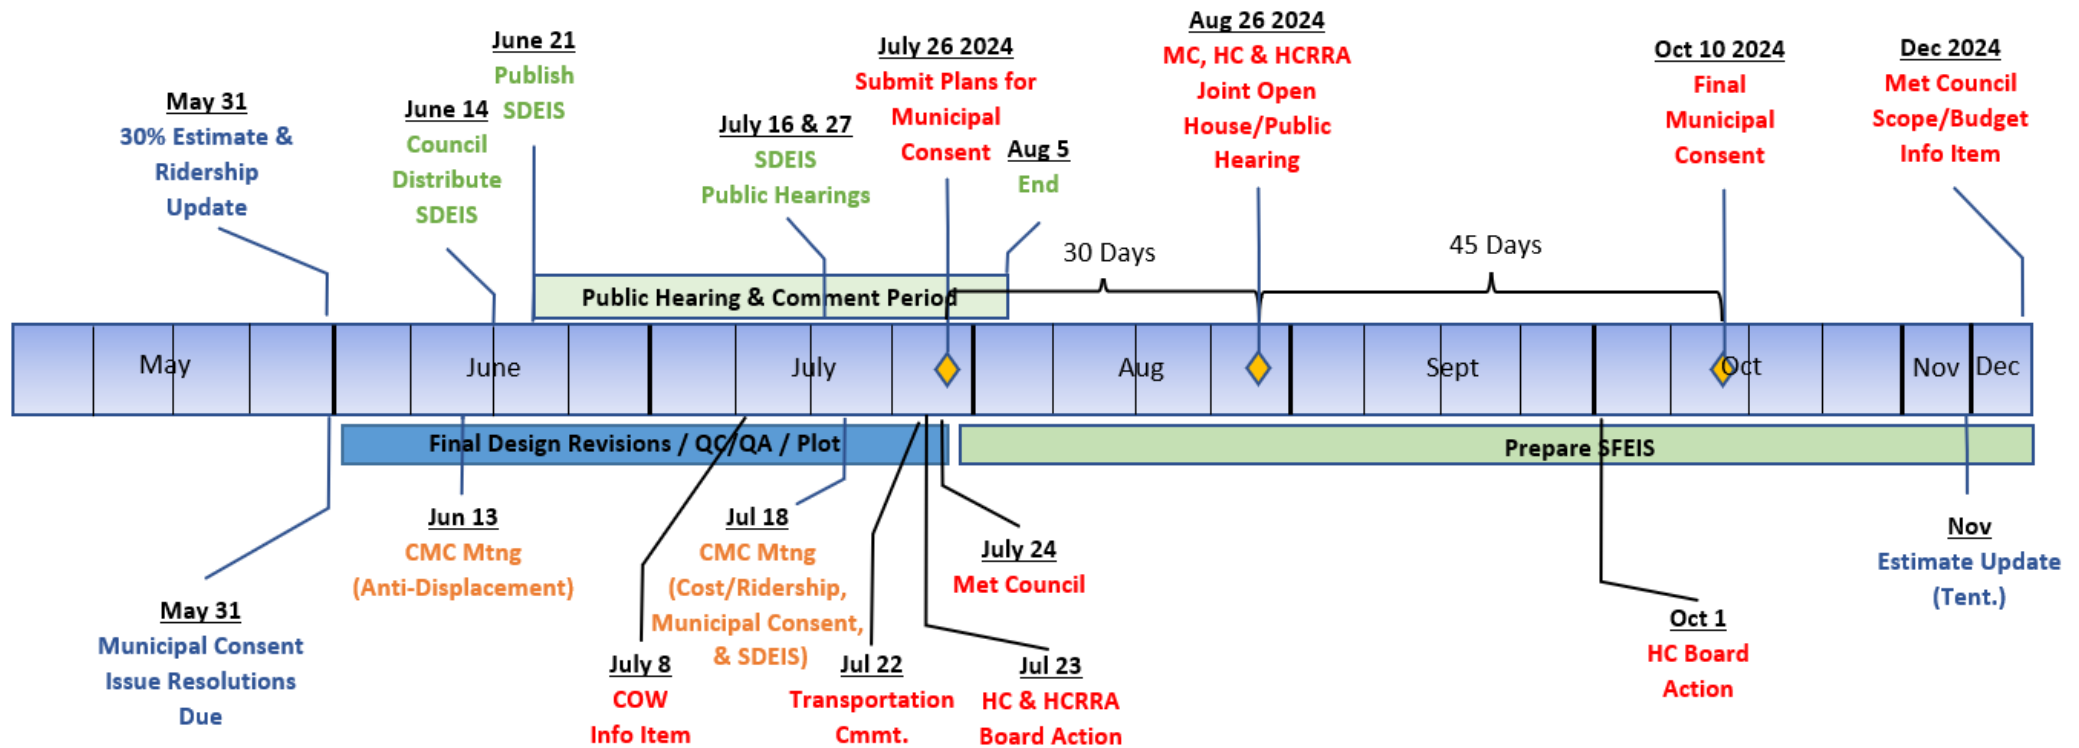

Municipal Consent Timeline Cont.

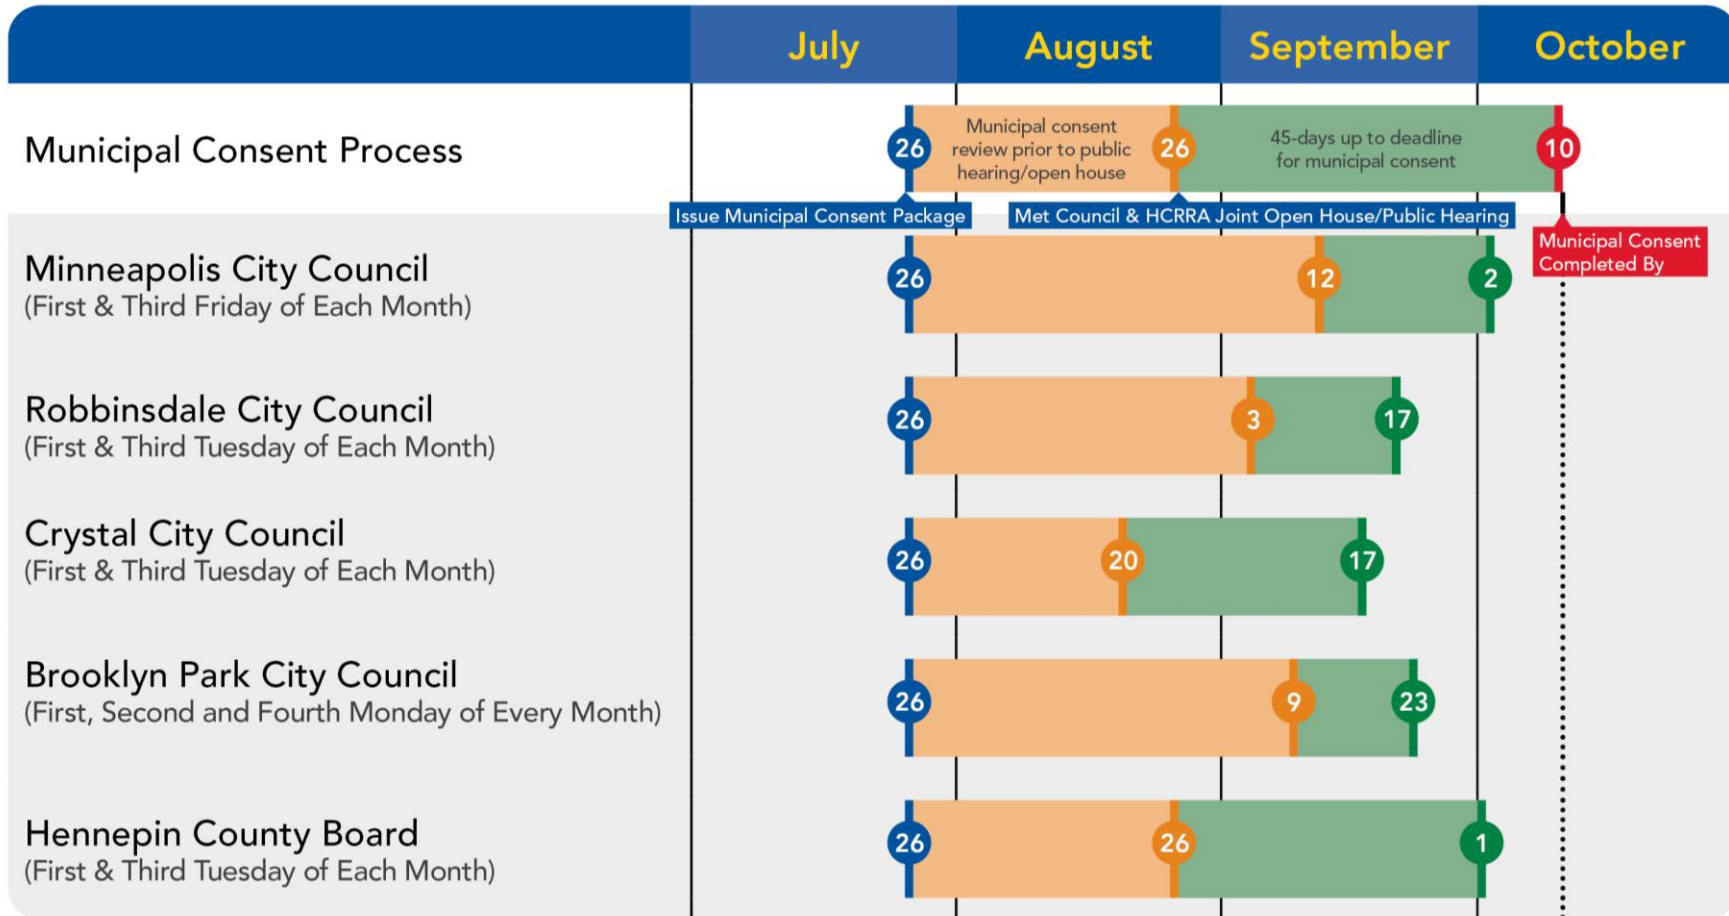

Begin Municipal Consent Review



Public Hearing




Council/Board Action

Procurement Strategy



Procurement Strategy Update

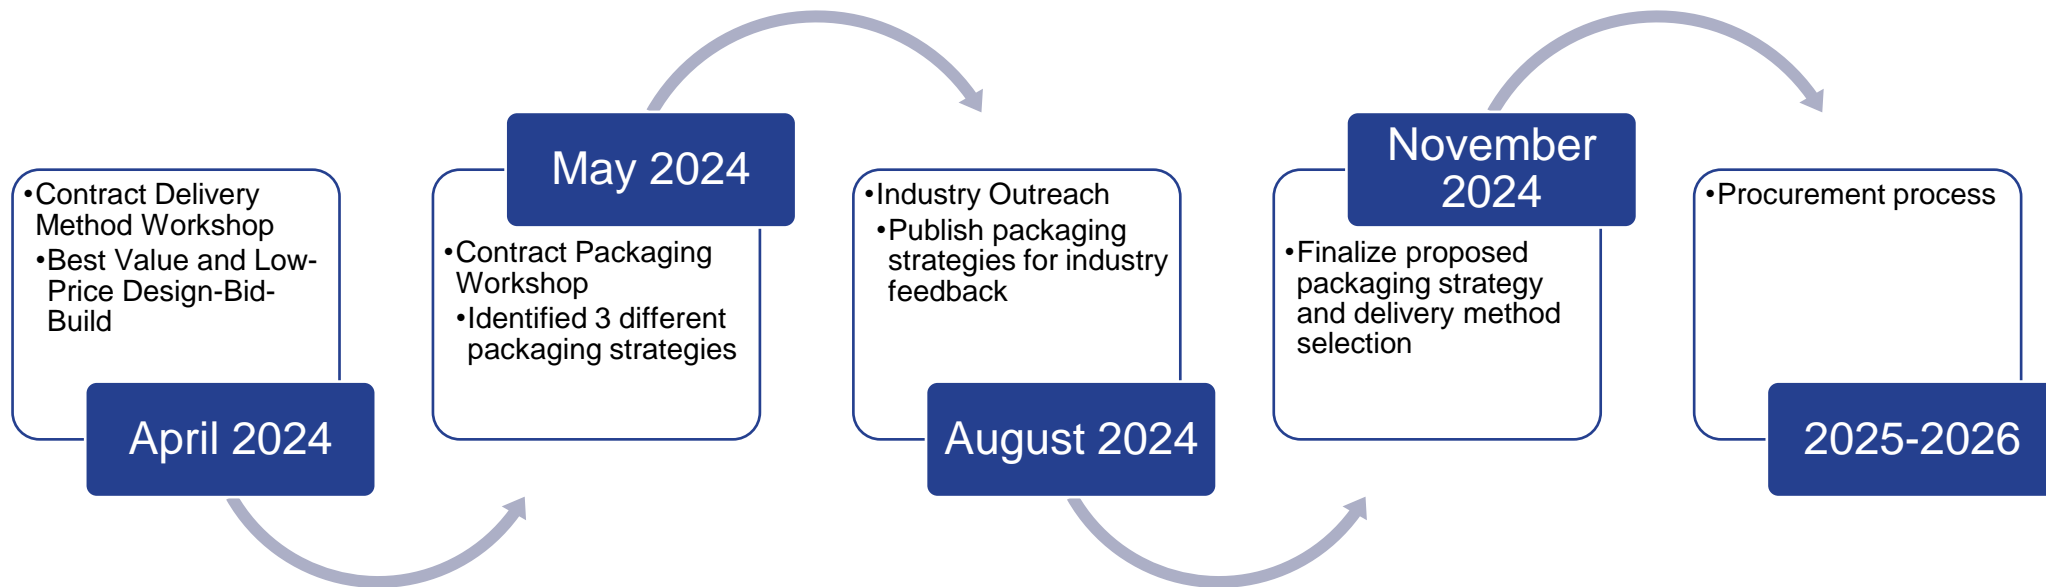

Packaging Strategies

- **Strategy A**

- 6 packages, divided by work activity
- Separate Civil & Track, Systems, Facilities, Park and Ride, and OMF packages

- **Strategy B**

- 7 packages, divided by geography
- Minneapolis Civil & Track package
- Systems included with Robbinsdale/Crystal/Brooklyn Park System & Track

- **Strategy C**

- 5 packages, combining Civil & Track, and Systems

	Component	Strategy A Package Number	Strategy B Package Number	Strategy C Package Number
1a	Civil - Minneapolis	1	1	1
1b	Civil - Robbinsdale	1	2	1
1c	Civil - Crystal	1	2	1
1d	Civil - Brooklyn Park	1	2	1
2a	Structures - Minneapolis	1	1	1
2b	Structures - Robbinsdale	1	2	1
2c	Structures - Crystal	1	2	1
2d	Structures - Brooklyn Park	1	2	1
3a	Track - Minneapolis	1	1	1
3b	Track - Robbinsdale	1	3	1
3c	Track - Crystal	1	3	1
3d	Track - Brooklyn Park	1	3	1
4	Systems	2	3	1
5a	Station Civil Work (Site Prep & Foundations) - Minneapolis	1	1	1
5b	Station Civil Work (Site Prep & Foundations) - Robbinsdale	1	2	1
5c	Station Civil Work (Site Prep & Foundations) - Crystal	1	2	1
5d	Station Civil Work (Site Prep & Foundations) - Brooklyn Park	1	2	1
5e	Station Facilities	3	4	2
6a	Park & Ride Facilities - Robbinsdale	4	5	3
6b	Park & Ride Facilities - Brooklyn Park	4	5	3
7	OMF	5	6	4
8	Vehicles	6	7	5



Next Meeting

- Next Meeting: September 18, 2024

